



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Mostly Sunny  High: 66°F Low: 44°F
 Winds: ESE 5-15 MPH Precipitation: 40%chance

Thursday, September 22th, 2005



101 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦Safety/Environmental:

- ♦ Next All Hands safety meeting Wednesday, September 28th, 2005 at 7:00 am.
- ♦ No injuries to date.
- ♦ Fire watch training today.

♦General:

- ♦ Electrical poles will be delivered Friday, September 23rd, 2005.
- ♦ Receiving substation and electrical materials.

♦Road Construction

- ♦ Gravel installation #18-#23 complete. Gravel installation at #7-#9 continues.
- ♦ Road construction to #3 started. 52nd St. gravel will start.
- ♦ Building access at highway 36 will complete today.

♦ Foundation Construction:

- ♦ Slurry #18 thru #22.(#20 complete)
- ♦ Excavating #18-#19, set CMP's today. Set CMP at #8.
- ♦ Building Template/Bolts #27-#28. Pour #29 today.

♦ Electrical Construction:

- ♦ Substation foundation installation continues, conduct installation
- ♦ Grounding turbine foundations.

♦Tower Erection: Erection Days Lost for High Winds: 0

- ♦ Not Started

♦Mechanical Completion:

- ♦ Not Started

♦Commissioning:


- ♦ Not Started

♦WAPA Interconnect:

- ♦ Not started

RECEIVING			
	Today	Total Received	Remaining
Bases	0	0	33
Mids	0	0	33
Tops	0	0	33
Nacelles	0	0	33
Controllers	0	0	33
Blades	0	0	33
Transformers	0	0	33
Hubs	0	0	33
4/0 Cable	0	150,148	0
1000 MCM	0	7,245	0

General Information & Announcements

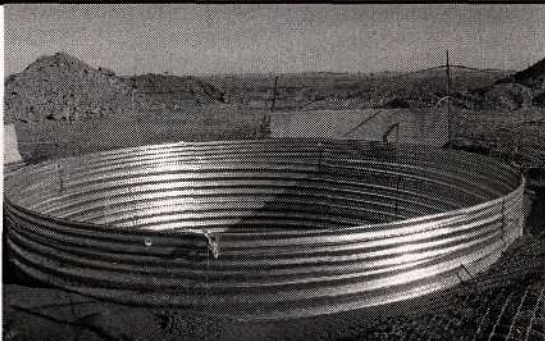

	Complete	Remaining	% complete
Roads Built	12,390	24,764	33.4%
Foundations completed & backfilled	0	33	0.0%
Tower Base sections installed	0	33	0.0%
Tower Mid sections installed	0	33	0.0%
Tower top sections installed	0	33	0.0%
Nacelles Installed	0	33	0.0%
Rotors installed	0	33	0.0%
Mechanically completed	0	33	0.0%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	0	49,291	0.0%
Trenching for 1000MCM cable (ft)	0	2,415	0.0%
Transformers Set/Terminated	0	33	0.0%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.
