



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Mostly Sunny



High: 71°F Low: 38°F

Winds: WNW 10-20 MPH

Precipitation: 20%chance

Tuesday, September 27th, 2005



96 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦Safety/Environmental:

- ♦ Next All Hands safety meeting tomorrow at 7:00 am.
- ♦ No injuries to date.

♦General:

- ♦ Management Meeting tomorrow at 9:00 am.
- ♦ Electrical poles were due 9/23/05, now scheduled for delivery 9/30/05.
- ♦ Receiving substation and electrical materials, 230KV breaker has arrived.

♦Road Construction

- ♦ 52nd St fabric and gravel continues.
- ♦ All road sub-base construction is complete with the exception of turbine #3.

♦ Foundation Construction:

- ♦ Setting inner can and backfill at #26.
- ♦ Set outer CMP at #5.
- ♦ Pre Dig #1 and #2.
- ♦ Excavating #3 and #4.
- ♦ Pour #27 today.
- ♦ Template setup #25.

♦ Electrical Construction:

- ♦ Grounding crews right behind foundation crews.
- ♦ Pier drilling starts tomorrow at the substation.
- ♦ Main XFMR containment wall forming today.

♦Tower Erection: Erection Days Lost for High Winds: 0

- ♦ Not Started

♦Mechanical Completion:

- ♦ Not Started

♦Commissioning:


- ♦ Not Started

♦WAPA Interconnect:

- ♦ Not started

RECEIVING			
	Today	Total Received	Remaining
Bases	0	0	33
Mids	0	0	33
Tops	0	0	33
Nacelles	0	0	33
Controllers	0	0	33
Blades	0	0	33
Transformers	0	0	33
Hubs	0	0	33
4/0 Cable	0	147,874	0
1000 MCM	0	7,245	0

General Information & Announcements

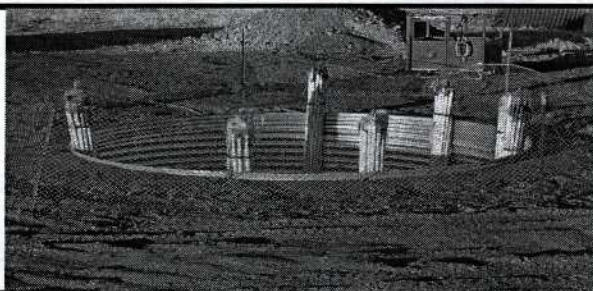

	Complete	Remaining	% complete
Roads Built	14,053	23,101	37.8%
Foundations completed & backfilled	2	31	6.1%
Tower Base sections installed	0	33	0.0%
Tower Mid sections installed	0	33	0.0%
Tower top sections installed	0	33	0.0%
Nacelles Installed	0	33	0.0%
Rotors installed	0	33	0.0%
Mechanically completed	0	33	0.0%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	0	49,291	0.0%
Trenching for 1000MCM cable (ft)	0	2,415	0.0%
Transformers Set/Terminated	0	33	0.0%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.
