



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Sunny  High: 58°F Low: 35°F
 Winds: NW 10-20 MPH Precipitation: 20%chance

Wednesday, September 28th, 2005  95 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

§ Safety/Environmental:

- § Next All Hands safety Wednesday, October 5, 2005 at 7:00 am.
- § No injuries to date.

§ General:

- § Electrical poles were due 9/23/05, now scheduled for delivery 9/30/05.
- § Receiving substation and electrical materials.

§ Road Construction

- § Fabric and gravel continues thru #10-#17.
- § All road sub-base construction is complete with the exception of turbine #3.

§ Foundation Construction:

- § Setting inner can and backfill at #23, #24, and #26.
- § Set outer CMP at #5.
- § Pre Dig #1 and #2.
- § Template setup #24 and #25.

§ Electrical Construction:

- § Grounding crews right behind foundation crews.
- § Pier drilling starts at the substation.
- § Main XFMR containment wall pour today.

§ Tower Erection: Erection Days Lost for High Winds: 0

- § Not Started

§ Mechanical Completion:

- § Not Started

§ Commissioning:


- § Not Started

§ WAPA Interconnect:

- § Not started

| RECEIVING | | | |
|--------------|-------|----------------|-----------|
| | Today | Total Received | Remaining |
| Bases | 0 | 0 | 33 |
| Mids | 0 | 0 | 33 |
| Tops | 0 | 0 | 33 |
| Nacelles | 0 | 0 | 33 |
| Controllers | 0 | 0 | 33 |
| Blades | 0 | 0 | 33 |
| Transformers | 0 | 0 | 33 |
| Hubs | 0 | 0 | 33 |
| 4/0 Cable | 0 | 147,874 | 0 |
| 1000 MCM | 0 | 7,245 | 0 |

General Information & Announcements

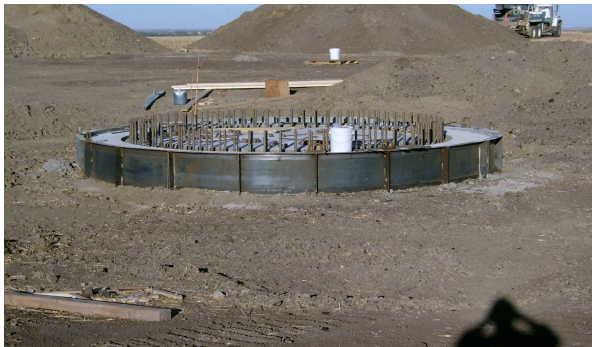

| | Complete | Remaining | % complete |
|------------------------------------|----------|-----------|------------|
| Roads Built | 19,753 | 17,401 | 53.2% |
| Foundations completed & backfilled | 3 | 30 | 9.1% |
| Tower Base sections installed | 0 | 33 | 0.0% |
| Tower Mid sections installed | 0 | 33 | 0.0% |
| Tower top sections installed | 0 | 33 | 0.0% |
| Nacelles Installed | 0 | 33 | 0.0% |
| Rotors installed | 0 | 33 | 0.0% |
| Mechanically completed | 0 | 33 | 0.0% |
| Pre-Commissioned | 0 | 33 | 0.0% |
| Final Commissioned | 0 | 33 | 0.0% |
| Trenching for 4/0 cable (ft) | 0 | 49,291 | 0.0% |
| Trenching for 1000MCM cable (ft) | 0 | 2,415 | 0.0% |
| Transformers Set/Terminated | 0 | 33 | 0.0% |

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.
