



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Snow Shower



High: 37°F Low: 22°F

Winds: NW 10-15 MPH

Precipitation: 60%

Monday, November 14th, 2005



48 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦ **Safety/Environmental:**

- ♦ Daily Safety meeting was held at Construction Trailer.
- ♦ No injuries to date.

♦ **General:**

- ♦ Next Management meeting Wednesday, November 30th, 2005 at 9:00 am.
- ♦ The Marmen tower ship has docked in Duluth, deliveries start this week.

♦ **Road Construction**

- ♦ Complete.

♦ **Foundation Construction:**

- ♦ Pour #31.
- ♦ Pour #32 tomorrow and #33 on Wednesday.

♦ **Electrical Construction:**

- ♦ Erecting substation buss, pulling and terminating control wiring.
- ♦ OPGW installation is on hold for parts.
- ♦ Main Xfmr dress out is complete.
- ♦ Continue setting pad mounts.
- ♦ Pad Mount Xfmr terminations continues.

♦ **Tower Erection: Erection Days Lost for High Winds: 2**

- ♦ Set mid #18 and build rotor.
- ♦ Set base #20 and build rotor.
- ♦ Flew rotors #26 and #27 yesterday.

♦ **Mechanical Completion:**

- ♦ Working #29, dropping cables and starting terminations.

♦ **Commissioning:**

- ♦ Not Started

♦ **WAPA Interconnect:**

- ♦ Interconnect installation continues, setting poles.


RECEIVING			
	Weekend	Total Received	Remaining
Bases	1	9	24
Mids	1	9	24
Tops	1	9	24
Nacelles	3	21	12
Controllers	0	33	0
Blades	4	13	20
Transformers	0	33	0
Hubs	4	28	5
4/0 Cable	0	147,874	0
1000 MCM	0	2,415	0

General Information & Announcements



	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	30	3	90.9%
Tower Base sections installed	9	24	27.3%
Tower Mid sections installed	8	25	24.2%
Tower top sections installed	4	29	12.1%
Nacelles Installed	4	29	12.1%
Rotors installed	4	29	12.1%
Mechanically completed	0	33	0.0%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	500	0	100.0%
Transformers Set/Terminated	13	20	39.4%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Partly Cloudy



High: 60°F Low: 37°F

Winds: NW 5-10 MPH

Precipitation: 50%

Friday, November 11th, 2005



51 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦ Safety/Environmental:

- ♦ Daily Safety meeting was held at 7:00 am at Construction Trailer.
- ♦ No injuries to date.

♦ General:

- ♦ Next Management meeting Wednesday, November 30th, 2005 at 9:00 am.
- ♦ The Marmen tower ship has docked in Duluth, deliveries start next week.

♦ Road Construction

- ♦ Clean up continues across the site.

♦ Foundation Construction:

- ♦ Setup #31, #32, and #33.

♦ Electrical Construction:

- ♦ Erecting substation steel, working control wiring.
- ♦ OPGW installation is on hold for parts.
- ♦ Main Xfmr dress out is complete.
- ♦ Continue setting pad mounts.
- ♦ Pad Mount Xfmr terminations continues.
- ♦ Fiber Optic terminations starts Monday.

♦ Tower Erection: Erection Days Lost for High Winds: 1

- ♦ Set base and mid #18.
- ♦ Building crane pads.
- ♦ Fly rotor #28.
- ♦ Build out #27.

♦ Mechanical Completion:

- ♦ Working #29, dropping cables and starting terminations.

♦ Commissioning:

- ♦ Not Started

♦ WAPA Interconnect:

- ♦ Interconnect installation continues, setting poles.

RECEIVING			
	Yesterday	Total Received	Remaining
Bases	1	8	25
Mids	1	8	25
Tops	1	8	25
Nacelles	1	18	15
Controllers	0	33	0
Blades	0	9	24
Transformers	0	33	0
Hubs	1	24	9
4/0 Cable	0	147,874	0
1000 MCM	0	2,415	0

General Information & Announcements




	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	30	3	90.9%
Tower Base sections installed	7	26	21.2%
Tower Mid sections installed	7	26	21.2%
Tower top sections installed	2	31	6.1%
Nacelles Installed	2	31	6.1%
Rotors installed	1	32	3.0%
Mechanically completed	0	33	0.0%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	500	0	100.0%
Transformers Set/Terminated	13	20	39.4%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPL.



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Sunny  High: 57°F Low: 35°F
 Winds: WSW 5-10 MPH Precipitation: 0%

Thursday, November 10th, 2005  52 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦ Safety/Environmental:

- ♦ Daily Safety meeting was held at 7:00 am at Construction Trailer.
- ♦ No injuries to date.

♦ General:

- ♦ Next Management meeting Wednesday, November 30th, 2005 at 9:00 am.

♦ Road Construction

- ♦ Clean up continues across the site.

♦ Foundation Construction:

- ♦ Pour #30 today.
- ♦ Setup #31 and #33.
- ♦ Slurry #32.

♦ Electrical Construction:

- ♦ Erecting substation steel, received second shipment of substation this morning. This shipment appears to be short (still investigating).
- ♦ OPGW installation is on hold for parts.
- ♦ Main Xfmr dress out continues.
- ♦ Continue setting pad mounts.
- ♦ Pad Mount Xfmr terminations continues.

♦ Tower Erection: Erection Days Lost for High Winds: 1

- ♦ Set Mid #23.
- ♦ Building crane pads.
- ♦ Preparing #28 for top out.
- ♦ #29 fly rotor.

♦ Mechanical Completion:

- ♦ Not Started

♦ Commissioning:


- ♦ Not Started

♦ WAPA Interconnect:

- ♦ Interconnect tap installation continues.

RECEIVING			
	Yesterday	Total Received	Remaining
Bases	1	7	26
Mids	1	7	26
Tops	1	7	26
Nacelles	1	17	16
Controllers	0	33	0
Blades	1	9	24
Transformers	0	33	0
Hubs	0	23	10
4/0 Cable	0	147,874	0
1000 MCM	0	2,415	0

General Information & Announcements

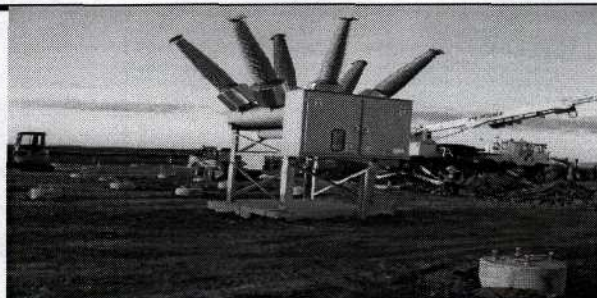

	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	29	4	87.9%
Tower Base sections installed	7	26	21.2%
Tower Mid sections installed	6	27	18.2%
Tower top sections installed	1	32	3.0%
Nacelles Installed	1	32	3.0%
Rotors installed	0	33	0.0%
Mechanically completed	0	33	0.0%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	500	0	100.0%
Transformers Set/Terminated	6	27	18.2%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Partly Cloudy



High: 44°F Low: 28°F

Winds: W 20-30 MPH

Precipitation: 20%

Wednesday, November 9th, 2005



53 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦ Safety/Environmental:

- ♦ Daily Safety meeting was held at 7:00 am at Construction Trailer.
- ♦ No injuries to date.

♦ General:

- ♦ Next Management meeting Wednesday, November 30th, 2005 at 9:00 am.

♦ Road Construction

- ♦ Clean up continues across the site.

♦ Foundation Construction:

- ♦ Pour #10 today.
- ♦ Setup #30 and #31.
- ♦ Slurry #32 and #33.

♦ Electrical Construction:

- ♦ Erecting substation steel.
- ♦ OPGW installation continues.
- ♦ Main Xfmr dress out continues.
- ♦ Continue setting pad mounts.
- ♦ Pad Mount Xfmr terminations continues.
- ♦ Continue underground installation.(1000 MCM)

♦ Tower Erection: Erection Days Lost for High Winds: 1

- ♦ Set Base and Mid #24.
- ♦ Building crane pads.
- ♦ High winds may delay turbine erection at #29.

♦ Mechanical Completion:

- ♦ Not Started

♦ Commissioning:

- ♦ Not Started

♦ WAPA Interconnect:

- ♦ Interconnect tap installation continues.

RECEIVING			
	Yesterday	Total Received	Remaining
Bases	1	6	27
Mids	1	6	27
Tops	1	6	27
Nacelles	0	16	17
Controllers	0	33	0
Blades	1	8	25
Transformers	0	33	0
Hubs	0	23	10
4/0 Cable	0	147,874	0
1000 MCM	0	2,415	0

General Information & Announcements



	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	28	5	84.8%
Tower Base sections installed	5	28	15.2%
Tower Mid sections installed	4	29	12.1%
Tower top sections installed	0	33	0.0%
Nacelles installed	0	33	0.0%
Rotors installed	0	33	0.0%
Mechanically completed	0	33	0.0%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	350	200	63.6%
Transformers Set/Terminated	5	28	15.2%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: PM Showers



High: 49°F Low: 27°F

Winds: W 20-30 MPH

Precipitation: 30%

Tuesday, November 8th, 2005



54 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦ Safety/Environmental:

- ♦ Daily Safety meeting was held at 7:00 am at Construction Trailer.
- ♦ No injuries to date.

♦ General:

- ♦ Next Management meeting Wednesday, November 30th, 2005 at 9:00 am.
- ♦ Received 1 of 2 substation steel shipments.

♦ Road Construction

- ♦ Clean up continues across the site.

♦ Foundation Construction:

- ♦ Pour #11 today.
- ♦ Setup #10 and #30.
- ♦ Slurry #32 and #33.

♦ Electrical Construction:

- ♦ OPGW installation continues.
- ♦ Main Xfmr dress out continues.
- ♦ Continue setting pad mounts.
- ♦ Pad Mount Xfmr terminations continues.
- ♦ Continue underground installation.(1000 MCM)

♦ Tower Erection: Erection Days Lost for High Winds: 0

- ♦ Set Base #25.
- ♦ Building crane pads.
- ♦ High winds will probably delay turbine erection at #29.

♦ Mechanical Completion:

- ♦ Not Started

♦ Commissioning:


- ♦ Not Started

♦ WAPA Interconnect:

- ♦ Interconnect tap installation continues.


RECEIVING			
	Yesterday	Total Received	Remaining
Bases	1	5	28
Mids	1	5	28
Tops	1	5	28
Nacelles	1	16	17
Controllers	3	33	0
Blades	0	7	26
Transformers	0	33	0
Hubs	0	23	10
4/0 Cable	0	147,874	0
1000 MCM	0	1,000	0

General Information & Announcements

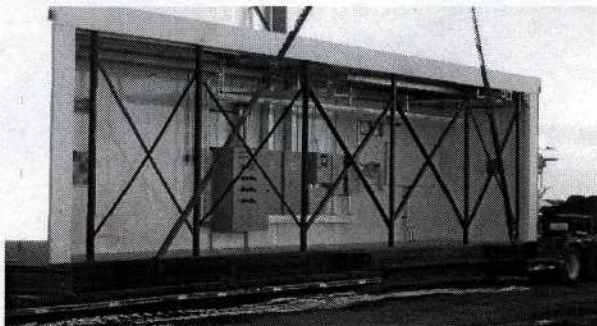

	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	27	6	81.8%
Tower Base sections installed	4	29	12.1%
Tower Mid sections installed	3	30	9.1%
Tower top sections installed	0	33	0.0%
Nacelles Installed	0	33	0.0%
Rotors installed	0	33	0.0%
Mechanically completed	0	33	0.0%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	0	1,000	0.0%
Transformers Set/Terminated	5	28	15.2%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Partly Cloudy



High: 50°F Low: 31°F

Winds: NNW 5-10 MPH

Precipitation: 20%

Monday, November 7th, 2005



55 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦ Safety/Environmental:

- ♦ Daily Safety meeting was held at 7:00 am at Construction Trailer.
- ♦ No injuries to date.

♦ General:

- ♦ Next Management meeting Wednesday, November 30th, 2005 at 9:00 am.

♦ Road Construction

- ♦ Clean up continues across the site.

♦ Foundation Construction:

- ♦ Pour #12 today.
- ♦ Setup #10.
- ♦ Slurry #32 and #33.

♦ Electrical Construction:

- ♦ OPGW installation continues.
- ♦ Main Xfmr dress out continues.
- ♦ Continue setting pad mounts.
- ♦ Pad Mount Xfmr terminations continues.
- ♦ Continue underground installation.
- ♦ The substation switchgear has been delivered, unloaded and set.
- ♦ **Substation construction has slowed due to lack of materials (steel and buss work)**

♦ Tower Erection: Erection Days Lost for High Winds: 0

- ♦ Set Base #26.

♦ Mechanical Completion:

- ♦ Not Started

♦ Commissioning:

- ♦ Not Started

♦ WAPA Interconnect:

- ♦ Interconnect tap installation continues.

RECEIVING			
	Weekend	Total Received	Remaining
Bases	1	4	29
Mids	1	4	29
Tops	0	4	29
Nacelles	0	15	18
Controllers	6	30	3
Blades	1	7	26
Transformers	0	33	0
Hubs	4	23	10
4/0 Cable	0	147,874	0
1000 MCM	0	7,245	0

General Information & Announcements



	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	26	7	78.8%
Tower Base sections installed	3	30	9.1%
Tower Mid sections installed	2	31	6.0%
Tower top sections installed	0	33	0.0%
Nacelles Installed	0	33	0.0%
Rotors installed	0	33	0.0%
Mechanically completed	0	33	0.0%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	0	2,415	0.0%
Transformers Set/Terminated	3	30	9.1%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPL.
