

# Burleigh County Wind, LLC; Wilton, ND

## Plan of the Day (POD)

Weather Forecast: Partly Cloudy



High: 50°F Low: 38°F

Winds: WNW 10-20 MPH

Precipitation: 20%

Tuesday, November 22th, 2005



FPL Energy

40 Days to Completion

5 Days to SWPP Inspection

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

### Activities:

#### ♦ Safety/Environmental:

- ♦ Daily Safety meeting was held at Construction Trailer.
- ♦ No injuries to date.

#### ♦ General:

- ♦ Next Management meeting Wednesday, November 30<sup>th</sup>, 2005 at 9:00 am.

#### ♦ Electrical Construction:

- ♦ Fiber Optic terminations/splices continues.
- ♦ Installing substation fence.
- ♦ Erecting substation buss, pulling and terminating control wiring.
- ♦ OPGW installation is on hold for parts.
- ♦ Pad Mount Xfmr terminations continues.

#### ♦ Tower Erection: Erection Days Lost for High Winds: 6

- ♦ Stack out #18.
- ♦ Setting bases and mids as they arrive.

#### ♦ Mechanical Completion:

- ♦ Working #24-#27 cable drops.

#### ♦ Commissioning:


- ♦ GE lead and one tech here on Monday.

#### ♦ WAPA Interconnect:

- ♦ Interconnect installation continues.

RECEIVING			
	Yesterday	Total Received	Remaining
Bases	1	16	17
Mids	1	16	17
Tops	1	16	17
Nacelles	0	25	8
Controllers	0	33	0
Blades	0	18	15
Transformers	0	33	0
Hubs	1	32	1
4/0 Cable	0	147,874	0
1000 MCM	0	2,415	0

## General Information & Announcements

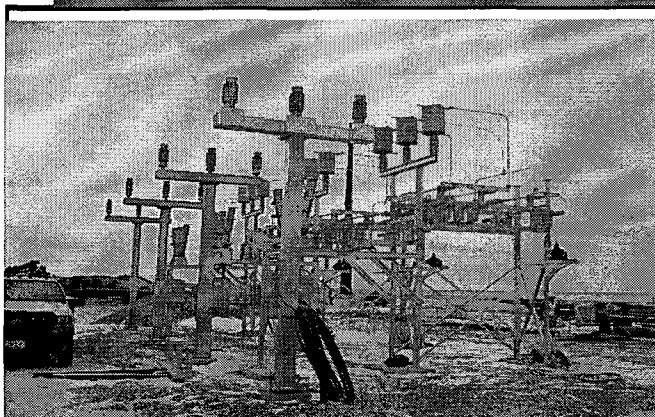

	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	33	0	100.0%
Tower Base sections installed	14	19	42.4%
Tower Mid sections installed	12	21	36.4%
Tower top sections installed	7	26	21.2%
Nacelles Installed	7	26	21.2%
Rotors installed	7	26	21.2%
Mechanically completed	2	31	6.1%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	500	0	100.0%
Transformers Set/Terminated	30	3	90.9%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.
