

Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Cloudy/Wind High: 45°F Low: 17°F
 Winds: NNW 20-30 MPH Precipitation: 20%



Wednesday, November 23th, 2005



FPL Energy

39 Days to Completion

4 Days to SWPP Inspection

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦ Safety/Environmental:

- ♦ Daily Safety meeting was held at Construction Trailer.
- ♦ No injuries to date.

♦ General:

- ♦ Next Management meeting Wednesday, November 30th, 2005 at 9:00 am.

♦ Electrical Construction:

- ♦ Rework at substation switchgear terminations due to engineering changes.
- ♦ Fiber Optic terminations/splices continues.
- ♦ Substation relay testing in progress.
- ♦ Erecting substation buss, pulling and terminating control wiring.
- ♦ OPGW installation will finish Monday.

♦ Tower Erection: Erection Days Lost for High Winds: 7

- ♦ Prepping and building crane pad mats.
- ♦ High winds today preventing turbine erection.
- ♦ Setting bases and mids as they arrive.

♦ Mechanical Completion:

- ♦ Working #23-#27 cable drops and terminations.

♦ Commissioning:


- ♦ Start Pre-commissioning Tuesday 11/29/05.

♦ WAPA Interconnect:

- ♦ Interconnect installation continues.

RECEIVING			
	Yesterday	Total Received	Remaining
Bases	3	19	14
Mids	1	17	16
Tops	1	17	16
Nacelles	0	25	8
Controllers	0	33	0
Blades	2	20	13
Transformers	0	33	0
Hubs	0	32	1
4/0 Cable	0	147,874	0
1000 MCM	0	2,415	0

General Information & Announcements

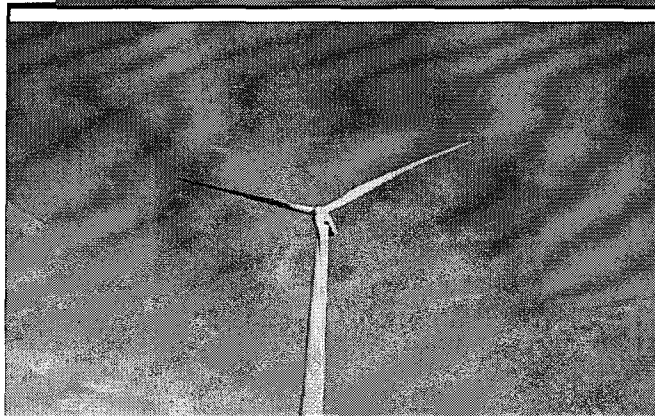

	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	33	0	100.0%
Tower Base sections installed	15	18	45.5%
Tower Mid sections installed	14	19	42.4%
Tower top sections installed	8	25	24.2%
Nacelles Installed	8	25	24.2%
Rotors installed	7	26	21.2%
Mechanically completed	2	31	6.1%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	500	0	100.0%
Transformers Set/Terminated	33	0	100.0%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.
