

Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: AM Snow/Wind

High: 22°F Low: 14°F

Winds: NNW 20-30 MPH



Precipitation: 30%

Monday, November 28th, 2005



FPL Energy

34 Days to Completion

13 Days to SWPP Inspection


FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

- ♦ **Safety/Environmental:**
 - ♦ Daily Safety meeting was held at Construction Trailer.
 - ♦ No injuries to date.
- ♦ **General:**
 - ♦ Next Management meeting Wednesday, November 30th, 2005 at 9:00 am.
- ♦ **Electrical Construction:**
 - ♦ 230 KV Breaker parts have been delivered.
 - ♦ Installing Substation static masts.
 - ♦ Substation buss work is complete.
 - ♦ Fiber Optic terminations/splices continues.
 - ♦ Substation relay testing in progress.
 - ♦ Pulling and terminating substation control wiring.
 - ♦ OPGW installation is delayed due to high winds.
- ♦ **Tower Erection: Erection Days Lost for High Winds: 8**
 - ♦ Prepping and building crane pad mats.
 - ♦ High winds today preventing turbine erection.
 - ♦ Tower and blade deliveries are being delayed due to weather.
- ♦ **Mechanical Completion:**
 - ♦ Working #23-#27 cable drops and terminations.
- ♦ **Commissioning:**
 - ♦ Start Pre-commissioning Tuesday 11/29/05.
- ♦ **WAPA Interconnect:**
 - ♦ Interconnect installation continues.

RECEIVING			
	Weekend	Total Received	Remaining
Bases	0	19	14
Mids	1	18	15
Tops	2	19	14
Nacelles	1	26	7
Controllers	0	33	0
Blades	2	22	11
Transformers	0	33	0
Hubs	0	32	1
4/0 Cable	0	147,874	0
1000 MCM	0	2,415	0

General Information & Announcements

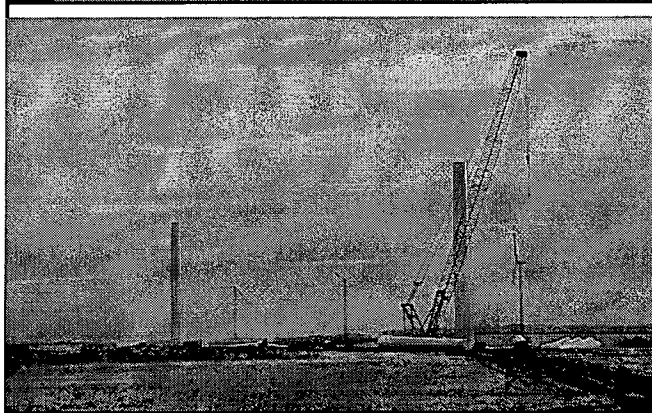

	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	33	0	100.0%
Tower Base sections installed	15	18	45.5%
Tower Mid sections installed	14	19	42.4%
Tower top sections installed	9	24	27.3%
Nacelles Installed	9	24	27.3%
Rotors installed	9	24	27.3%
Mechanically completed	2	31	6.1%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	500	0	100.0%
Transformers Set/Terminated	33	0	100.0%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.
