



FPL ENERGY LANGDON WIND, LLC

LANGDON, NORTH DAKOTA

Plan of the Day (POD)

Weather Forecast: **Sunny**

High: **57°F** / Low: **32°F**

Winds: **E @ 5-15 mph**

Rain Chances: **20%**

Rain received this month: **1.0 inches**

Monday, October 15, 2007 COD **December 31, 2007** **78 Days to COD**

FPL Energy

D.H. Blattner

GEWE

Safety/Environmental:

- Near T13, be aware of possible swarming bees
- Watch for slippery surfaces due to rain
- Blattner will be holding First Aid Classes during the month of October
- Be aware of pinch points
- Lights on for safety
- Watch for soft shoulders
- Appropriate PPE is required at all times!
- Maximum speed limit on site is 25 mph for all vehicles
- Slow down to 5-10 mph when passing crews working near the road

Civil:

- Building crane pads at T21, T22, T48-T53

Erection:

- Setting base & mid at T16 & T36, base at T17 & T34
- Assembling rotor at T16, T36
- Erecting top at T13
- Installing machine head at T13
- Flying rotor at T13

Collection:

- (4/0)Trenching & installing on from T4-T1, T23-T26

Installation:

O & M:

- Installing sheetrock on interior walls


FUTURE ACTIVITIES:

- Next SWPPP inspection scheduled for October 16

RECEIVING (As of COB Yesterday)

	Total	Rec'd	Balanc
Bases	79	12	67
Mids	79	12	67
Tops	79	14	65
Machine Heads	79	0	79
Down Tower Assemblies	79	32	47
Blade Sets	79	16	63
Hubs	79	8	71
Grounding XFR	7	3	4
PMT XFR	79	0	79
4/0 Cable	504,000	510,034	0
1000 KCM	333,000	339,914	0
12 SM Fiber	152,000	143,975	8,025
12 MM Fiber	144,000	152,087	0
DLO Substitute	27,500	28,220	0
Copper Clad Steel	54,000	30,666	23,334

General Construction Status

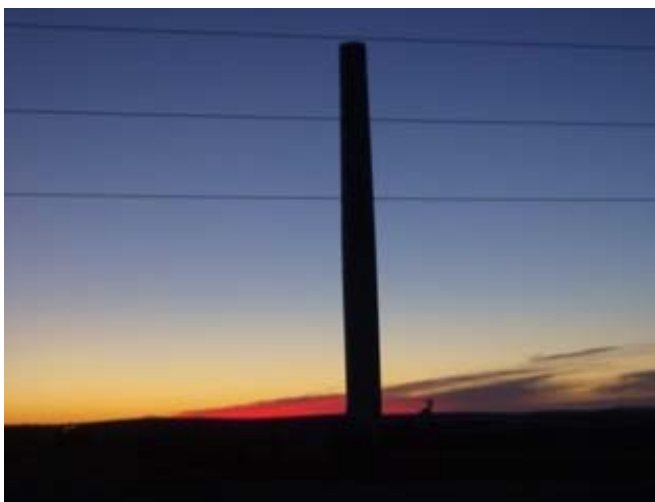

	Complete	Total	% complete
Roads subgraded	98,843	118,924	83.1%
Roads complete	98,843	118,924	83.1%
Foundations excavated	79	79	100.0%
Foundations poured	79	79	100.0%
Foundations backfilled	79	79	100.0%
Crane pads complete	30	79	38.0%
Tower base sections erected	6	79	7.6%
Tower mid sections erected	6	79	7.6%
Tower top sections erected	0	79	0.0%
Machine Heads installed	0	79	0.0%
Rotors flown	0	79	0.0%
Mechanically completed	0	79	0.0%
Pre-commissioned	0	79	0.0%
Final commissioned	0	79	0.0%
Underground trenching instal.(ft)-4/0	413,031	517,688	79.8%
Underground trenching instal.(ft)-1000	312,498	275,105	113.6%
Underground trenching instal.(ft)-12 MM	137,677	145,783	94.4%
Underground trenching instal.(ft)-12 SM	104,166	142,390	73.2%
Transformers set/terminated	0	79	0.0%
(as of COB yesterday)			

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE
