


Rhame to Belfield T-line (Rev. 1)



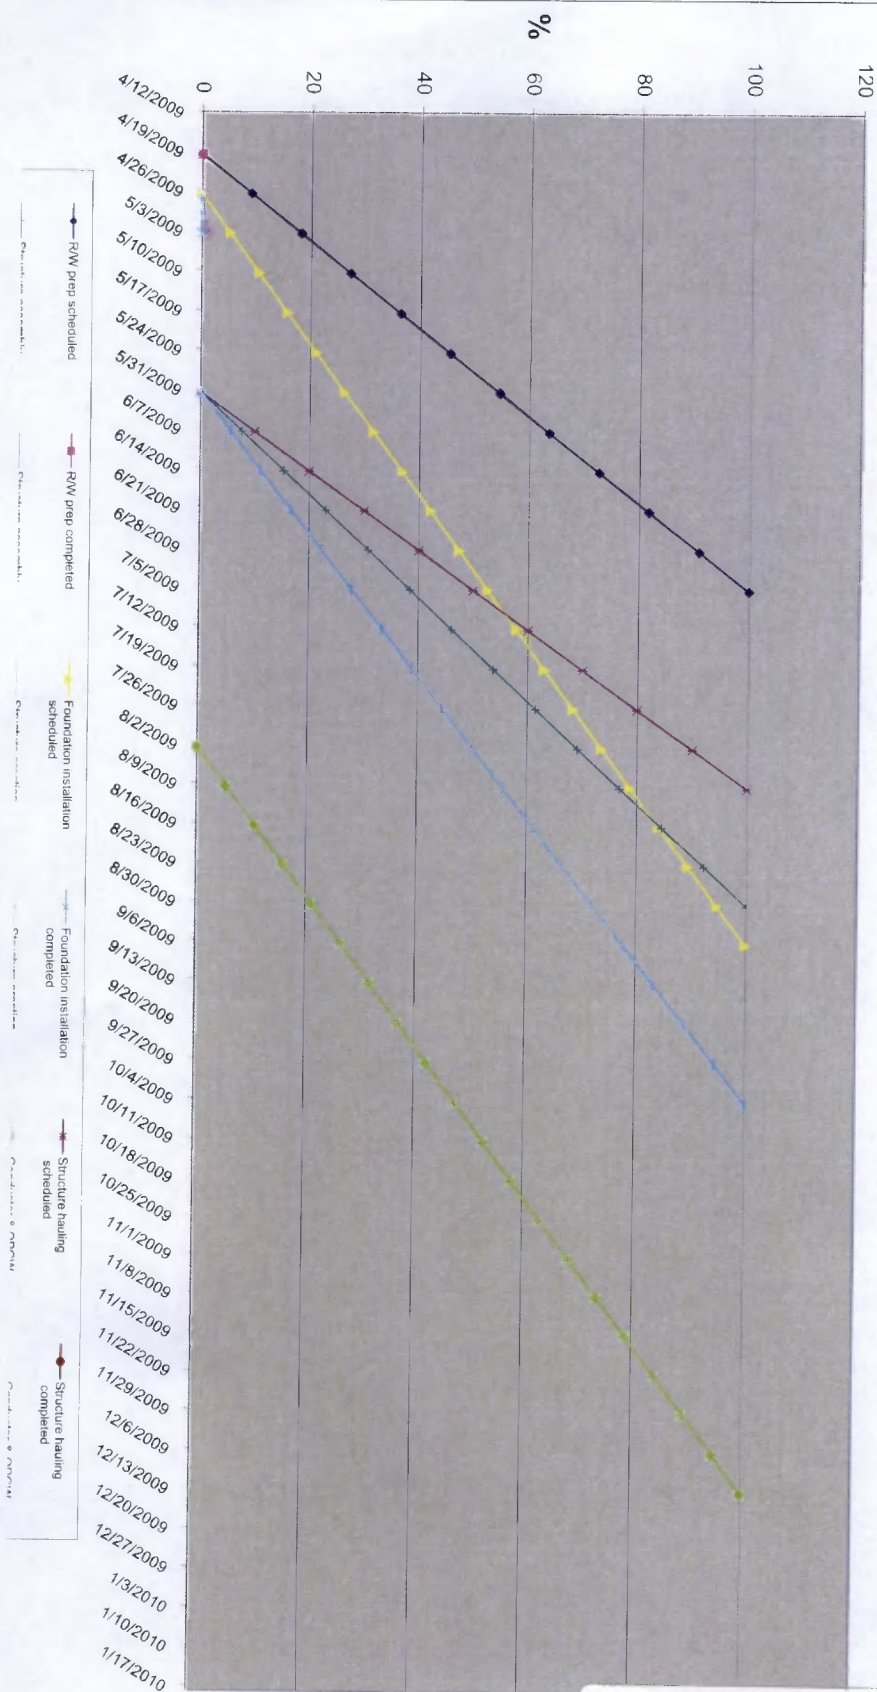

Date	R/W prep scheduled	R/W prep completed	Foundation installation scheduled	Foundation installation completed	Structure hauling scheduled	Structure hauling completed	Structure assembly scheduled	Structure assembly completed	Structure erection scheduled	Structure erection completed	Conductor & OPGW pulling scheduled	Conductor & OPGW pulling completed	R/W cleanup scheduled	R/W cleanup completed	R/W restoration scheduled	R/W restoration completed
4/12/2009																
4/19/2009	0	0														
4/26/2009	9.09	0	0	0												
5/3/2009	18.18	1	5.26	0												
5/10/2009	27.27		10.52	0												
5/17/2009	36.36		15.78													
5/24/2009	45.45		21.05													
5/31/2009	54.54		26.31		0		0		0							
6/7/2009	63.63		31.57		10	7.69			5.55							
6/14/2009	72.72		36.84		20	15.38			11.11							
6/21/2009	81.81		42.1		30	23.07			16.67							
6/28/2009	90.9		47.36		40	30.76			22.22							
7/5/2009	100		52.63		50	38.46			27.77							
7/12/2009			57.89		60	46.15			33.33							
7/19/2009			63.15		70	53.84			38.88							
7/26/2009			68.42		80	61.53			44.44							
8/2/2009			73.68		90	69.23			50							
8/9/2009			78.94		100	76.92			55.55							
8/16/2009			84.2			84.61			61.11		5.26			0		
8/23/2009			89.47			92.3			66.66		10.52		5.26	0		
8/30/2009			94.73			100			72.22		15.78		10.52	0		
9/6/2009			100						77.77		21.05		15.78	0		
9/13/2009									83.33		26.31		15.78	0		
9/20/2009									88.88		31.57		15.78	0		
9/27/2009									94.44		36.84		15.78	0		
10/4/2009									100		42.1		15.78	0		
10/11/2009											47.36		15.78	0		
10/18/2009											52.63		15.78	0		
10/25/2009											57.89		15.78	0		
11/1/2009											63.15		15.78	0		
11/8/2009											68.42		15.78	0		
11/15/2009											73.68		15.78	0		
11/22/2009											78.94		15.78	0		
11/29/2009											84.2		15.78	0		
12/6/2009											89.47		15.78	0		
											94.73		15.78	0		

BASIN ELECTRIC POWER COOPERATIVE
Project: Rhame to Belfield T-line Contract
Contractor: TESSCO

Weekly Progress Report

Progress for the week ending : 5/2/2009

Manpower = 8

- Note:
- Completion the past week
 - Completion to date
 - Condemnation proceedings @ Str#
 - X - indicates a foundation location

Str #1 @ Rhame and Str #524 @ Belfield


	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep	5	1.0	5	1.0
Foundation Inst'l. (55)	0.0	0.0	0.0	0.0
Structure hauling	0.0	0.0	0.0	0.0
Structure assembly	0.0	0.0	0.0	0.0
Conductor/OPGW installation	0.0	0.0	0.0	0.0
R/W cleanup	0.0	0.0	0.0	0.0
R/W restoration	0.0	0.0	0.0	0.0

Str. Number	Takeoff
R/W prep	1
Foundation Installation	2
Structure hauling	3
Structure assembly	4
Structure erection	5
Conductor/OPGW installation	6
R/W cleanup	7
R/W restoration	8
Condemnation proceedings	9
	10
	11
	12
	13
	14
	15
	16
	17
	18
	19
	20
	21
	22
	23
	24
	25
	26
	27
	28
	29
	30
	31
	32
	33
	34
	35
	36
	37
	38
	39
	40
	41
	42
	43
	44
	45
	46
	47
	48
	49
	50

51	
52	
53	
54	
55	
56	
57	
58	X
59	
60	
61	X
62	
63	
64	
65	
66	
67	
68	
69	
70	
71	
72	
73	
74	
75	X
76	
77	
78	
79	
80	
81	
82	
83	
84	
85	X
86	
87	
88	
89	
90	
91	
92	
93	
94	
95	
96	
97	X
98	
99	
100	

Basin Electric Power Cooperative
 Rhame Substation Grading
 Contractor: Northern Improvement

Rhame Sub Grading

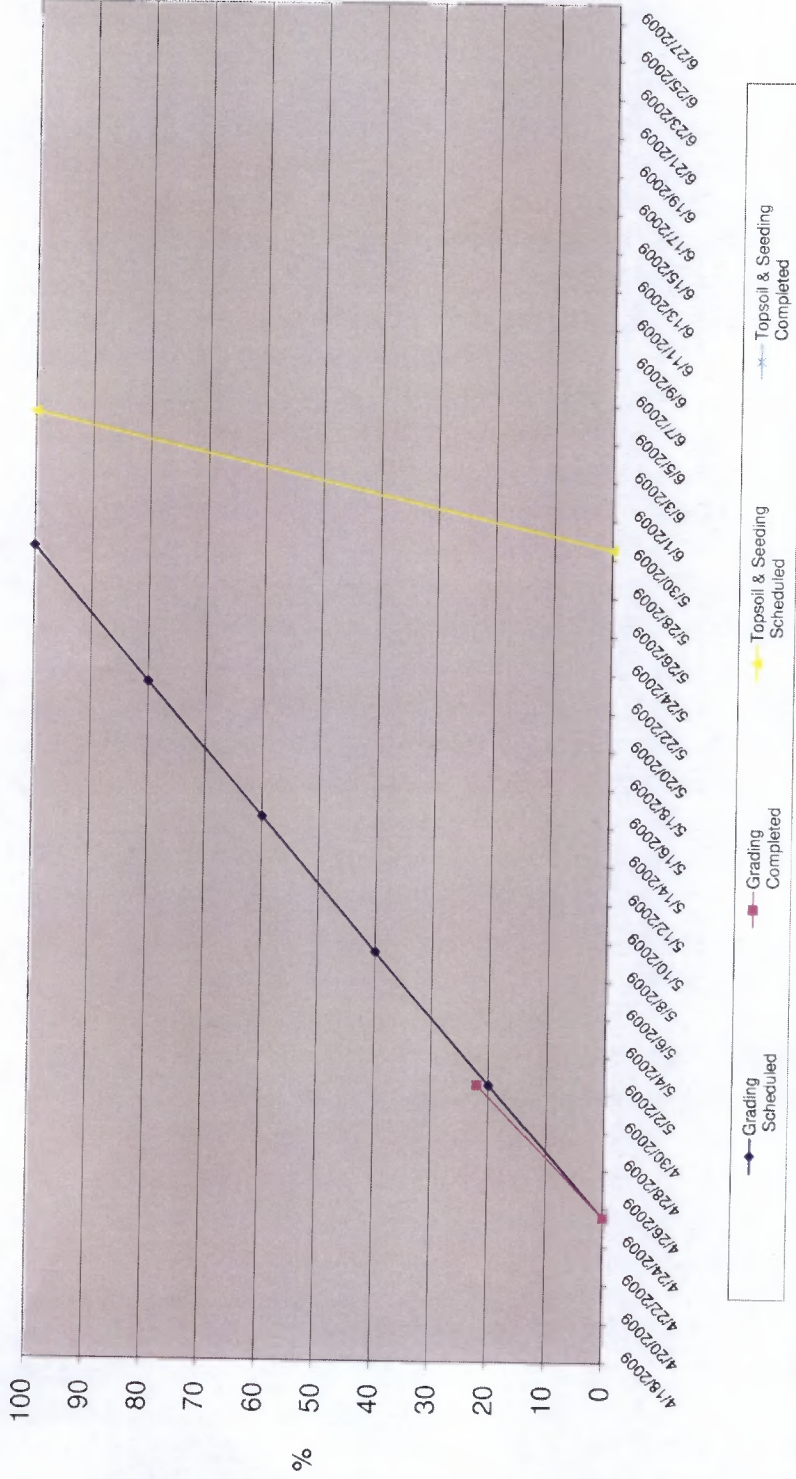

Date	Grading Completed	Grading Scheduled	Topsoil & Seeding Completed	Topsoil & Seeding Scheduled
4/18/2009	0	0	0	0
4/25/2009	0	0	0	0

