

BASIN ELECTRIC POWER COOPERATIVE
Project: Rhame to Belfield T-line Contract
Contractor: TESSCO

Weekly Progress Report




Progress for the week ending : 06/06/2009

Manpower = 24

| | Weekly total | Weekly % | Cumulative total | Cumulative % |
|-----------------------------|--------------|----------|------------------|--------------|
| R/W Prep | 68 | 13.0 | 238 | 45.4 |
| Foundation Instl. (55) | 4 | 7.3 | 15 | 27.3 |
| Structure hauling | 4 | 0.8 | 7 | 1.3 |
| Structure assembly | | 0.0 | | 0.0 |
| Structure erection | | 0.0 | | 0.0 |
| Conductor/OPGW installation | | 0.0 | | 0.0 |
| R/W cleanup | | 0.0 | | 0.0 |
| R/W restoration | | 0.0 | | 0.0 |

- Note:
- Completion the past week
 - Completion to date
 - Condemnation proceedings
 - X - indicates a foundation location

Str.#1 @ Rhame and Str #524 @ Belfield

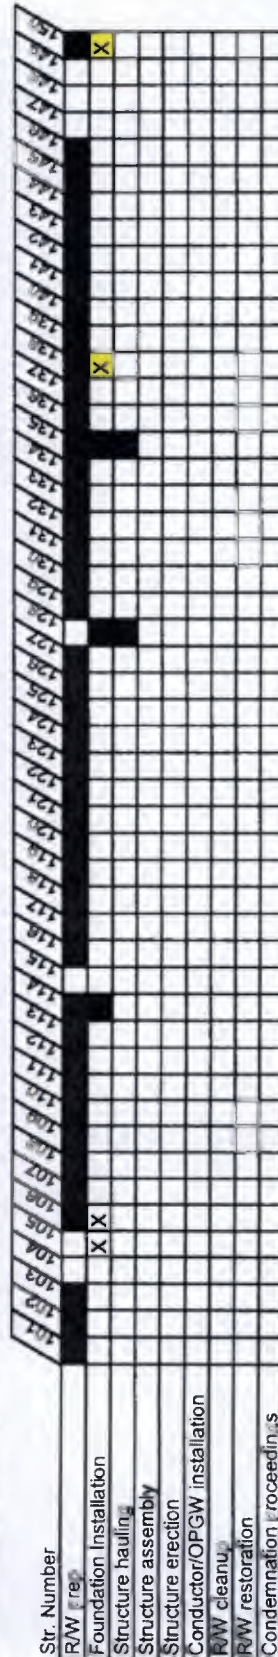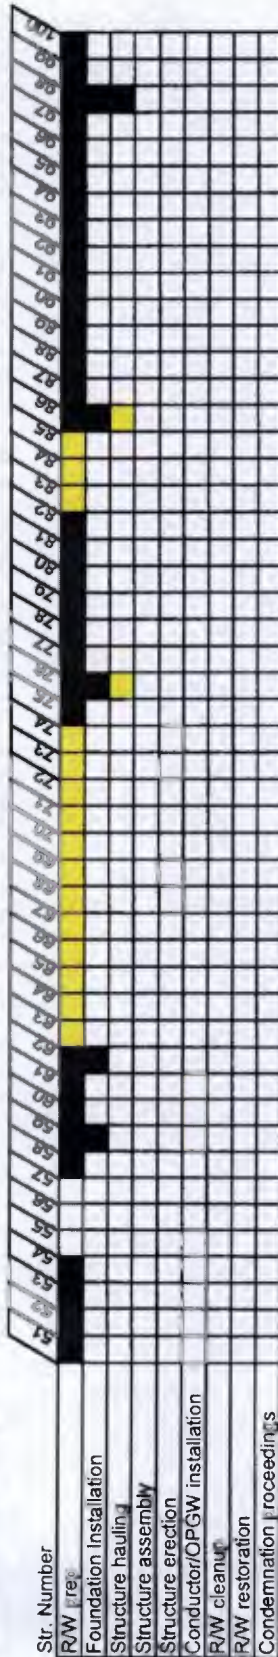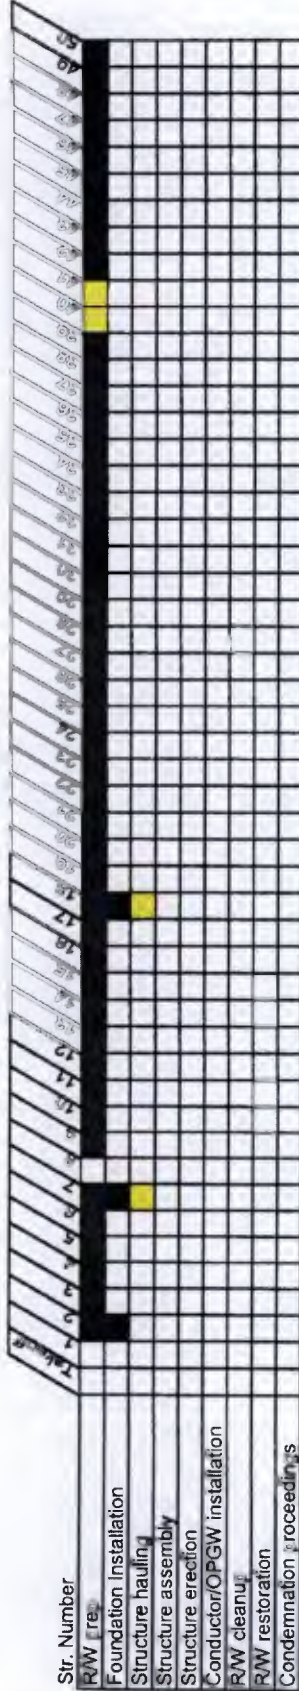

Rhame Sub Grading

