

BASIN ELECTRIC POWER COOPERATIVE
Project: Rhame to Belfield T-line Contract
Contractor: TESSCO

Weekly Progress Report




Progress for the week ending : 06/27/2009

Manpower = 24


- Note:
- Completion the past week
 - Completion to date
 - Condemnation proceedings
 - X - indicates a foundation location

Str #1 @ Rhame and Str #524 @ Belfield

	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep	92	17.6	347	86.2
Foundation Instl. (55)	9	16.4	27	49.1
Structure hauling	51	9.7	58	11.1
Structure assembly		0.0		0.0
Structure erection		0.0		0.0
Conductor/OPGW installation		0.0		0.0
R/W cleanup		0.0		0.0
R/W restoration		0.0		0.0

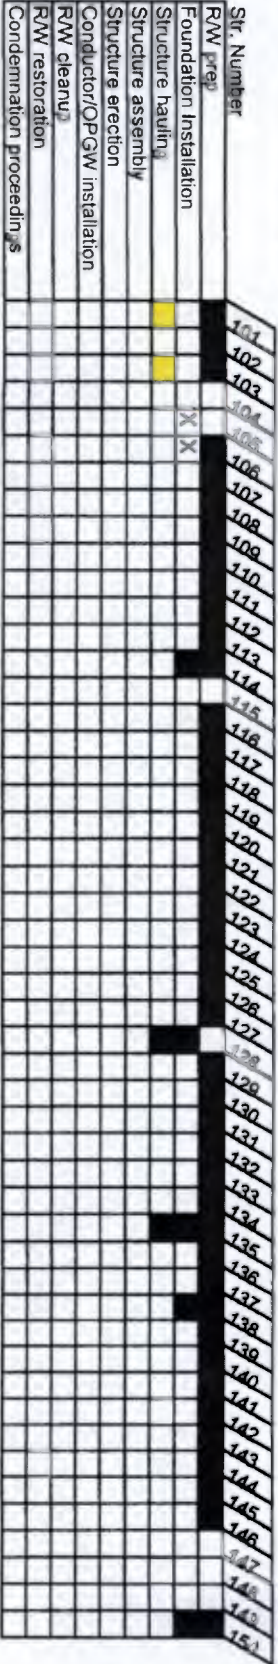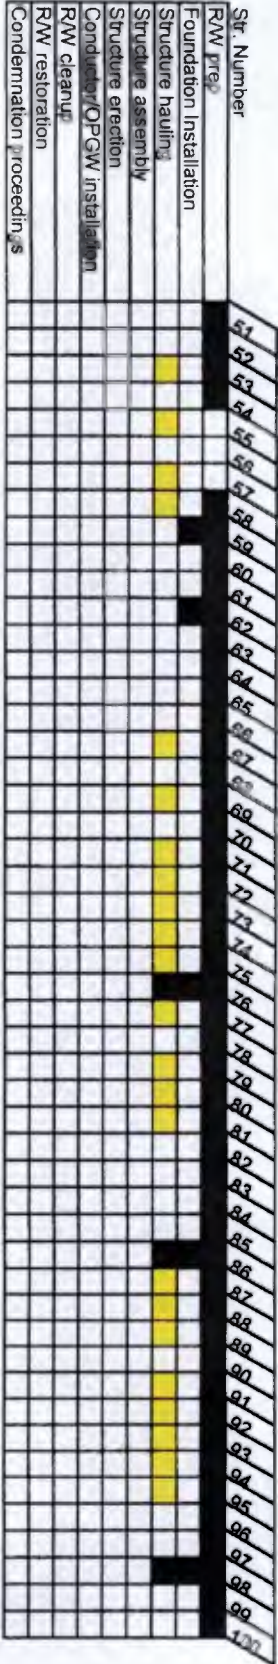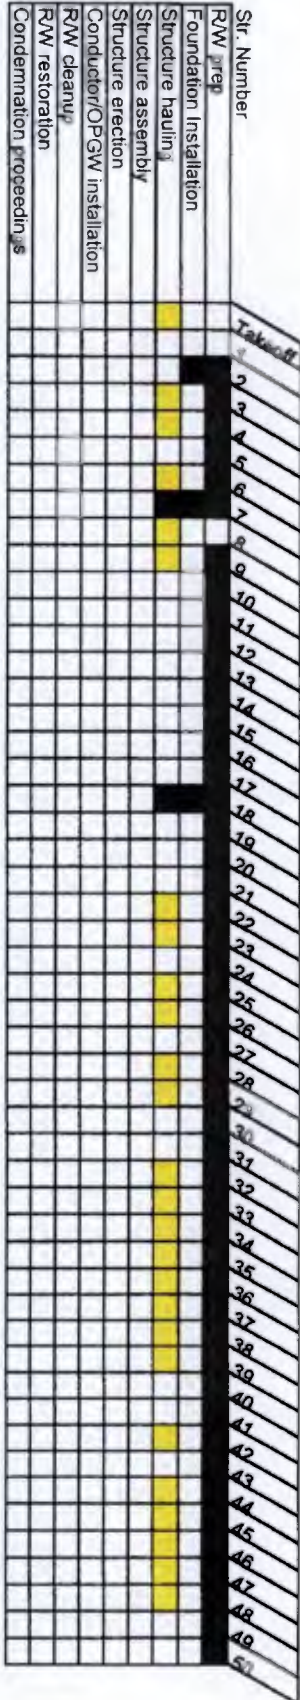

Rhame to Belfield T-line (Rev. 1)

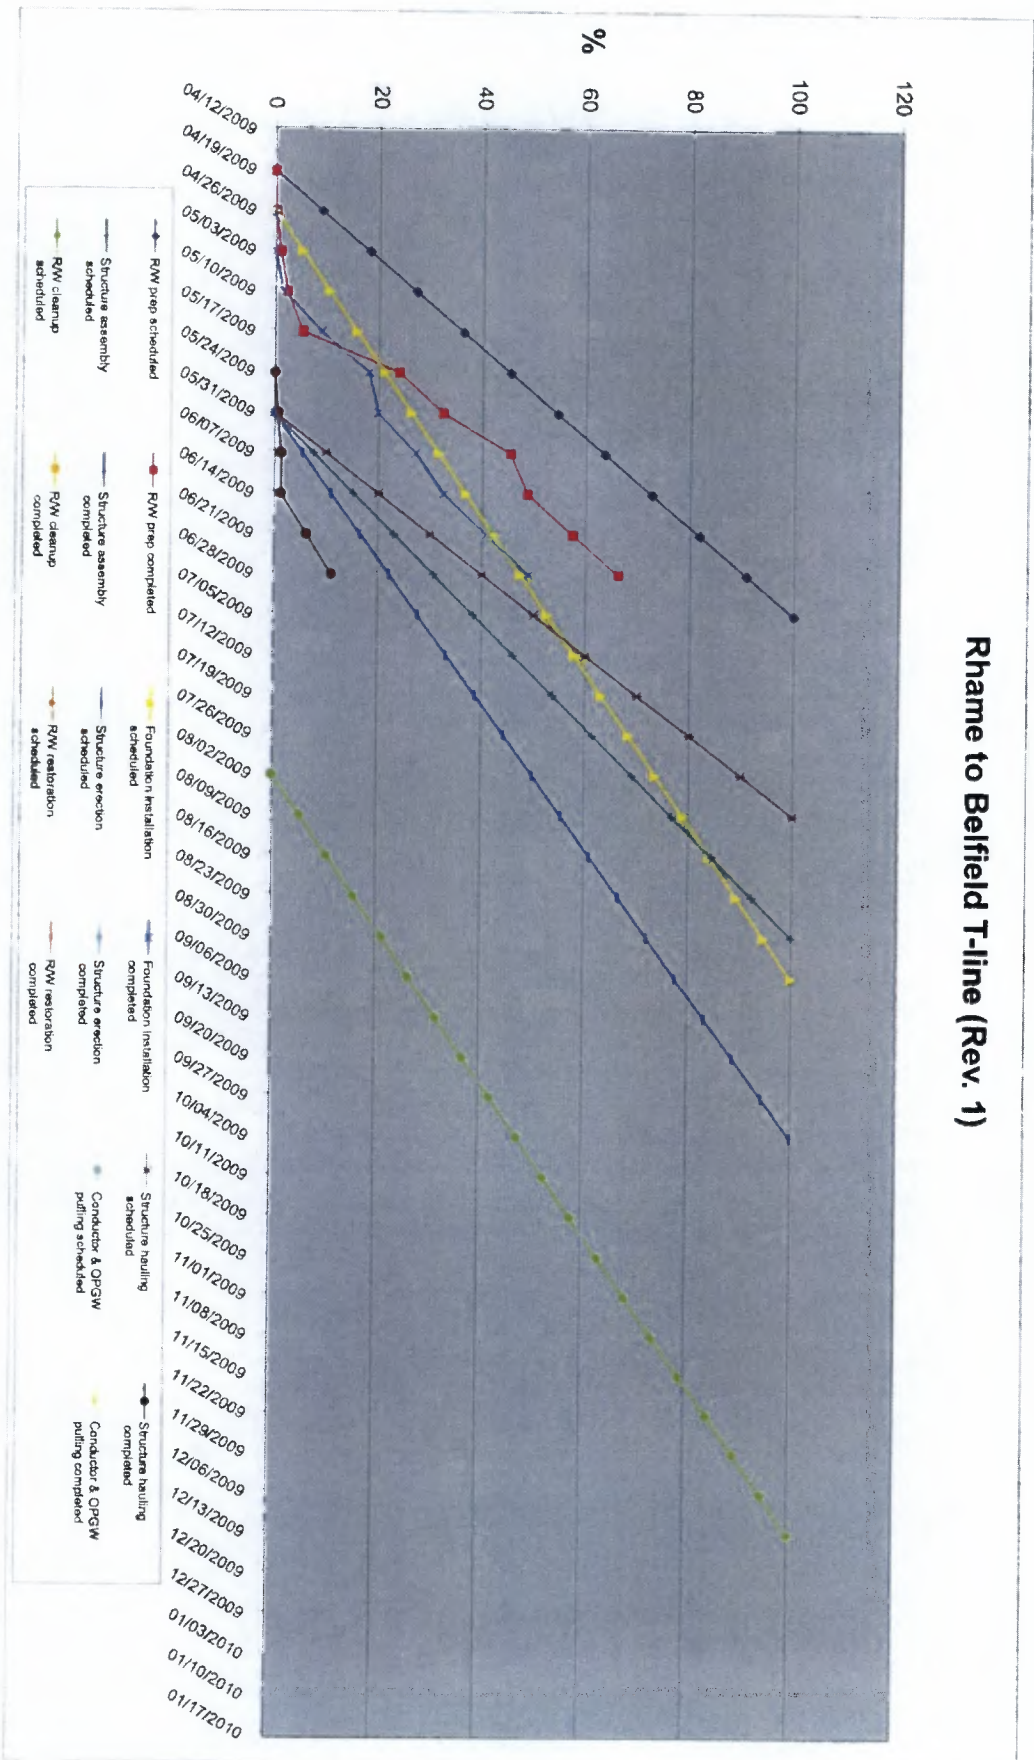

Rhame Sub & ER Access Grading

