


# Rhame to Belfield T-line (Rev. 1)

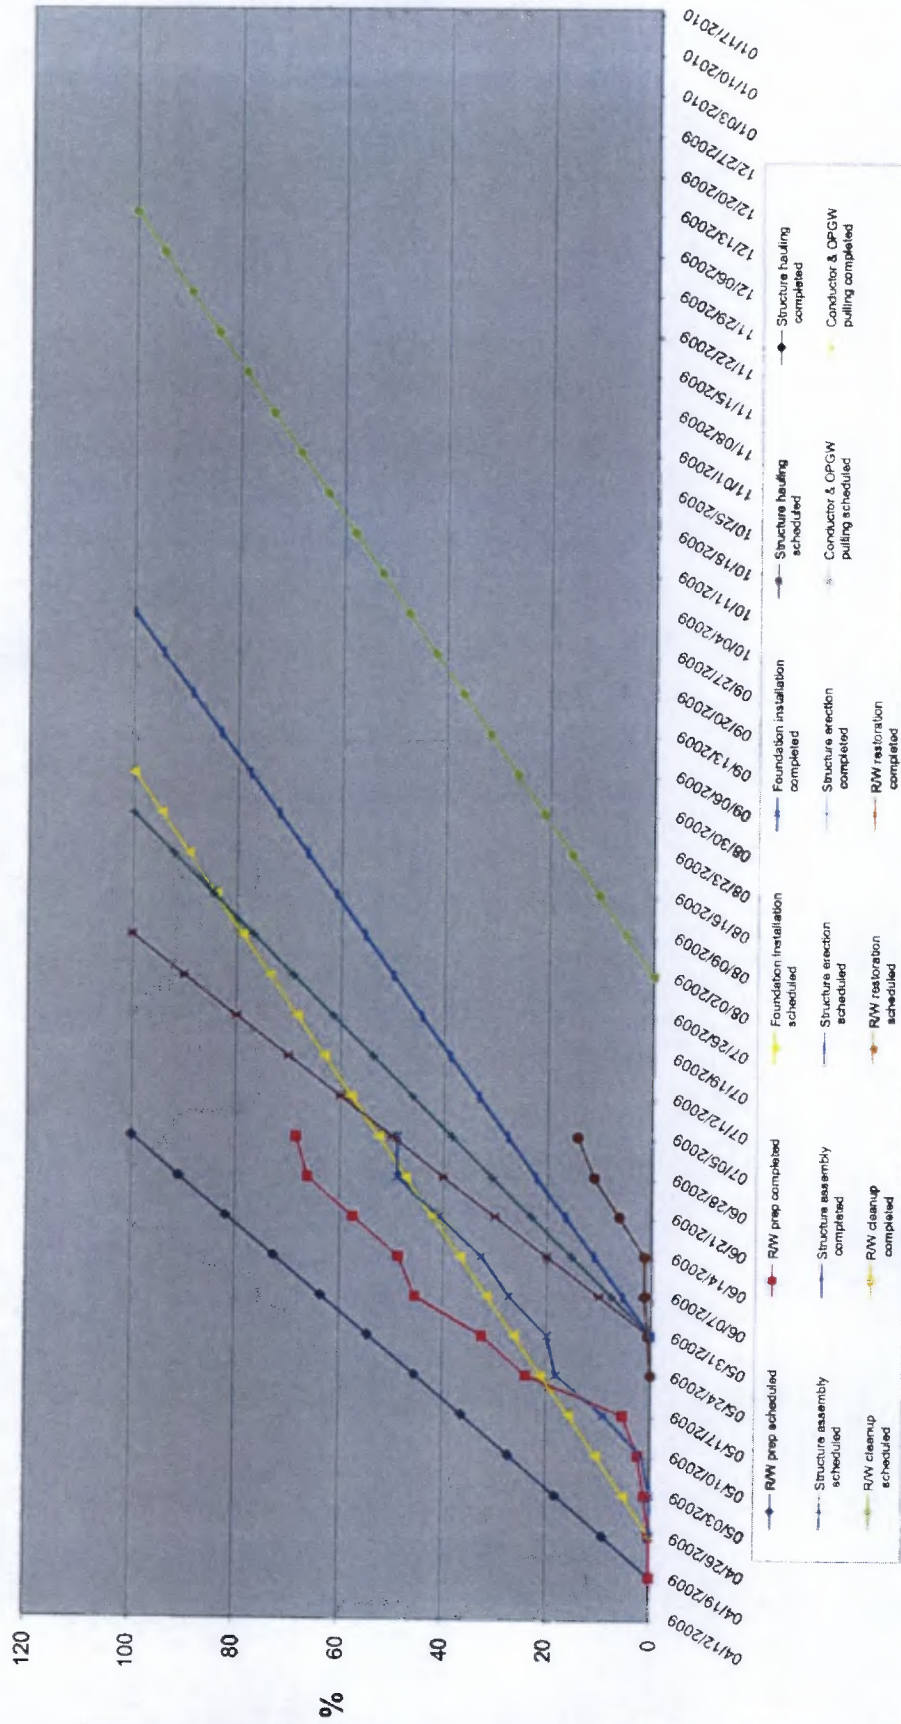

**BASIN ELECTRIC POWER COOPERATIVE**  
**Project: Rhame to Belfield T-line Contract**  
**Contractor: TESSCO**

**Weekly Progress Report**

Progress for the week ending : 07/04/2009

Manpower = 24

- Note:
- Completion the past week
  - Completion to date
  - 6 STRS Condemnation proceedings
  - X - indicates a foundation location

Str #1 @ Rhame and Str #524 @ Belfield

	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep	12	2.3	359	68.5
Foundation Inst'l. (55)	0	0.0	27	49.1
Structure hauling	17	3.2	75	14.3
Structure assembly		0.0		0.0
Structure erection		0.0		0.0
Conductor/OPGW installation		0.0		0.0
R/W cleanup		0.0		0.0
R/W restoration		0.0		0.0

