

BASIN ELECTRIC POWER COOPERATIVE
Project: Rhame to Belfield T-line Contract
Contractor: TESSCO

Weekly Progress Report



Progress for the week ending : 08/01/2009

Manpower = 37


- Note:
- Completion the past week
 - Completion to date
 - Condemnation proceedings
 - X - indicates a foundation location

Str.#1 @ Rhame and Str #524 @ Belfield

	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep	0	0.0	406	77.5
Foundation instll. (55)	7	12.7	52	94.5
Structure hauling	39	7.4	202	38.5
Structure assembly	40	7.6	170	32.4
Structure erection	37	7.1	62	11.8
Conductor/OPGW installation		0.0		0.0
R/W cleanup		0.0		0.0
R/W restoration		0.0		0.0

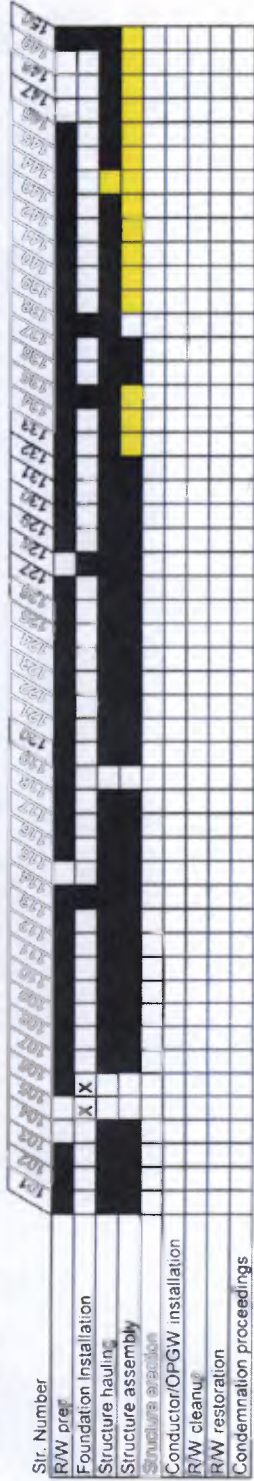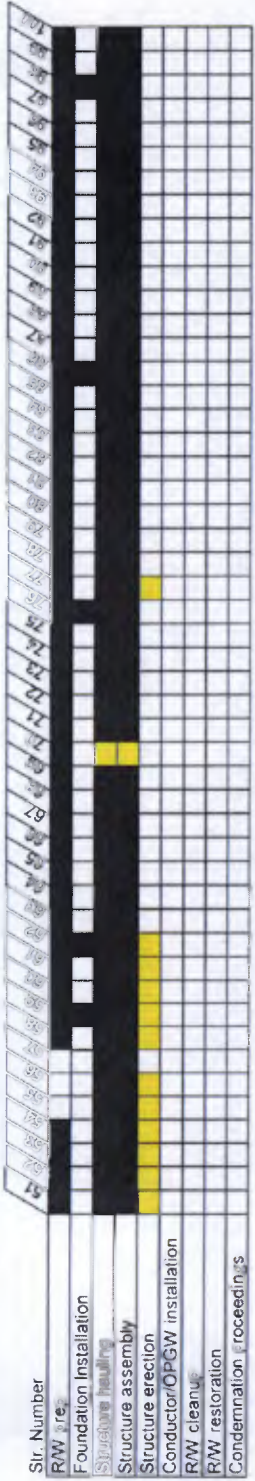

Rhame Substation Construction

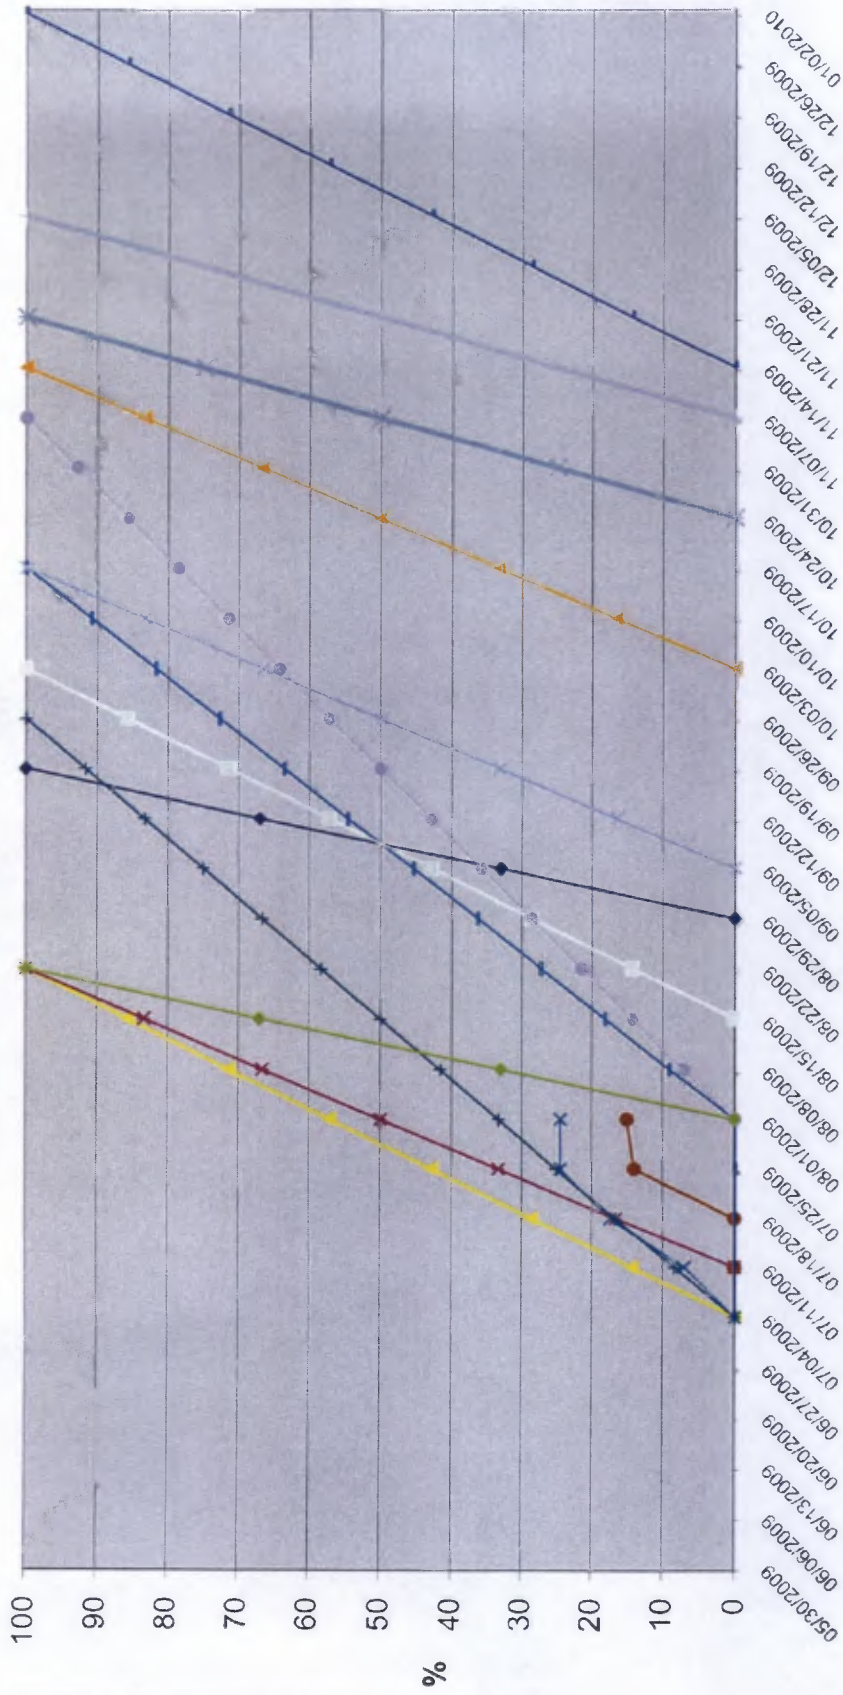

- Fencing Scheduled
- Control Building Scheduled
- Ground Grid Scheduled
- CB Equipment Scheduled
- Yard surfacing Scheduled
- Fencing Completed
- Control Building Completed
- Ground Grid Completed
- CB Equipment Completed
- Yard surfacing Completed
- Drilled Piers Scheduled
- Structure Erection Scheduled
- Yard Equipment Scheduled
- Cable Installation Scheduled
- Drilled Piers Completed
- Structure Erection Completed
- Yard Equipment Completed
- Cable Installation Completed
- Formed Concrete Scheduled
- Trench & Conduit Scheduled
- Buswork Scheduled
- Suprv & Comm Scheduled
- Formed Concrete Completed
- Trench & Conduit Completed
- Buswork Completed
- Suprv & Comm Completed
