



BASIN ELECTRIC POWER COOPERATIVE  
 Project: Rhame to Belfield T-line Contract  
 Contractor: TESCO



**Weekly Progress Report**

Progress for the week ending : 08/22/2009

Manpower = 56

Note:  
 Completion the past week  
 Completion to date  
 X - indicates a foundation location  
 Str.#1 @ Rhame and Str #524 @ Belfield

	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep	73	13.9	483	92.2
Foundation Instl. (55)	0	0.0	53	96.4
Structure hauling	30	5.7	291	55.5
Structure assembly	39	7.4	255	48.7
Structure erection	29	5.5	135	25.8
Conductor/OPGW installation	17	3.2	17	3.2
R/W cleanup		0.0		0.0
R/W restoration		0.0		0.0

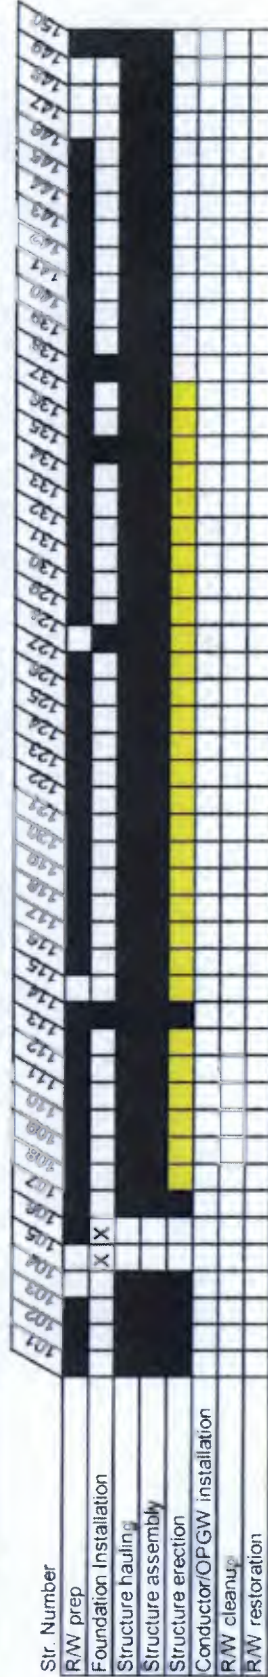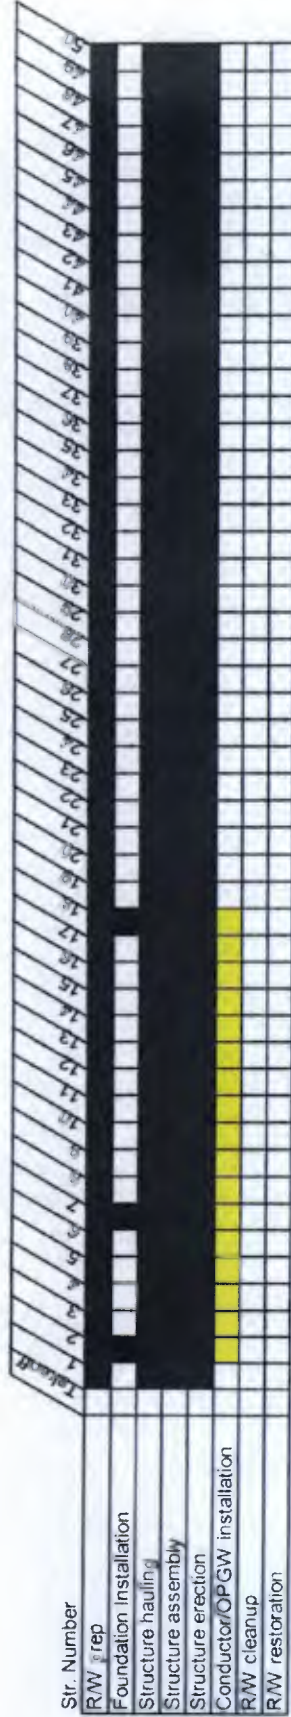



# Rhame to Belfield T-line (Rev. 1)

