

BASIN ELECTRIC POWER COOPERATIVE
Project: Rhame to Belfield T-line Contract
Contractor: TESSCO


Weekly Progress Report

Progress for the week ending : 09/12/2009

Manpower = 48

	Weekly total	Weekly %	Cumulative total	Cumulative %
RW Prep	5	1.0	488	93.1
Foundation Instl. (55)	0	0.0	55	100.0
Structure hauling	0	0.0	335	63.9
Structure assembly	2	0.4	291	55.5
Structure erection	24	4.6	209	39.9
Conductor/OPGW installation	34	6.5	109	20.8
RW cleanup	0	0.0	0.0	0.0
RW restoration	0	0.0	0.0	0.0

Note:
 Completion the past week
 Completion to date
 X - indicates a foundation location
 Str.#1 @ Rhame and Str #524 @ Belfield

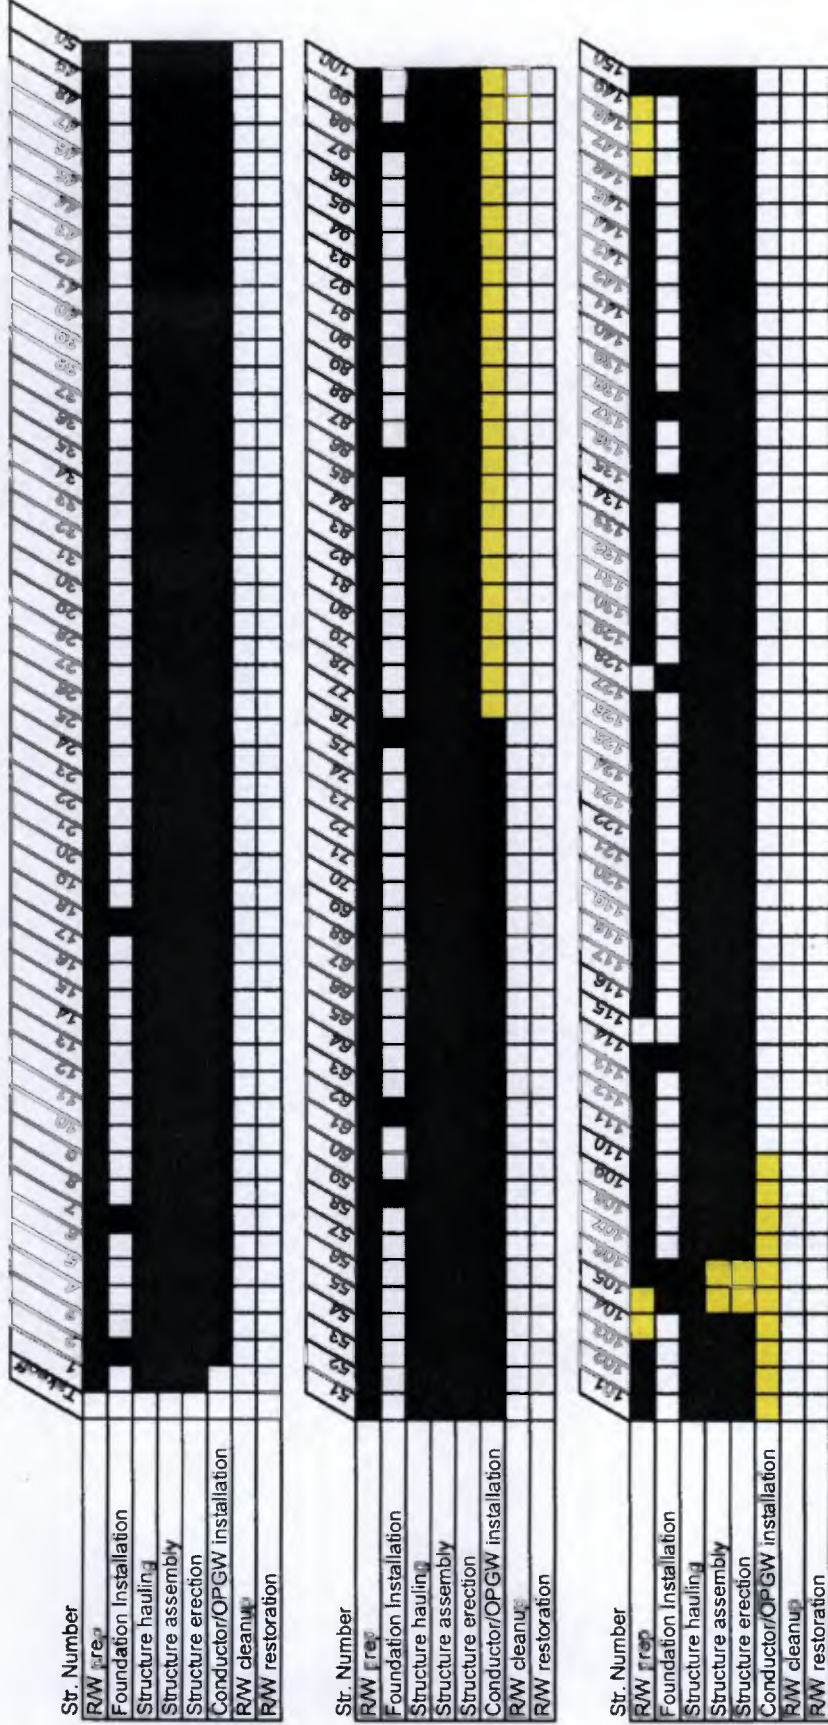

Rhame to Belfield T-line (Rev. 1)

