

**BASIN ELECTRIC POWER COOPERATIVE**  
**Project: Rhame to Belfield T-line Contract**  
**Contractor: TESSCO**


**Weekly Progress Report**

Progress for the week ending : 09/26/2009

Manpower = 48

- Note:
- Completion the past week
  - Completion to date
  - X - indicates a foundation location
  - Str.#1 @ Rhame and Str #524 @ Belfield


	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep		0.0	489	93.3
Foundation Inst'l. (55)		0.0	55	100.0
Structure hauling	55	10.5	435	83.0
Structure assembly	22	4.2	320	61.1
Structure erection	43	8.2	290	55.3
Conductor/OPGW installation	25	4.8	163	31.1
R/W cleanup		0.0		0.0
R/W restoration		0.0		0.0

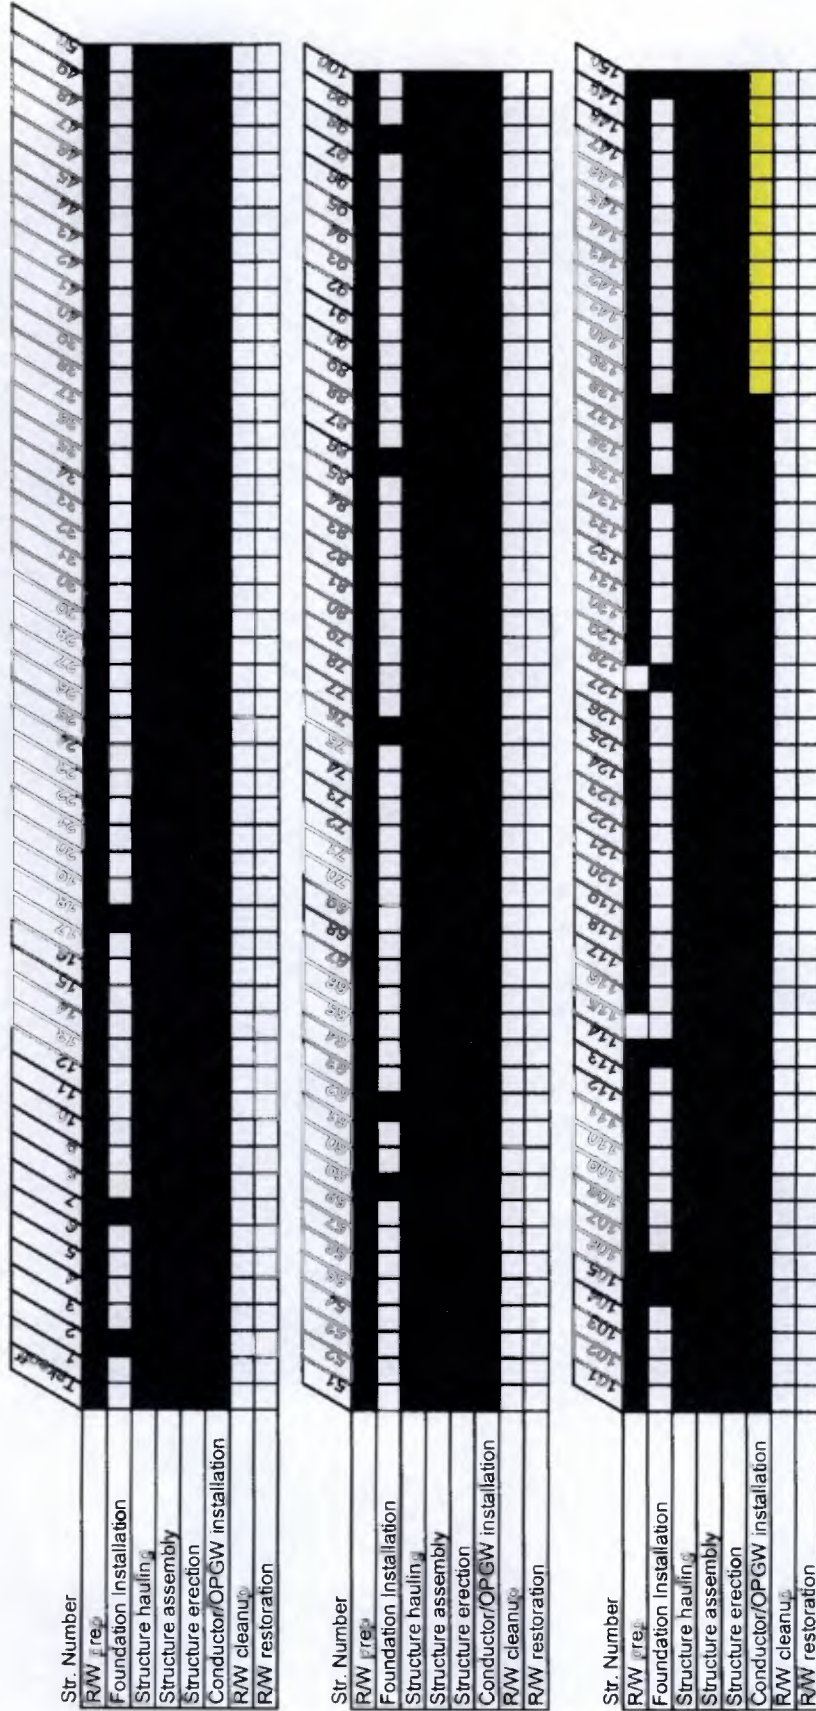





# Rhame to Belfield T-line (Rev. 1)

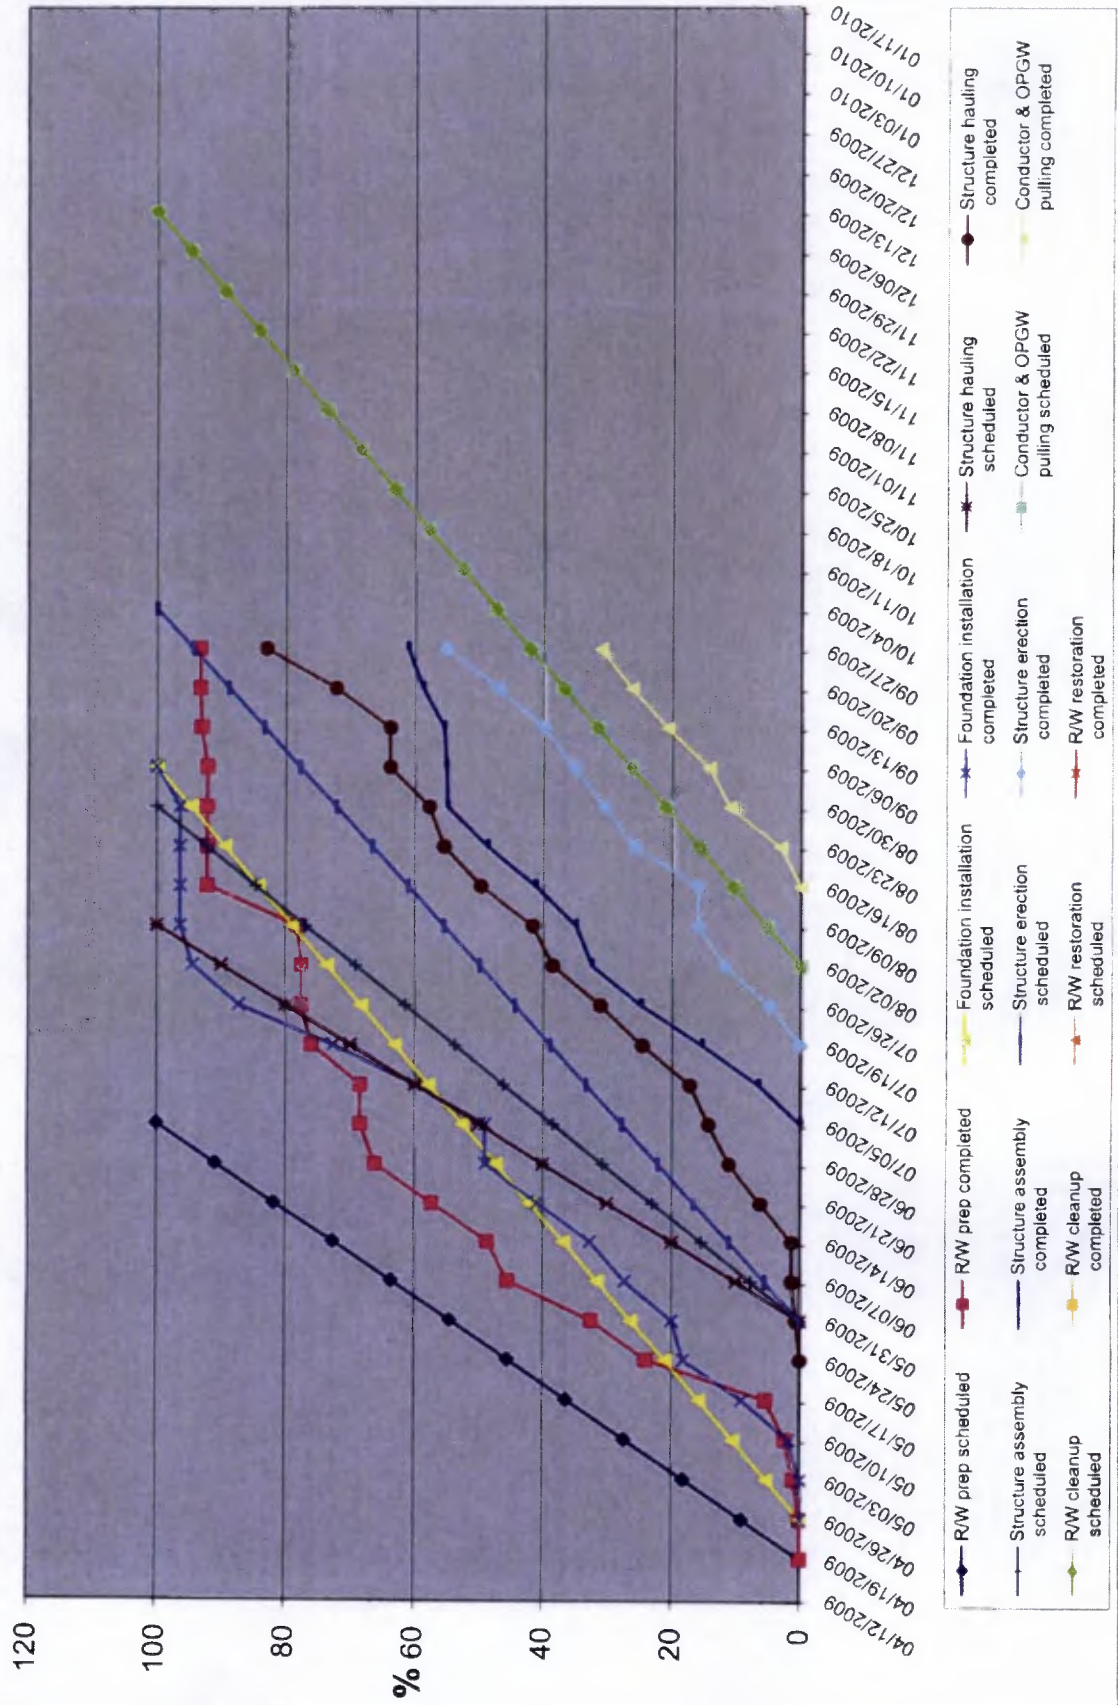

# Rhame Substation Construction

