

BASIN ELECTRIC POWER COOPERATIVE
Project: Rhame to Belfield T-line Contract
Contractor: TESSCO

Weekly Progress Report

Progress for the week ending : 11/14/2009


Manpower = 43

Note:
 Completion the past week
 Completion to date
 X - indicates a foundation location
 Str.#1 @ Rhame and Str #524 @ Belfield


	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep		0.0	523	100.0
Foundation Inst'l. (55)		0.0	55	100.0
Structure hauling		0.0	524	100.0
Structure assembly		0.0	523	99.8
Structure erection	50	9.5	512	97.7
Conductor/OPGW installation	60	11.5	440	84.0
R/W cleanup	9	1.7	159	30.3
R/W restoration		0.0		0.0

Str. Number	Foundation Installation	Structure hauling	Structure assembly	Structure erection	Conductor/OPGW installation	R/W cleanup	R/W restoration
51							
52							
53							
54							
55							
56							
57							
58							
59							
60							
61							
62							
63							
64							
65							
66							
67							
68							
69							
70							
71							
72							
73							
74							
75							
76							
77							
78							
79							
80							
81							
82							
83							
84							
85							
86							
87							
88							
89							
90							
91							
92							
93							
94							
95							
96							
97							
98							
99							
100							
101							
102							
103							
104							
105							
106							
107							
108							
109							
110							
111							
112							
113							
114							
115							
116							
117							
118							
119							
120							
121							
122							
123							
124							
125							
126							
127							
128							
129							
130							
131							
132							
133							
134							
135							
136							
137							
138							
139							
140							
141							
142							
143							
144							
145							
146							
147							
148							
149							
150							

Rhame to Belfield T-line (Rev. 1)

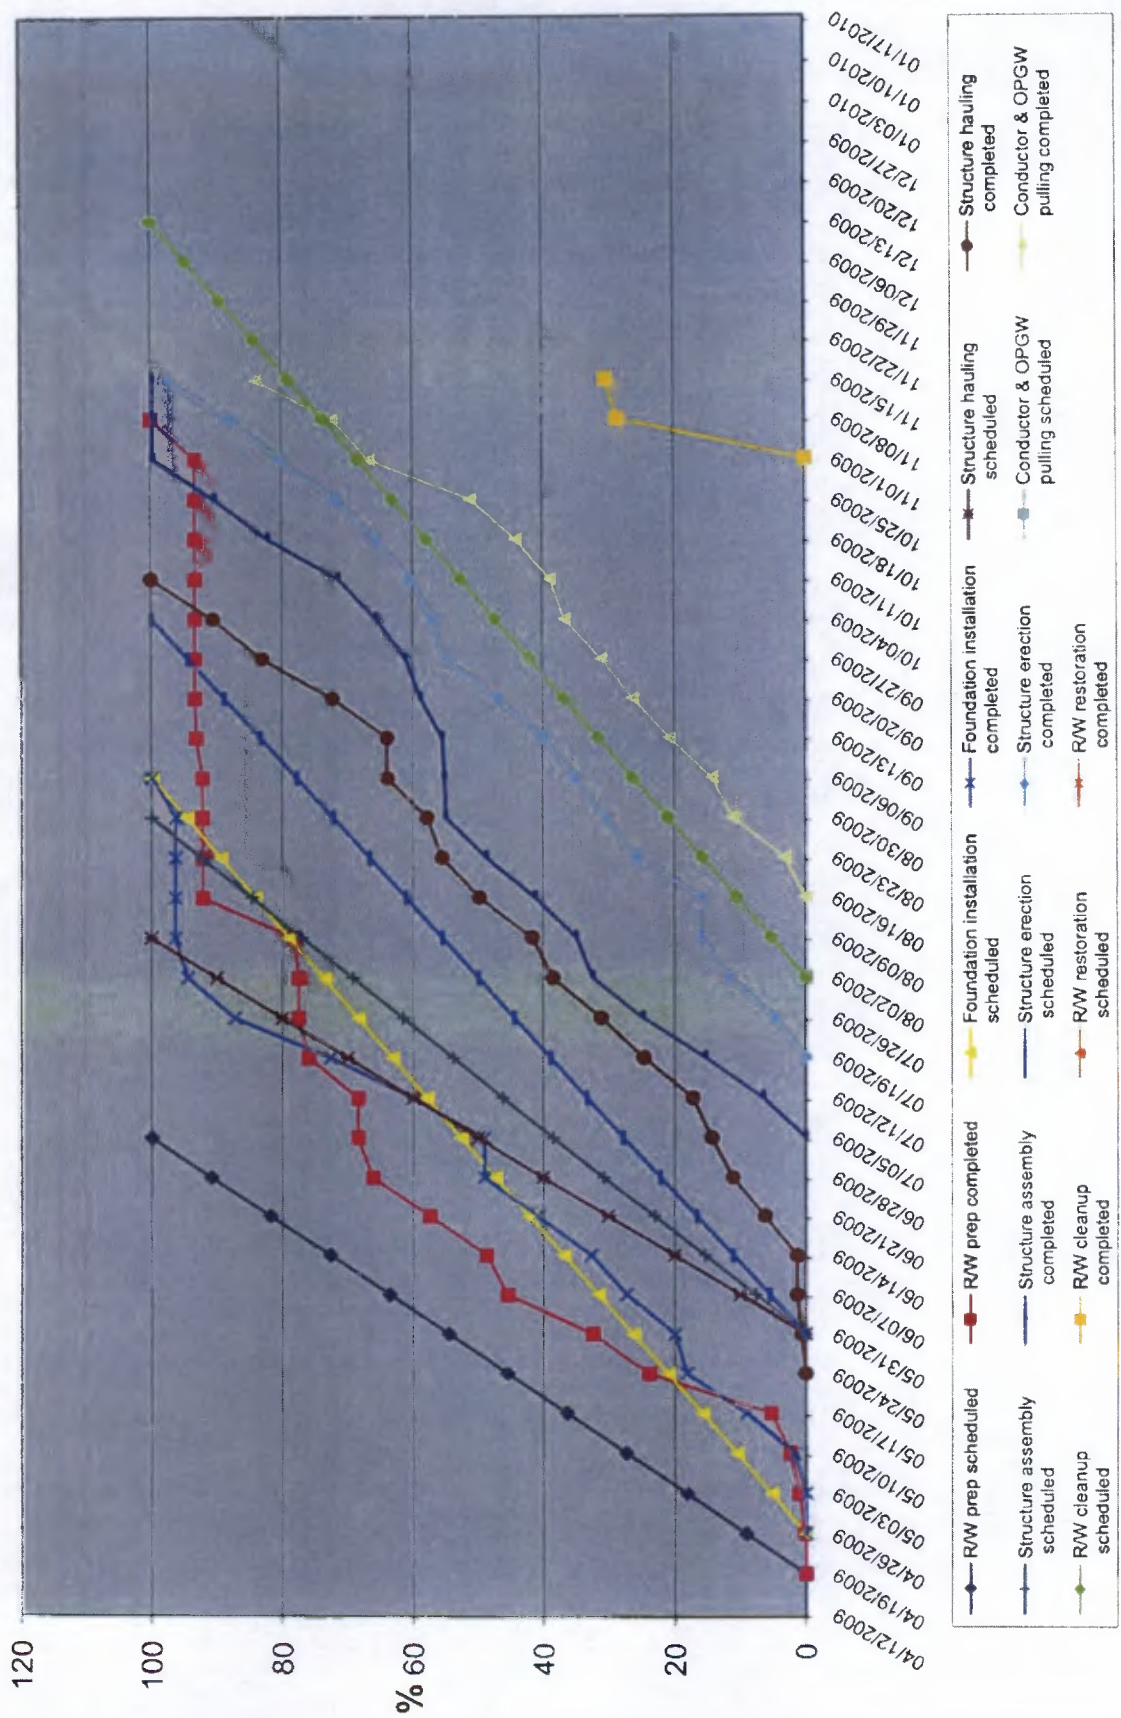

Rhame Substation Construction Rev. #1

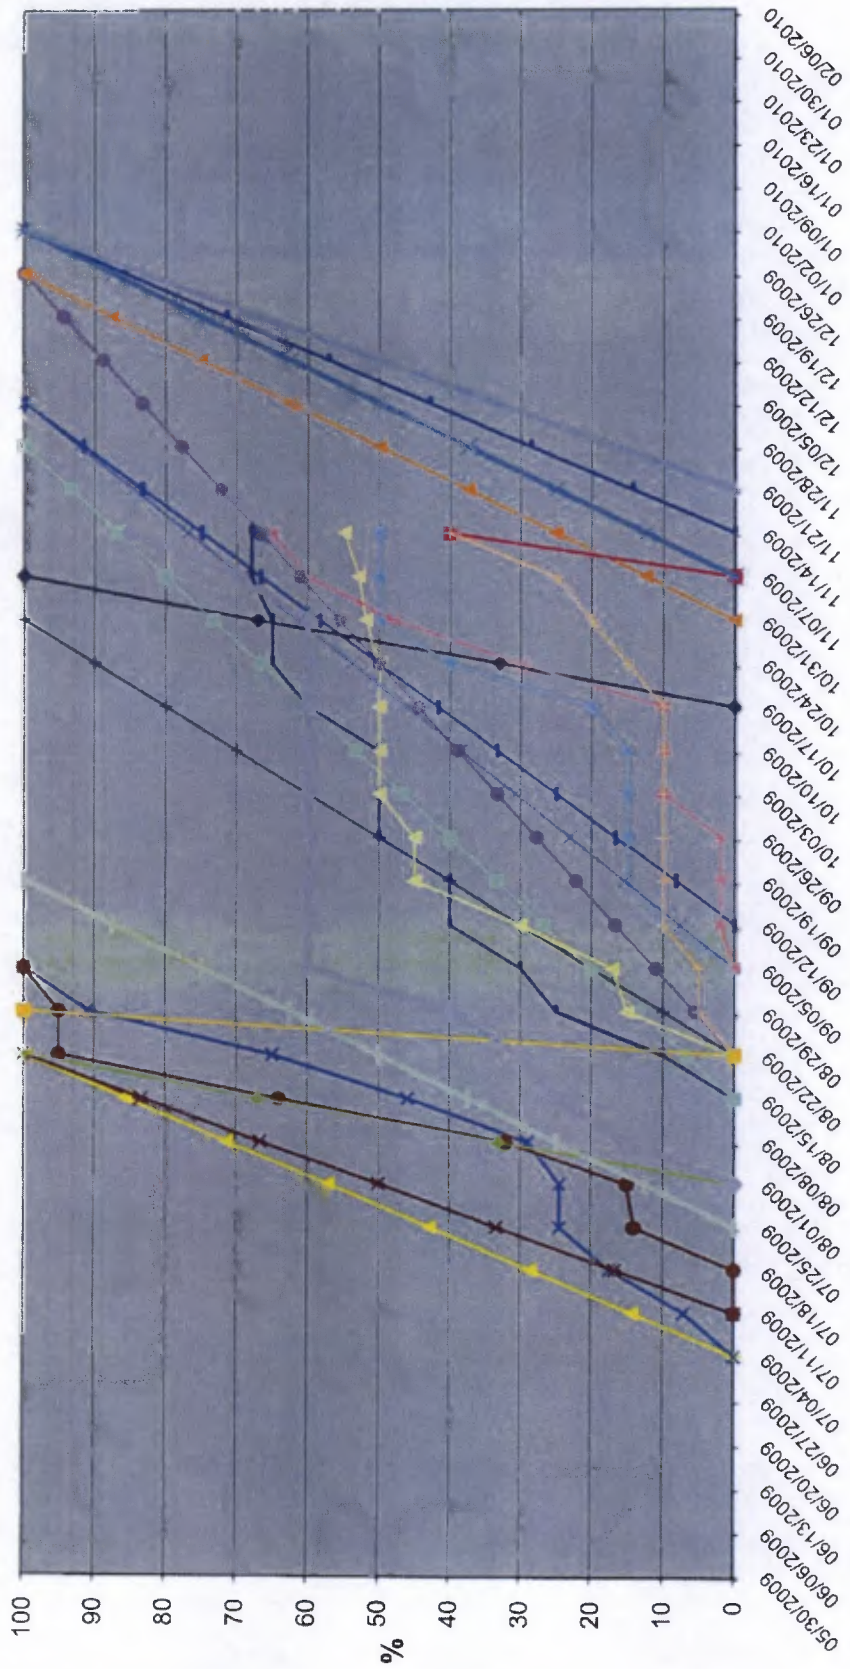

Task	Status
Fencing	Scheduled
Control Building	Scheduled
Ground Grid	Scheduled
CB Equipment	Scheduled
Yard surfacing	Scheduled
Drilled Piers	Scheduled
Structure Erection	Scheduled
Yard Equipment	Scheduled
Cable Installation	Scheduled
Microwave installation	Scheduled
Formed Concrete	Scheduled
Trench & Conduit	Scheduled
Buswork	Scheduled
Suprv & Comm	Scheduled
Fencing	Completed
Control Building	Completed
Ground Grid	Completed
CB Equipment	Completed
Yard surfacing	Completed
Drilled Piers	Completed
Structure Erection	Completed
Yard Equipment	Completed
Cable Installation	Completed
Microwave installation	Completed
Formed Concrete	Completed
Trench & Conduit	Completed
Buswork	Completed
Suprv & Comm	Completed
