

**BASIN ELECTRIC POWER COOPERATIVE**  
**Project: Rhame to Belfield T-line Contract**  
**Contractor: TESSCO**

**Weekly Progress Report**

Progress for the week ending : 11/21/2009

Manpower = 43

Note:  
 Completion the past week

Completion to date

X - indicates a foundation location

Str.#1 @ Rhame and Str #524 @ Belfield


	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep		0.0	523	100.0
Foundation Inst'l. (55)		0.0	55	100.0
Structure hauling		0.0	524	100.0
Structure assembly	1	0.2	524	100.0
Structure erection	12	2.3	524	100.0
Conductor/OPGW installation	27	5.2	467	89.1
R/W cleanup	41	7.8	200	38.2
R/W restoration		0.0		0.0

Str. Number	R/W Prep	Foundation Installation	Structure hauling	Structure assembly	Structure erection	Conductor/OPGW installation	R/W cleanup	R/W restoration
51								
52								
53								
54								
55								
56								
57								
58								
59								
60								
61								
62								
63								
64								
65								
66								
67								
68								
69								
70								
71								
72								
73								
74								
75								
76								
77								
78								
79								
80								
81								
82								
83								
84								
85								
86								
87								
88								
89								
90								
91								
92								
93								
94								
95								
96								
97								
98								
99								
100								
101								
102								
103								
104								
105								
106								
107								
108								
109								
110								
111								
112								
113								
114								
115								
116								
117								
118								
119								
120								
121								
122								
123								
124								
125								
126								
127								
128								
129								
130								
131								
132								
133								
134								
135								
136								
137								
138								
139								
140								
141								
142								
143								
144								
145								
146								
147								
148								
149								
150								






# Rhame to Belfield T-line (Rev. 1)

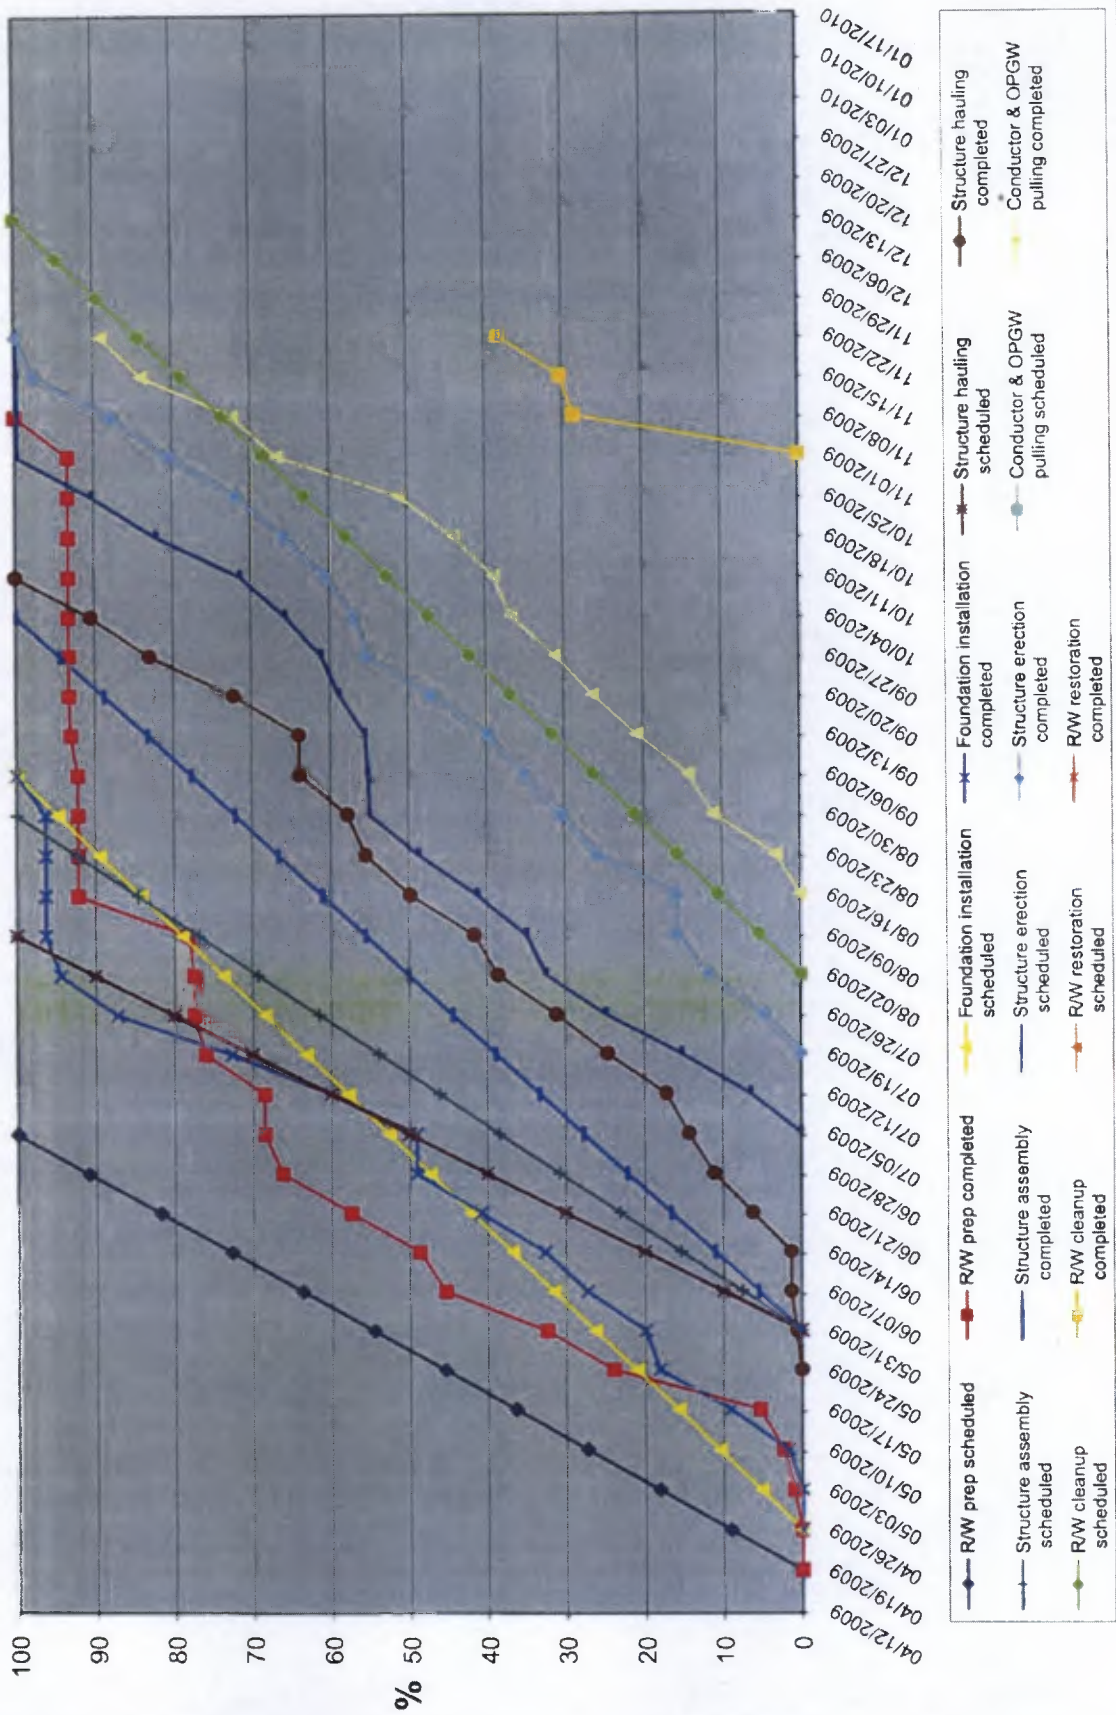

# Rhame Substation Construction Rev. #2

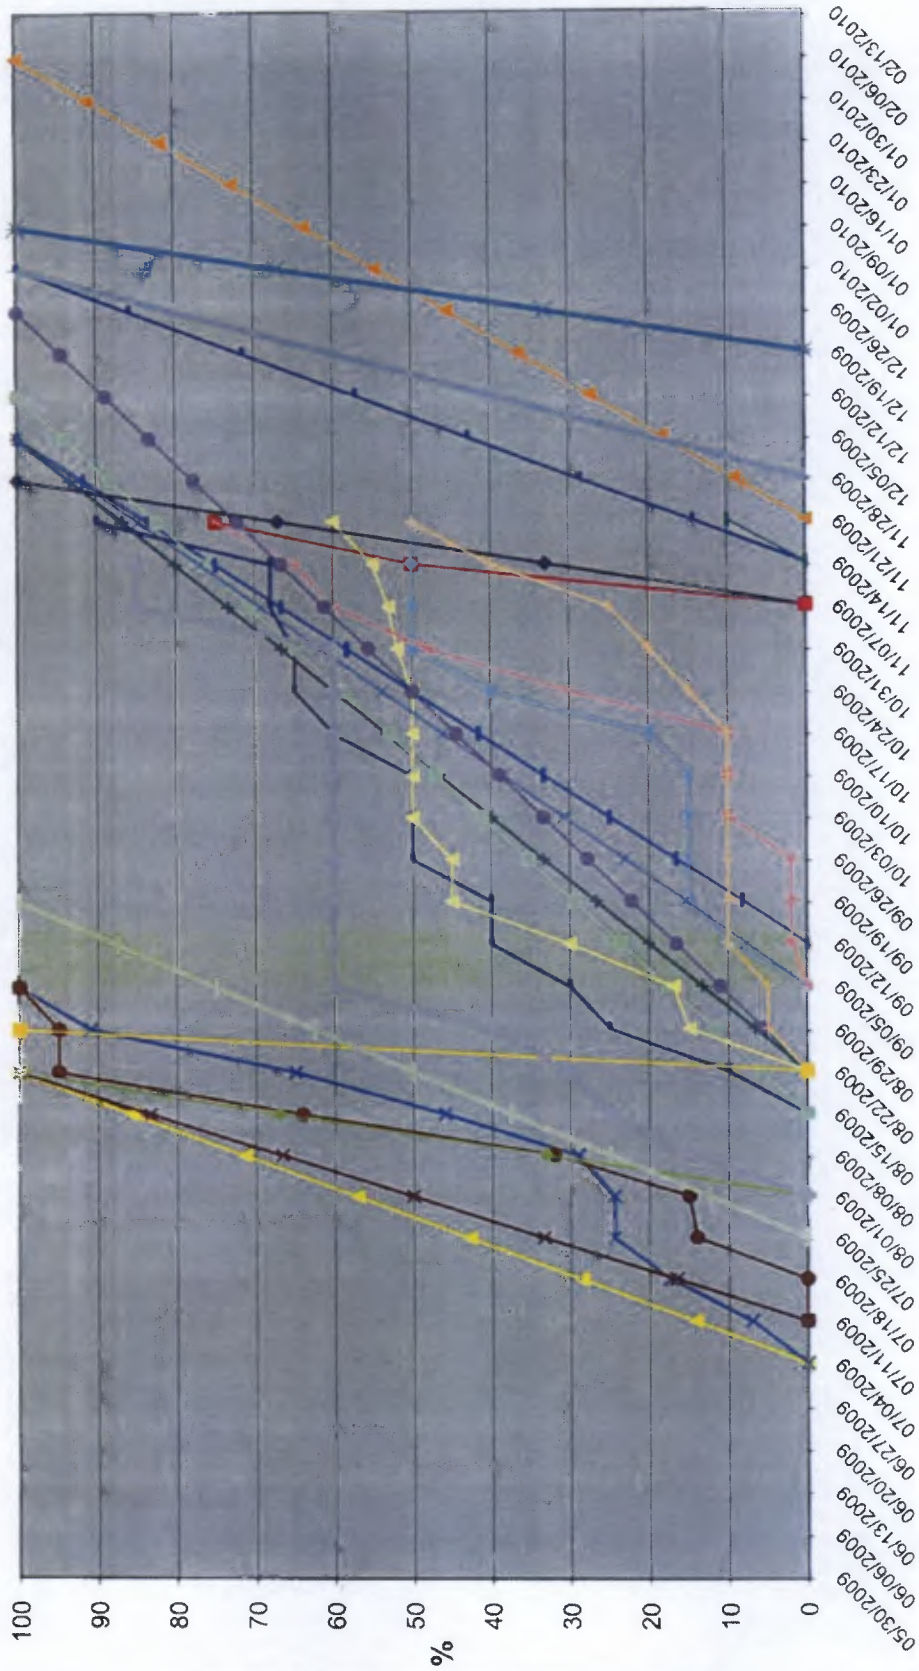

- Fencing Completed
- Fencing Scheduled
- Control Building Completed
- Control Building Scheduled
- Ground Grid Completed
- Ground Grid Scheduled
- CB Equipment Completed
- CB Equipment Scheduled
- Yard surfacing Completed
- Yard surfacing Scheduled
- Fencing Completed
- Control Building Completed
- Ground Grid Completed
- CB Equipment Completed
- Yard surfacing Completed
- Drilled Piers Scheduled
- Structure Erection Scheduled
- Yard Equipment Scheduled
- Cable installation Scheduled
- Microwave installation Scheduled
- Drilled Piers Completed
- Structure Erection Completed
- Yard Equipment Completed
- Cable installation Completed
- Microwave installation Completed
- Formed Concrete Scheduled
- Trench & Conduit Scheduled
- Buswork Scheduled
- Suprv & Comm Scheduled
- Formed Concrete Completed
- Trench & Conduit Completed
- Buswork Completed
- Suprv & Comm Completed
