


Rhame Substation Construction Rev. #2

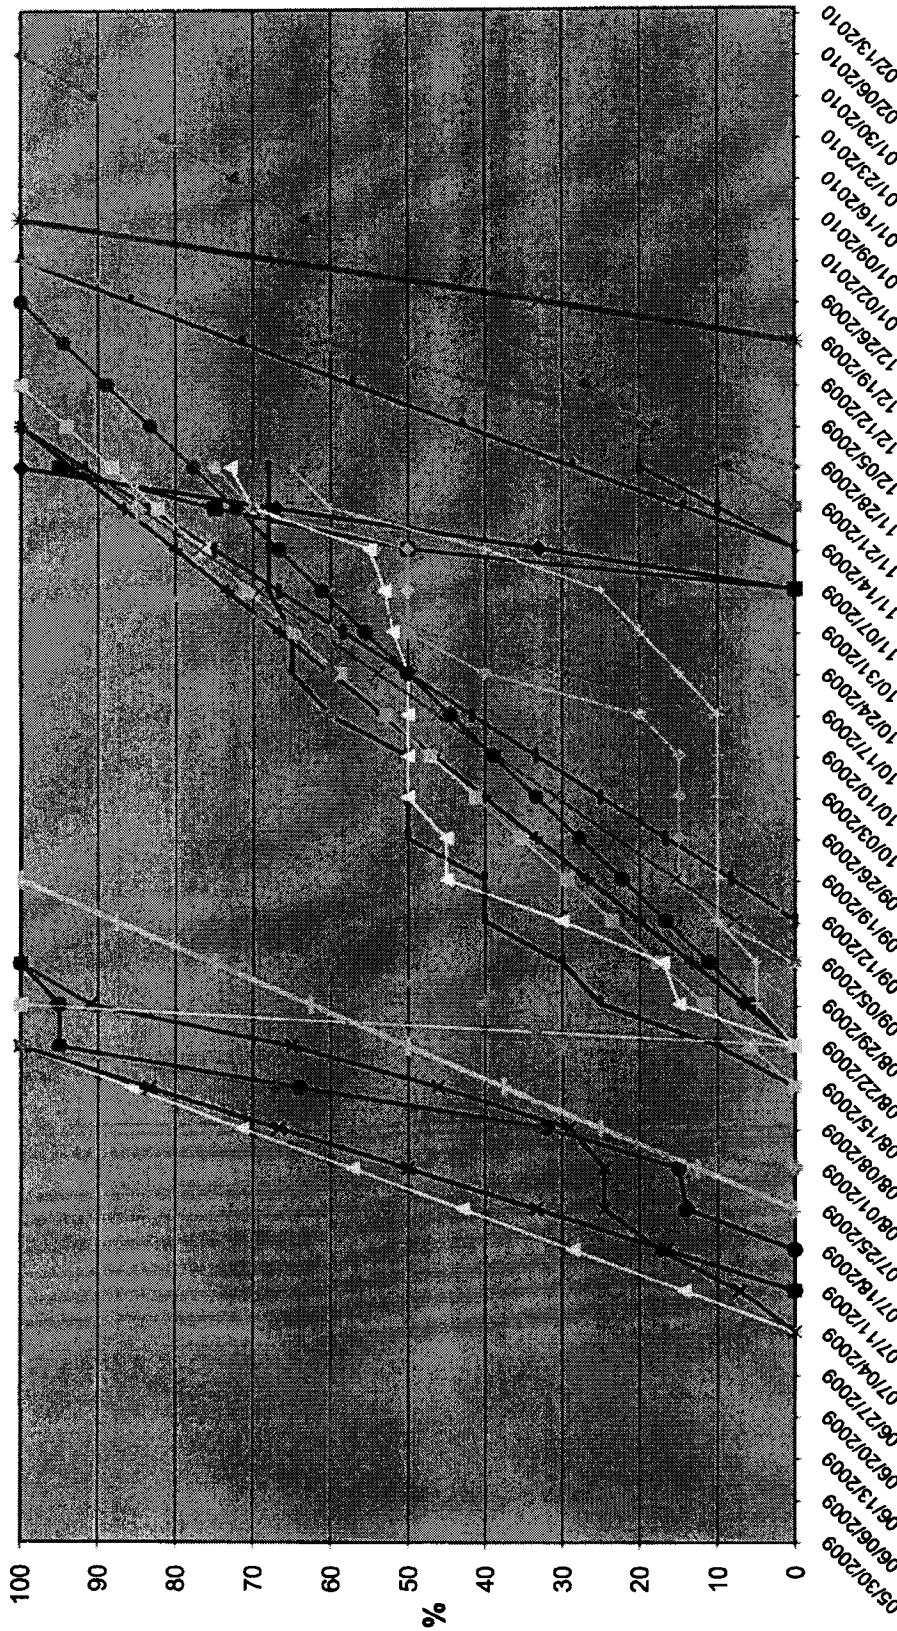

Task	Status
Fencing	Scheduled
Control Building	Scheduled
Ground Grid	Scheduled
CB Equipment	Scheduled
Yard surfacing	Scheduled
Fencing	Completed
Control Building	Completed
Ground Grid	Completed
CB Equipment	Completed
Yard surfacing	Completed
Drilled Piers	Scheduled
Structure Erection	Scheduled
Yard Equipment	Scheduled
Cable Installation	Scheduled
Microwave Installation	Scheduled
Drilled Piers	Completed
Structure Erection	Completed
Yard Equipment	Completed
Cable Installation	Completed
Microwave Installation	Completed
Formed Concrete	Scheduled
Trench & Conduit	Scheduled
Buswork	Scheduled
Suprv & Comm	Scheduled
Formed Concrete	Completed
Trench & Conduit	Completed
Buswork	Completed
Suprv & Comm	Completed
