

Hamre, John G.

From: Bauske, Shelly A.
Sent: Monday, December 21, 2009 10:34 AM
To: Hamre, John G.
Subject: FW: Rhame/Belfield weekly proress report 121909
Attachments: wr121909.pdf

From: Rick Mucha [mailto:RMucha@bepc.com]
Sent: Friday, December 18, 2009 1:15 PM
To: Alan Burgard; Cory Bauer; Dave Wulke (dwulke@tesscousa.com); Deborah Levchak; Don Stone (dstone@tesscousa.com); Duey Marthaller; Gary Bindert (addison3@q.com); Gary Stoddard; Harlan Fortin; Lein, Jerry R.; Joseph Volk; Kevin Solie; Mark Nygard; Mark Winn; Megan Milbradt; Mike Murray; Pius Fischer; -Info-Public Service Commission; Shad Erdmann; Shane Vasbinder; Steve Hartnell (shartnell@tesscousa.com)
Subject: Rhame/Belfield weekly proress report 121909

Progress report attached.


The transmission line is complete with the exception of a few structure punch list items which will be addressed next week and a foundation repair is to be complete the week of Jan 4th.

All crews will be out for the holidays beginning Dec 23 thru Jan 4.

The next progress report will address the remaining substation construction on 1/9/10. The T-line restoration will be scheduled in the spring.

RJM

Rhame Substation Construction Rev. #2

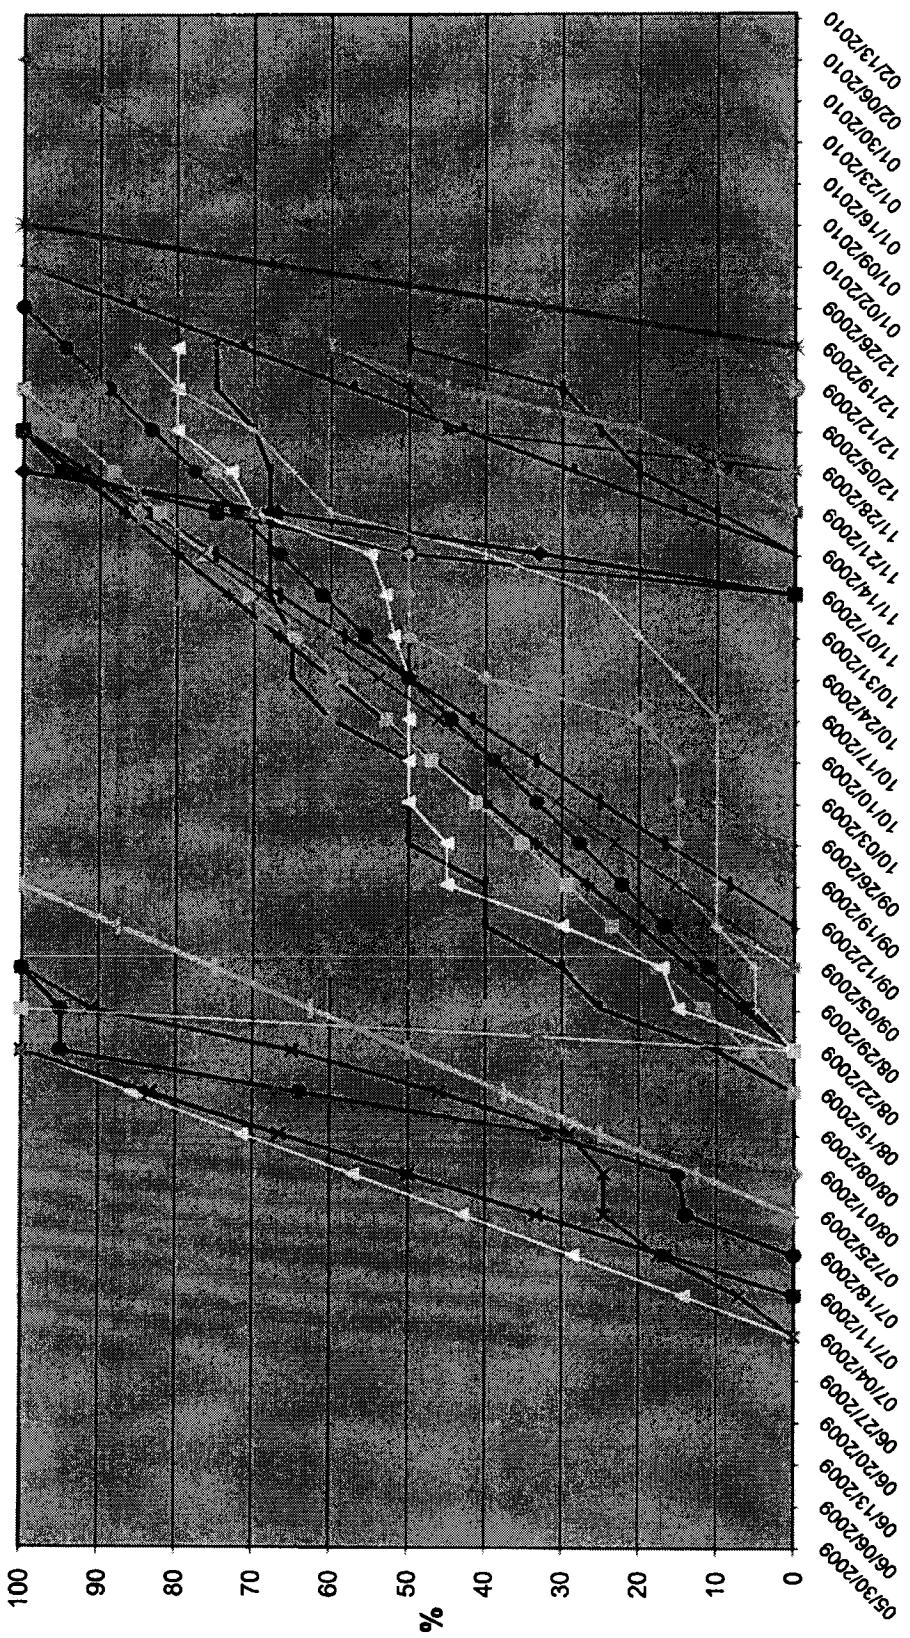

- Completed Fencing
- Scheduled Control Building
- Completed Ground Grid
- Scheduled CB Equipment
- Completed Yard surfacing
- Completed Formed Concrete
- Scheduled Trench & Conduit
- Completed Buswork
- Scheduled Suprv & Comm
- Completed Drilled Piers
- Scheduled Structure Erection
- Completed Yard Equipment
- Scheduled Cable Installation
- Completed Microwave Installation
- Completed Formed Concrete
- Scheduled Trench & Conduit
- Completed Buswork
- Scheduled Suprv & Comm
- Completed Drilled Piers
- Scheduled Structure Erection
- Completed Yard Equipment
- Scheduled Cable Installation
- Completed Microwave Installation
- Completed Fencing
- Scheduled Control Building
- Completed Ground Grid
- Scheduled CB Equipment
- Completed Yard surfacing
- Completed Formed Concrete
- Scheduled Trench & Conduit
- Completed Buswork
- Scheduled Suprv & Comm
- Completed Drilled Piers
- Scheduled Structure Erection
- Completed Yard Equipment
- Scheduled Cable Installation
- Completed Microwave Installation
