

Hamre, John G.


From: Bauske, Shelly A.
Sent: Wednesday, January 13, 2010 8:40 AM
To: Hamre, John G.
Subject: FW: Rhame/Belfield weekly progress report 010910
Attachments: wr010910.pdf

From: Rick Mucha [mailto:RMucha@bepc.com]
Sent: Wednesday, January 13, 2010 7:41 AM
To: Alan Burgard; Cory Bauer; Dave Wulke (dwulke@tesscousa.com); Deborah Levchak; Don Stone (dstone@tesscousa.com); Duey Marthaller; Gary Bindert (addison3@q.com); Gary Stoddard; Harlan Fortin; Lein, Jerry R.; Joseph Volk; Kevin Solie; Mark Nygard; Mark Winn; Megan Milbradt; Mike Murray; Pius Fischer; -Info-Public Service Commission; Shad Erdmann; Shane Vasbinder; Steve Hartnell (shartnell@tesscousa.com)
Subject: Rhame/Belfield weekly progress report 010910

Progress report attached.

RJM

Rhame Substation Construction Rev. #2

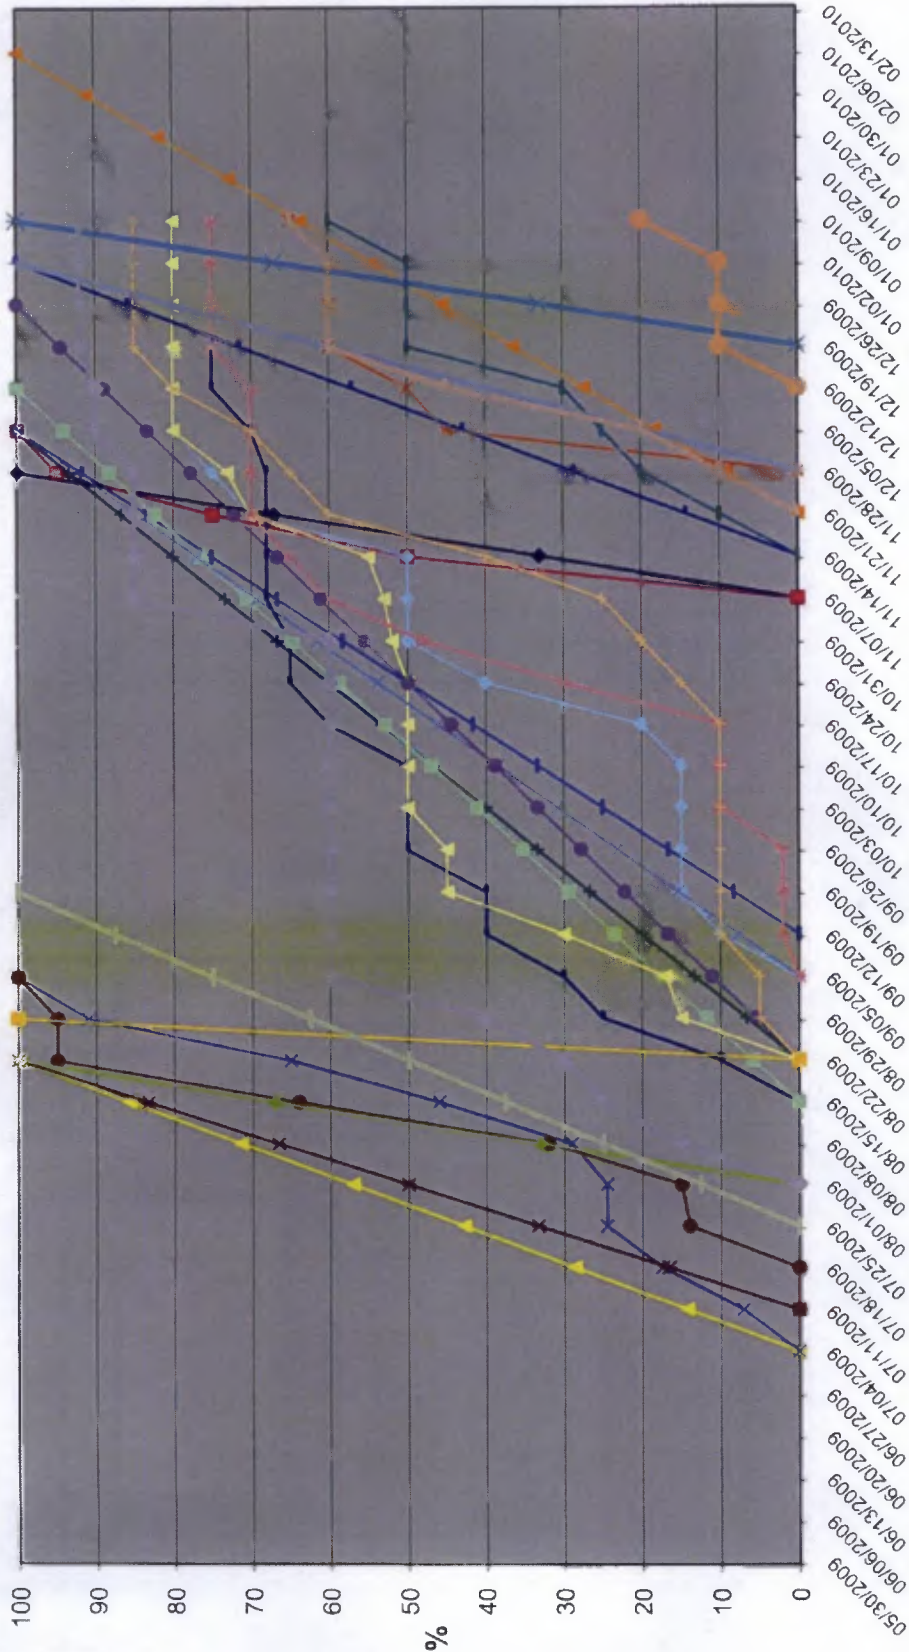

- | | | | |
|--------------------|--------------------|--------------------------|--------------------|
| ● Fencing | ● Formed Concrete | ● Drilled Piers | ● Formed Concrete |
| ● Scheduled | ● Completed | ● Completed | ● Scheduled |
| ● Control Building | ● Trench & Conduit | ● Structure Erection | ● Trench & Conduit |
| ● Scheduled | ● Completed | ● Scheduled | ● Scheduled |
| ● Ground Grid | ● Buswork | ● Yard Equipment | ● Buswork |
| ● Completed | ● Completed | ● Completed | ● Completed |
| ● CB Equipment | ● Suprv & Comm | ● Cable Installation | ● Suprv & Comm |
| ● Scheduled | ● Scheduled | ● Completed | ● Scheduled |
| ● Yard surfacing | ● Scheduled | ● Microwave installation | ● Scheduled |
| ● Completed | ● Completed | ● Completed | ● Completed |
