



Weekly Progress Report

Progress for the week ending : 05/01/2010

Manpower = 5

Note:
 Completion the past week 
 Completion to date 
 X - indicates a foundation location
 Str #1 @ Rhame and Str #524 @ Belfield

	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep	0.0	0.0	523	100.0
Foundation Inst'l. (55)	0.0	0.0	55	100.0
Structure hauling	0.0	0.0	524	100.0
Structure assembly	0.0	0.0	524	100.0
Structure erection	0.0	0.0	524	100.0
Conductor/OPGW installation	0.0	0.0	524	100.0
R/W cleanup	0.0	0.0	524	100.0
R/W restoration	114	21.8	114	21.8

Str. Number	Takeoff
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	
31	
32	
33	
34	
35	
36	
37	
38	
39	
40	
41	
42	
43	
44	
45	
46	
47	
48	
49	
50	

R/W Prep	
Foundation Installation	
Structure hauling	
Structure assembly	
Structure erection	
Conductor/OPGW installation	
R/W cleanup	
R/W restoration	

51	
52	
53	
54	
55	
56	
57	
58	
59	
60	
61	
62	
63	
64	
65	
66	
67	
68	
69	
70	
71	
72	
73	
74	
75	
76	
77	
78	
79	
80	
81	
82	
83	
84	
85	
86	
87	
88	
89	
90	
91	
92	
93	
94	
95	
96	
97	
98	
99	
100	


Str. Number	151
R/W prep	152
Foundation Installation	153
Structure hauling	154
Structure assembly	155
Structure erection	156
Conductor/OP GW installation	157
R/W cleanup	158
R/W restoration	159
Str. Number	160
R/W prep	161
Foundation Installation	162
Structure hauling	163
Structure assembly	164
Structure erection	165
Conductor/OP GW installation	166
R/W cleanup	167
R/W restoration	168
Str. Number	169
R/W prep	170
Foundation Installation	171
Structure hauling	172
Structure assembly	173
Structure erection	174
Conductor/OP GW installation	175
R/W cleanup	176
R/W restoration	177
Str. Number	178
R/W prep	179
Foundation Installation	180
Structure hauling	181
Structure assembly	182
Structure erection	183
Conductor/OP GW installation	184
R/W cleanup	185
R/W restoration	186
Str. Number	187
R/W prep	188
Foundation Installation	189
Structure hauling	190
Structure assembly	191
Structure erection	192
Conductor/OP GW installation	193
R/W cleanup	194
R/W restoration	195
Str. Number	196
R/W prep	197
Foundation Installation	198
Structure hauling	199
Structure assembly	200
Structure erection	201
Conductor/OP GW installation	202
R/W cleanup	203
R/W restoration	204

Str. Number	205
R/W prep	206
Foundation Installation	207
Structure hauling	208
Structure assembly	209
Structure erection	210
Conductor/OP GW installation	211
R/W cleanup	212
R/W restoration	213
Str. Number	214
R/W prep	215
Foundation Installation	216
Structure hauling	217
Structure assembly	218
Structure erection	219
Conductor/OP GW installation	220
R/W cleanup	221
R/W restoration	222
Str. Number	223
R/W prep	224
Foundation Installation	225
Structure hauling	226
Structure assembly	227
Structure erection	228
Conductor/OP GW installation	229
R/W cleanup	230
R/W restoration	231
Str. Number	232
R/W prep	233
Foundation Installation	234
Structure hauling	235
Structure assembly	236
Structure erection	237
Conductor/OP GW installation	238
R/W cleanup	239
R/W restoration	240
Str. Number	241
R/W prep	242
Foundation Installation	243
Structure hauling	244
Structure assembly	245
Structure erection	246
Conductor/OP GW installation	247
R/W cleanup	248
R/W restoration	249
Str. Number	250
R/W prep	251
Foundation Installation	252
Structure hauling	253
Structure assembly	254
Structure erection	255
Conductor/OP GW installation	256
R/W cleanup	257
R/W restoration	258

Str. Number	259
R/W prep	260
Foundation Installation	261
Structure hauling	262
Structure assembly	263
Structure erection	264
Conductor/OP GW installation	265
R/W cleanup	266
R/W restoration	267
Str. Number	268
R/W prep	269
Foundation Installation	270
Structure hauling	271
Structure assembly	272
Structure erection	273
Conductor/OP GW installation	274
R/W cleanup	275
R/W restoration	276
Str. Number	277
R/W prep	278
Foundation Installation	279
Structure hauling	280
Structure assembly	281
Structure erection	282
Conductor/OP GW installation	283
R/W cleanup	284
R/W restoration	285
Str. Number	286
R/W prep	287
Foundation Installation	288
Structure hauling	289
Structure assembly	290
Structure erection	291
Conductor/OP GW installation	292
R/W cleanup	293
R/W restoration	294
Str. Number	295
R/W prep	296
Foundation Installation	297
Structure hauling	298
Structure assembly	299
Structure erection	300
Conductor/OP GW installation	301
R/W cleanup	302
R/W restoration	303

Str. Number	304
R/W prep	305
Foundation Installation	306
Structure hauling	307
Structure assembly	308
Structure erection	309
Conductor/OP GW installation	310
R/W cleanup	311
R/W restoration	312
Str. Number	313
R/W prep	314
Foundation Installation	315
Structure hauling	316
Structure assembly	317
Structure erection	318
Conductor/OP GW installation	319
R/W cleanup	320
R/W restoration	321
Str. Number	322
R/W prep	323
Foundation Installation	324
Structure hauling	325
Structure assembly	326
Structure erection	327
Conductor/OP GW installation	328
R/W cleanup	329
R/W restoration	330
Str. Number	331
R/W prep	332
Foundation Installation	333
Structure hauling	334
Structure assembly	335
Structure erection	336
Conductor/OP GW installation	337
R/W cleanup	338
R/W restoration	339
Str. Number	340
R/W prep	341
Foundation Installation	342
Structure hauling	343
Structure assembly	344
Structure erection	345
Conductor/OP GW installation	346
R/W cleanup	347
R/W restoration	348
Str. Number	349
R/W prep	350
Foundation Installation	351
Structure hauling	352
Structure assembly	353
Structure erection	354
Conductor/OP GW installation	355
R/W cleanup	356
R/W restoration	357

Rhame to Belfield T-line (Rev. 1)

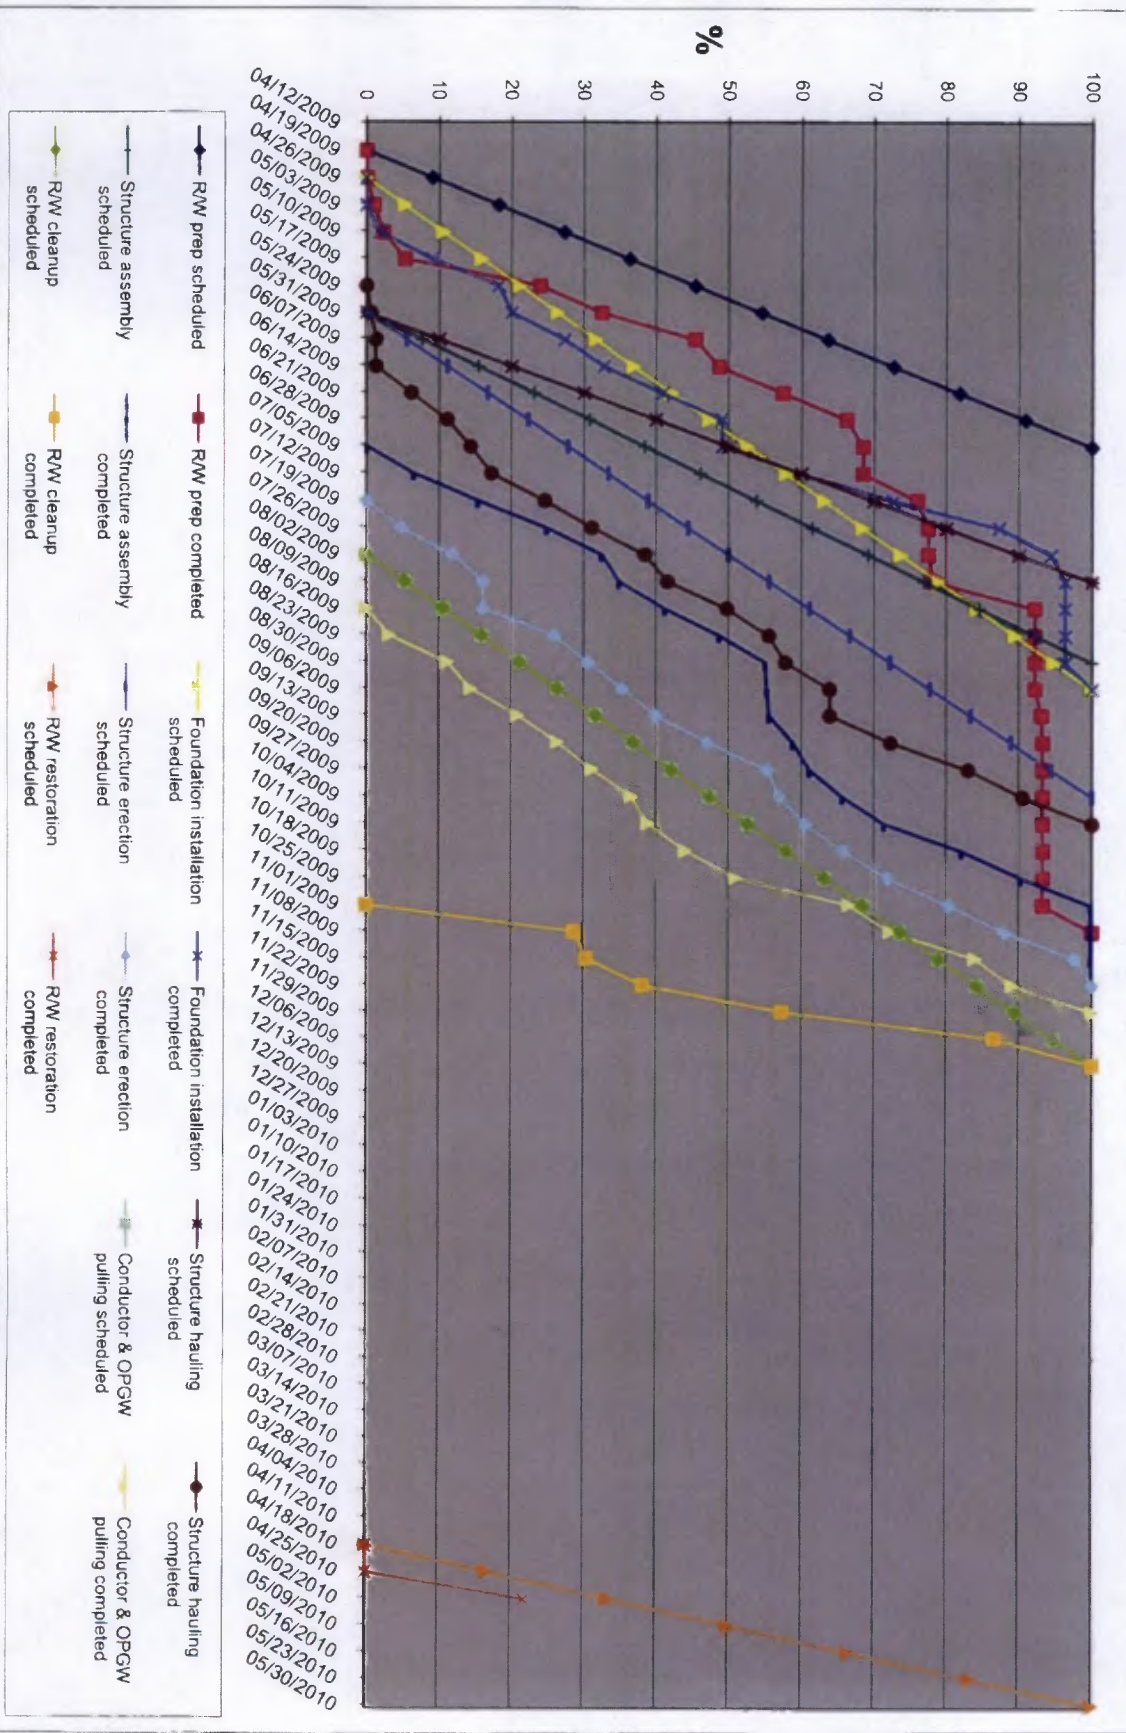

Rhame Substation Construction Rev. #2

