

BASIN ELECTRIC POWER COOPERATIVE
Project: Rhame to Belfield T-line Contract
Contractor: TESSCO
 Restoration contractor - MMI Excavation

Weekly Progress Report

Progress for the week ending : 05/08/2010

Manpower = 0

Note:

Completion the past week

Completion to date

X - indicates a foundation location

Str #1 @ Rhame and Str #524 @ Belfield

	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep	0.0	0.0	523	100.0
Foundation Instl. (55)	0.0	0.0	55	100.0
Structure hauling	0.0	0.0	524	100.0
Structure assembly	0.0	0.0	524	100.0
Structure erection	0.0	0.0	524	100.0
Conductor/OPGW Installation	0.0	0.0	524	100.0
R/W cleanup	0.0	0.0	524	100.0
R/W restoration	0	0.0	114	21.8

Str. Number	Takeoff
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	
31	
32	
33	
34	
35	
36	
37	
38	
39	
40	
41	
42	
43	
44	
45	
46	
47	
48	
49	
50	

R/W prep	
Foundation Installation	
Structure hauling	
Structure assembly	
Structure erection	
Conductor/OPGW Installation	
R/W cleanup	
R/W restoration	

51	
52	
53	
54	
55	
56	
57	
58	
59	
60	
61	
62	
63	
64	
65	
66	
67	
68	
69	
70	
71	
72	
73	
74	
75	
76	
77	
78	
79	
80	
81	
82	
83	
84	
85	
86	
87	
88	
89	
90	
91	
92	
93	
94	
95	
96	
97	
98	
99	
100	

Sr. Number	151
R/W prep	152
Foundation Installation	153
Structure hauling	154
Structure assembly	155
Structure erection	156
Conductor/OPGW installation	157
R/W cleanup	158
R/W restoration	159
Sr. Number	160
R/W prep	161
Foundation Installation	162
Structure hauling	163
Structure assembly	164
Structure erection	165
Conductor/OPGW installation	166
R/W cleanup	167
R/W restoration	168
Sr. Number	169
R/W prep	170
Foundation Installation	171
Structure hauling	172
Structure assembly	173
Structure erection	174
Conductor/OPGW installation	175
R/W cleanup	176
R/W restoration	177
Sr. Number	178
R/W prep	179
Foundation Installation	180
Structure hauling	181
Structure assembly	182
Structure erection	183
Conductor/OPGW installation	184
R/W cleanup	185
R/W restoration	186
Sr. Number	187
R/W prep	188
Foundation Installation	189
Structure hauling	190
Structure assembly	191
Structure erection	192
Conductor/OPGW installation	193
R/W cleanup	194
R/W restoration	195
Sr. Number	196
R/W prep	197
Foundation Installation	198
Structure hauling	199
Structure assembly	200

Sr. Number	201
R/W prep	202
Foundation Installation	203
Structure hauling	204
Structure assembly	205
Structure erection	206
Conductor/OPGW installation	207
R/W cleanup	208
R/W restoration	209
Sr. Number	210
R/W prep	211
Foundation Installation	212
Structure hauling	213
Structure assembly	214
Structure erection	215
Conductor/OPGW installation	216
R/W cleanup	217
R/W restoration	218
Sr. Number	219
R/W prep	220
Foundation Installation	221
Structure hauling	222
Structure assembly	223
Structure erection	224
Conductor/OPGW installation	225
R/W cleanup	226
R/W restoration	227
Sr. Number	228
R/W prep	229
Foundation Installation	230
Structure hauling	231
Structure assembly	232
Structure erection	233
Conductor/OPGW installation	234
R/W cleanup	235
R/W restoration	236
Sr. Number	237
R/W prep	238
Foundation Installation	239
Structure hauling	240
Structure assembly	241
Structure erection	242
Conductor/OPGW installation	243
R/W cleanup	244
R/W restoration	245
Sr. Number	246
R/W prep	247
Foundation Installation	248
Structure hauling	249
Structure assembly	250

Sr. Number	251
R/W prep	252
Foundation Installation	253
Structure hauling	254
Structure assembly	255
Structure erection	256
Conductor/OPGW installation	257
R/W cleanup	258
R/W restoration	259
Sr. Number	260
R/W prep	261
Foundation Installation	262
Structure hauling	263
Structure assembly	264
Structure erection	265
Conductor/OPGW installation	266
R/W cleanup	267
R/W restoration	268
Sr. Number	269
R/W prep	270
Foundation Installation	271
Structure hauling	272
Structure assembly	273
Structure erection	274
Conductor/OPGW installation	275
R/W cleanup	276
R/W restoration	277
Sr. Number	278
R/W prep	279
Foundation Installation	280
Structure hauling	281
Structure assembly	282
Structure erection	283
Conductor/OPGW installation	284
R/W cleanup	285
R/W restoration	286
Sr. Number	287
R/W prep	288
Foundation Installation	289
Structure hauling	290
Structure assembly	291
Structure erection	292
Conductor/OPGW installation	293
R/W cleanup	294
R/W restoration	295
Sr. Number	296
R/W prep	297
Foundation Installation	298
Structure hauling	299
Structure assembly	300

Sr. Number	301
R/W prep	302
Foundation Installation	303
Structure hauling	304
Structure assembly	305
Structure erection	306
Conductor/OPGW installation	307
R/W cleanup	308
R/W restoration	309
Sr. Number	310
R/W prep	311
Foundation Installation	312
Structure hauling	313
Structure assembly	314
Structure erection	315
Conductor/OPGW installation	316
R/W cleanup	317
R/W restoration	318
Sr. Number	319
R/W prep	320
Foundation Installation	321
Structure hauling	322
Structure assembly	323
Structure erection	324
Conductor/OPGW installation	325
R/W cleanup	326
R/W restoration	327
Sr. Number	328
R/W prep	329
Foundation Installation	330
Structure hauling	331
Structure assembly	332
Structure erection	333
Conductor/OPGW installation	334
R/W cleanup	335
R/W restoration	336
Sr. Number	337
R/W prep	338
Foundation Installation	339
Structure hauling	340
Structure assembly	341
Structure erection	342
Conductor/OPGW installation	343
R/W cleanup	344
R/W restoration	345
Sr. Number	346
R/W prep	347
Foundation Installation	348
Structure hauling	349
Structure assembly	350


Str. Number	351
R/W prep	352
Foundation installation	353
Structure hauling	354
Structure assembly	355
Structure erection	356
Conductor/OPGW installation	357
R/W cleanup	358
R/W restoration	359
Str. Number	360
R/W prep	361
Foundation installation	362
Structure hauling	363
Structure assembly	364
Structure erection	365
Conductor/OPGW installation	366
R/W cleanup	367
R/W restoration	368
Str. Number	369
R/W prep	370
Foundation installation	371
Structure hauling	372
Structure assembly	373
Structure erection	374
Conductor/OPGW installation	375
R/W cleanup	376
R/W restoration	377
Str. Number	378
R/W prep	379
Foundation installation	380
Structure hauling	381
Structure assembly	382
Structure erection	383
Conductor/OPGW installation	384
R/W cleanup	385
R/W restoration	386
Str. Number	387
R/W prep	388
Foundation installation	389
Structure hauling	390
Structure assembly	391
Structure erection	392
Conductor/OPGW installation	393
R/W cleanup	394
R/W restoration	395
Str. Number	396
R/W prep	397
Foundation installation	398
Structure hauling	399
Structure assembly	400

Str. Number	401
R/W prep	402
Foundation installation	403
Structure hauling	404
Structure assembly	405
Structure erection	406
Conductor/OPGW installation	407
R/W cleanup	408
R/W restoration	409
Str. Number	410
R/W prep	411
Foundation installation	412
Structure hauling	413
Structure assembly	414
Structure erection	415
Conductor/OPGW installation	416
R/W cleanup	417
R/W restoration	418
Str. Number	419
R/W prep	420
Foundation installation	421
Structure hauling	422
Structure assembly	423
Structure erection	424
Conductor/OPGW installation	425
R/W cleanup	426
R/W restoration	427
Str. Number	428
R/W prep	429
Foundation installation	430
Structure hauling	431
Structure assembly	432
Structure erection	433
Conductor/OPGW installation	434
R/W cleanup	435
R/W restoration	436
Str. Number	437
R/W prep	438
Foundation installation	439
Structure hauling	440
Structure assembly	441
Structure erection	442
Conductor/OPGW installation	443
R/W cleanup	444
R/W restoration	445
Str. Number	446
R/W prep	447
Foundation installation	448
Structure hauling	449
Structure assembly	450

Str. Number	451
R/W prep	452
Foundation installation	453
Structure hauling	454
Structure assembly	455
Structure erection	456
Conductor/OPGW installation	457
R/W cleanup	458
R/W restoration	459
Str. Number	460
R/W prep	461
Foundation installation	462
Structure hauling	463
Structure assembly	464
Structure erection	465
Conductor/OPGW installation	466
R/W cleanup	467
R/W restoration	468
Str. Number	469
R/W prep	470
Foundation installation	471
Structure hauling	472
Structure assembly	473
Structure erection	474
Conductor/OPGW installation	475
R/W cleanup	476
R/W restoration	477
Str. Number	478
R/W prep	479
Foundation installation	480
Structure hauling	481
Structure assembly	482
Structure erection	483
Conductor/OPGW installation	484
R/W cleanup	485
R/W restoration	486
Str. Number	487
R/W prep	488
Foundation installation	489
Structure hauling	490
Structure assembly	491
Structure erection	492
Conductor/OPGW installation	493
R/W cleanup	494
R/W restoration	495
Str. Number	496
R/W prep	497
Foundation installation	498
Structure hauling	499
Structure assembly	500

Str. Number	501
R/W prep	502
Foundation installation	503
Structure hauling	504
Structure assembly	505
Structure erection	506
Conductor/OPGW installation	507
R/W cleanup	508
R/W restoration	509
Str. Number	510
R/W prep	511
Foundation installation	512
Structure hauling	513
Structure assembly	514
Structure erection	515
Conductor/OPGW installation	516
R/W cleanup	517
R/W restoration	518
Str. Number	519
R/W prep	520
Foundation installation	521
Structure hauling	522
Structure assembly	523
Structure erection	524
Conductor/OPGW installation	Takeoff
R/W cleanup	
R/W restoration	

Rhame to Belfield T-line (Rev. 1)

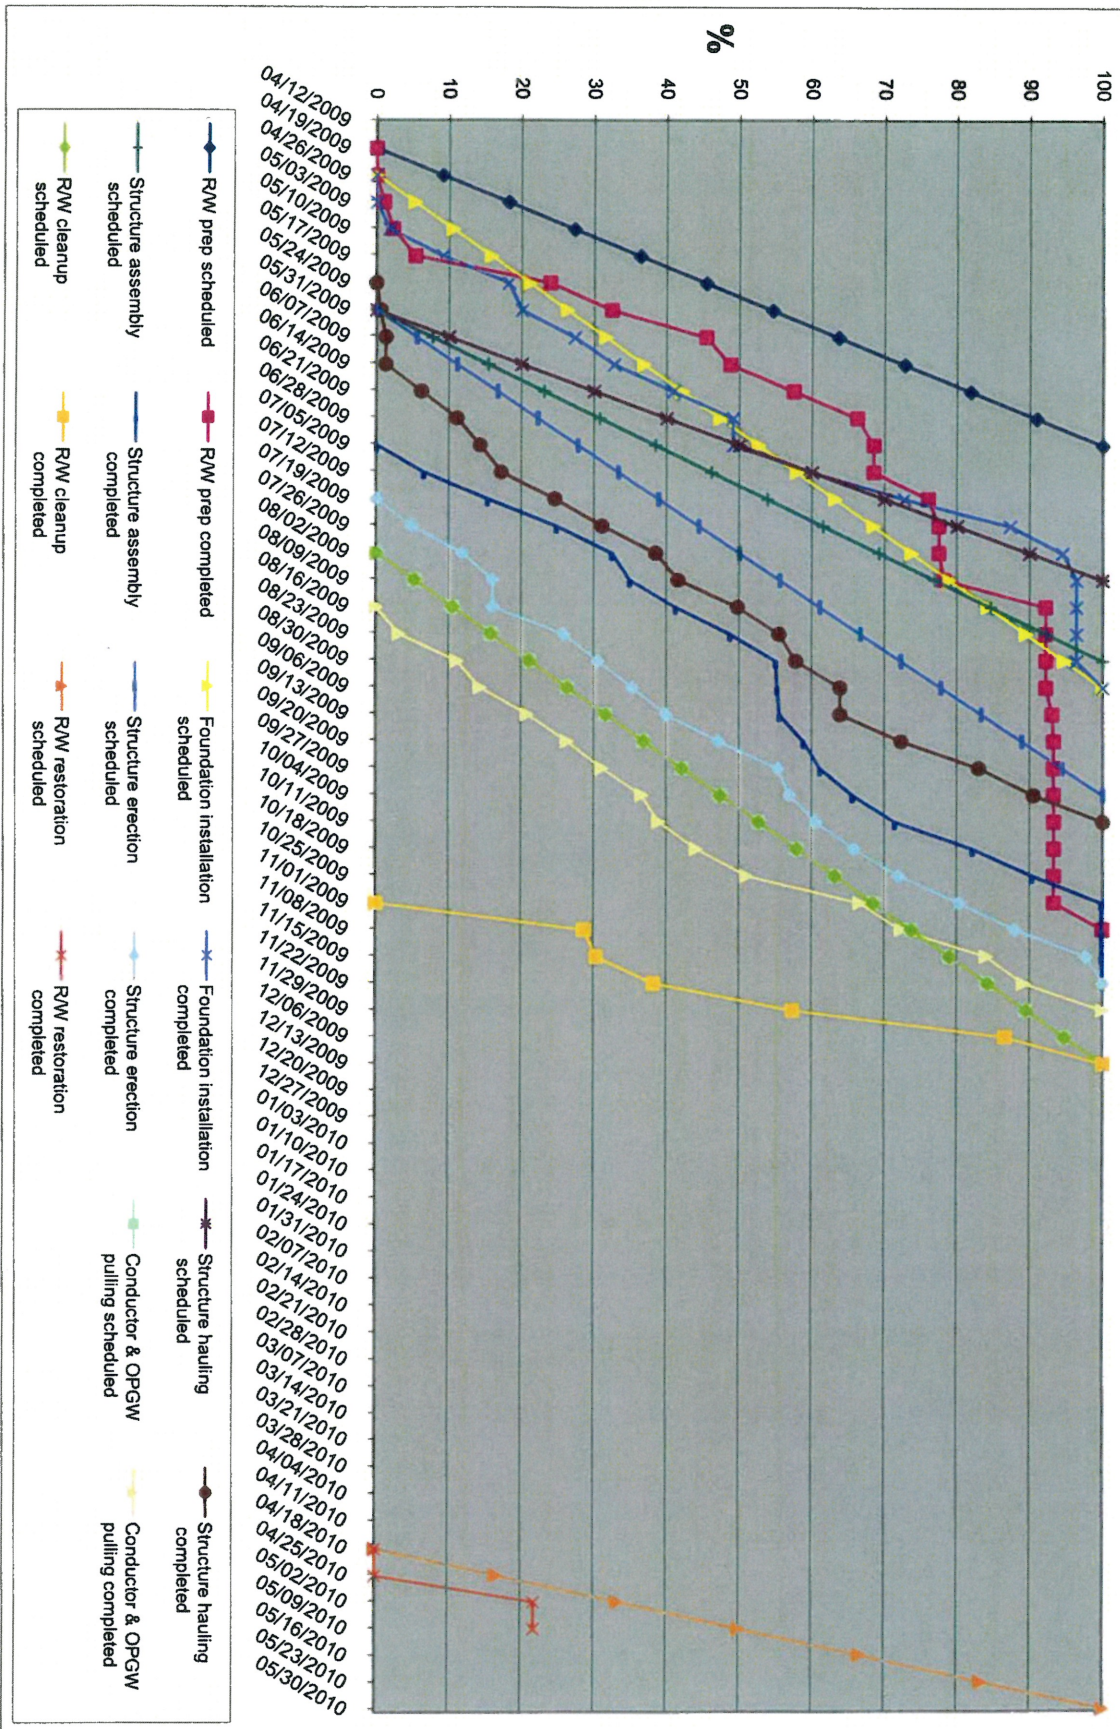

Rhame Substation Construction Rev. #2

