

BASIN ELECTRIC POWER COOPERATIVE
Project: Rhame to Belfield T-line Contract
Contractor: TESSCO
Restoration contractor - MMI Excavation

Weekly Progress Report

Progress for the week ending : 05/15/2010

Manpower = 6

Note:
 Completion the past week

Completion to date

X - indicates a foundation location

Sr #1 @ Rhame and Sr #524 @ Belfield

	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep	0.0	523	100.0	
Foundation Instl (55)	0.0	55	100.0	
Structure hauling	0.0	524	100.0	
Structure assembly	0.0	524	100.0	
Structure erection	0.0	524	100.0	
Conductor/OP/GW Installation	0.0	524	100.0	
R/W cleanup	0.0	524	100.0	
R/W restoration	57	10.9	171	32.6

Sr. Number	Takeoff
R/W prep	1
Foundation Installation	2
Structure hauling	3
Structure assembly	4
Structure erection	5
Conductor/OP/GW Installation	6
R/W cleanup	7
R/W restoration	8
	9
	10
	11
	12
	13
	14
	15
	16
	17
	18
	19
	20
	21
	22
	23
	24
	25
	26
	27
	28
	29
	30
	31
	32
	33
	34
	35
	36
	37
	38
	39
	40
	41
	42
	43
	44
	45
	46
	47
	48
	49
	50

R/W prep	51
Foundation Installation	52
Structure hauling	53
Structure assembly	54
Structure erection	55
Conductor/OP/GW Installation	56
R/W cleanup	57
R/W restoration	58
	59
	60
	61
	62
	63
	64
	65
	66
	67
	68
	69
	70
	71
	72
	73
	74
	75
	76
	77
	78
	79
	80
	81
	82
	83
	84
	85
	86
	87
	88
	89
	90
	91
	92
	93
	94
	95
	96
	97
	98
	99
	100

Sr. Number	101
R/W prep	102
Foundation Installation	103
Structure hauling	104
Structure assembly	105
Structure erection	106
Conductor/OP/GW Installation	107
R/W cleanup	108
R/W restoration	109
	110
	111
	112
	113
	114
	115
	116
	117
	118
	119
	120
	121
	122
	123
	124
	125
	126
	127
	128
	129
	130
	131
	132
	133
	134
	135
	136
	137
	138
	139
	140
	141
	142
	143
	144
	145
	146
	147
	148
	149
	150

Str. Number	151
R/W prep	152
Foundation Installation	153
Structure hauling	154
Structure assembly	155
Structure erection	156
Conductor/OPGW Installation	157
R/W cleanup	158
R/W restoration	159
	160
	161
	162
	163
	164
	165
	166
	167
	168
	169
	170
	171
	172
	173
	174
	175
	176
	177
	178
	179
	180
	181
	182
	183
	184
	185
	186
	187
	188
	189
	190
	191
	192
	193
	194
	195
	196
	197
	198
	199
	200

Str. Number	201
R/W prep	202
Foundation Installation	203
Structure hauling	204
Structure assembly	205
Structure erection	206
Conductor/OPGW Installation	207
R/W cleanup	208
R/W restoration	209
	210
	211
	212
	213
	214
	215
	216
	217
	218
	219
	220
	221
	222
	223
	224
	225
	226
	227
	228
	229
	230
	231
	232
	233
	234
	235
	236
	237
	238
	239
	240
	241
	242
	243
	244
	245
	246
	247
	248
	249
	250

Str. Number	251
R/W prep	252
Foundation Installation	253
Structure hauling	254
Structure assembly	255
Structure erection	256
Conductor/OPGW Installation	257
R/W cleanup	258
R/W restoration	259
	260
	261
	262
	263
	264
	265
	266
	267
	268
	269
	270
	271
	272
	273
	274
	275
	276
	277
	278
	279
	280
	281
	282
	283
	284
	285
	286
	287
	288
	289
	290
	291
	292
	293
	294
	295
	296
	297
	298
	299
	300

Str. Number	301
R/W prep	302
Foundation Installation	303
Structure hauling	304
Structure assembly	305
Structure erection	306
Conductor/OPGW Installation	307
R/W cleanup	308
R/W restoration	309
	310
	311
	312
	313
	314
	315
	316
	317
	318
	319
	320
	321
	322
	323
	324
	325
	326
	327
	328
	329
	330
	331
	332
	333
	334
	335
	336
	337
	338
	339
	340
	341
	342
	343
	344
	345
	346
	347
	348
	349
	350


Str. Number	351
R/W prep	352
Foundation Installation	353
Structure hauling	354
Structure assembly	355
Structure erection	356
Conductor/OPGW installation	357
R/W cleanup	358
R/W restoration	359
	360
	361
	362
	363
	364
	365
	366
	367
	368
	369
	370
	371
	372
	373
	374
	375
	376
	377
	378
	379
	380
	381
	382
	383
	384
	385
	386
	387
	388
	389
	390
	391
	392
	393
	394
	395
	396
	397
	398
	399
	400

Str. Number	401
R/W prep	402
Foundation Installation	403
Structure hauling	404
Structure assembly	405
Structure erection	406
Conductor/OPGW installation	407
R/W cleanup	408
R/W restoration	409
	410
	411
	412
	413
	414
	415
	416
	417
	418
	419
	420
	421
	422
	423
	424
	425
	426
	427
	428
	429
	430
	431
	432
	433
	434
	435
	436
	437
	438
	439
	440
	441
	442
	443
	444
	445
	446
	447
	448
	449
	450

Str. Number	451
R/W prep	452
Foundation Installation	453
Structure hauling	454
Structure assembly	455
Structure erection	456
Conductor/OPGW installation	457
R/W cleanup	458
R/W restoration	459
	460
	461
	462
	463
	464
	465
	466
	467
	468
	469
	470
	471
	472
	473
	474
	475
	476
	477
	478
	479
	480
	481
	482
	483
	484
	485
	486
	487
	488
	489
	490
	491
	492
	493
	494
	495
	496
	497
	498
	499
	500

Str. Number	501
R/W prep	502
Foundation Installation	503
Structure hauling	504
Structure assembly	505
Structure erection	506
Conductor/OPGW installation	507
R/W cleanup	508
R/W restoration	509
	510
	511
	512
	513
	514
	515
	516
	517
	518
	519
	520
	521
	522
	523
	524
	Takeoff

Rhame to Belfield T-line (Rev. 1)

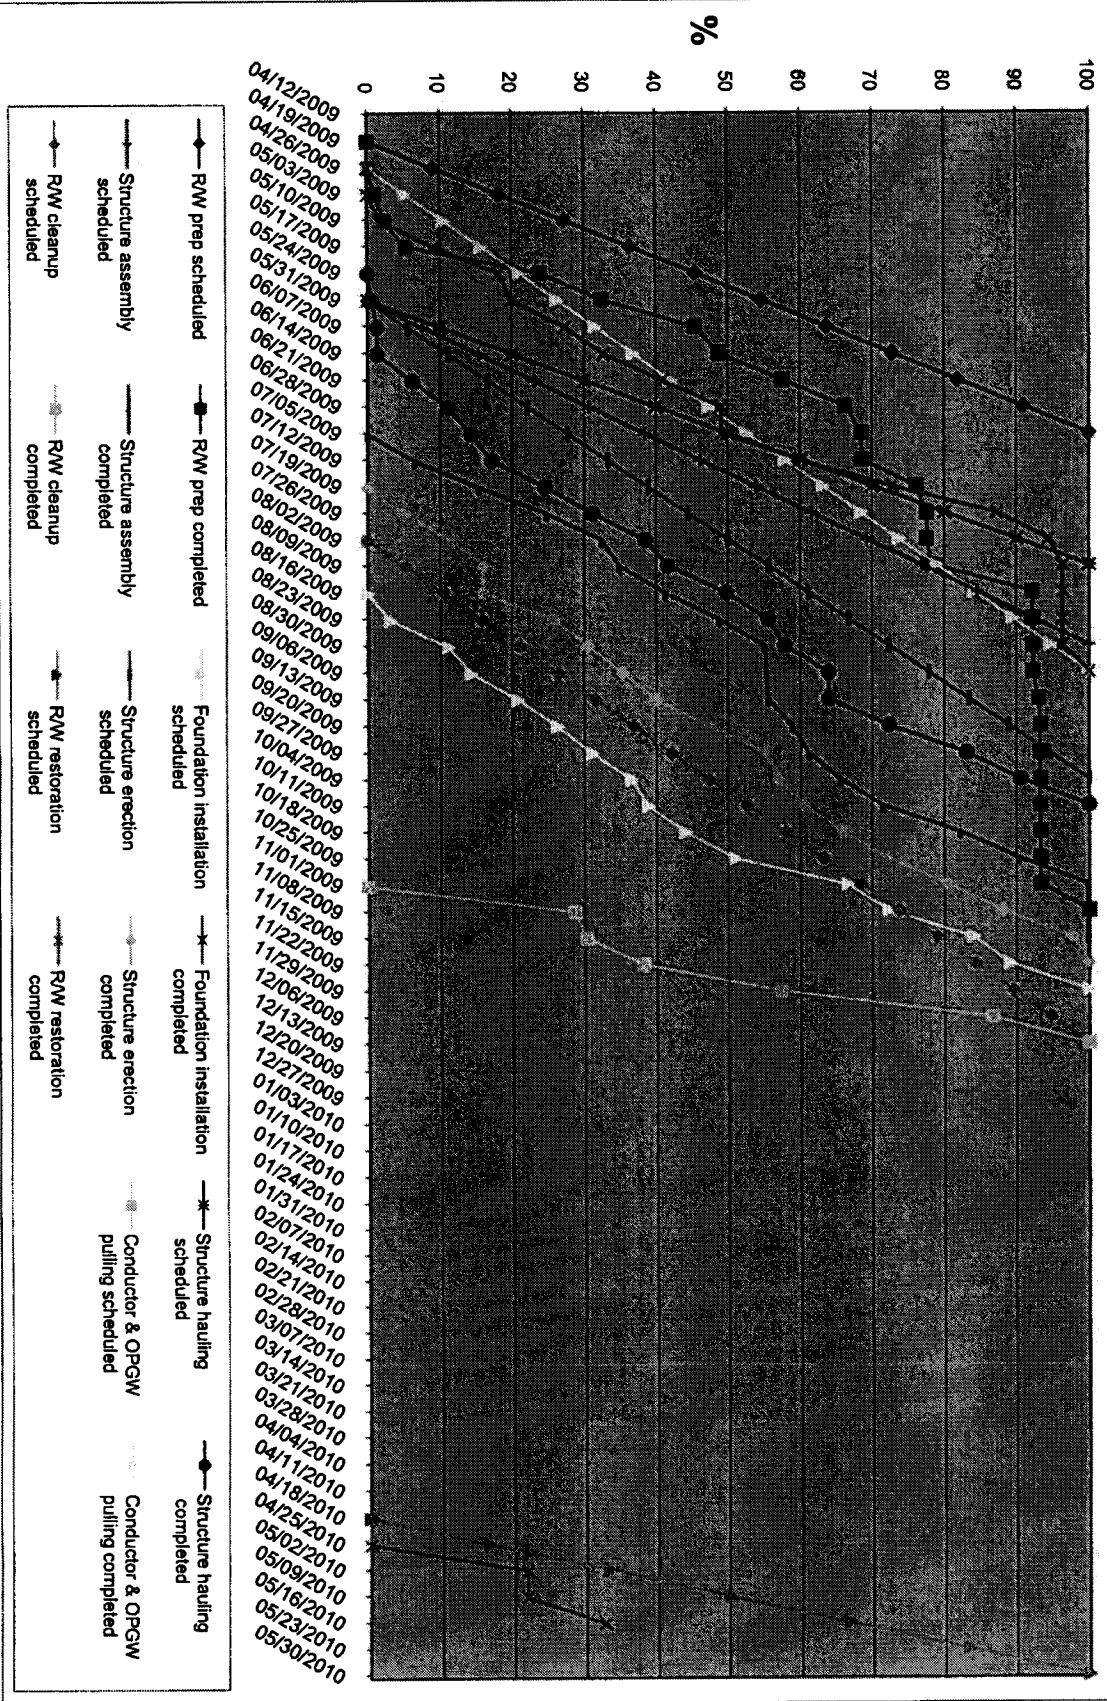

Rhame Substation Construction Rev. #2

