



**FPL ENERGY LANGDON WIND II, LLC  
LANGDON, NORTH DAKOTA**

*Plan of the Day (POD)*

Weather Forecast: Cloudy  
High: 69°F Low: 44°F  
Winds: W @ 11 mph  
Precipitation Chances: 50 %

Tuesday, September 23, 2008

COD - 09/26/08

4 Days to COD

**FPL Energy**

**Wanzek**

**GEWE**

**Safety/Environmental:**

- SWPPP inspection today due to 1.7 inches of rain
- Caution loading materials, watch for pinch points
- Color of the month is White
- Caution when maneuvering near operating turbines

**Civil:**

- Tower reclaim – on hold due to wet conditions

**Erection:**

- Met towers

**Electrical:**

- All feeders energized
- Final commissioning on L2-2

**Substation:**

- Complete


**Ongoing Activities:**

- Contractor is continuing to mobilize equipment and materials out of laydown yard. Reclaim work in laydown yard continues.

**General Construction Status**

117 PU-07-722 Filed: 9/23/2008 Pages: 1  
Langdon Wind Plan of the Day, Sept. 23, 2008

Langdon Wind, LLC

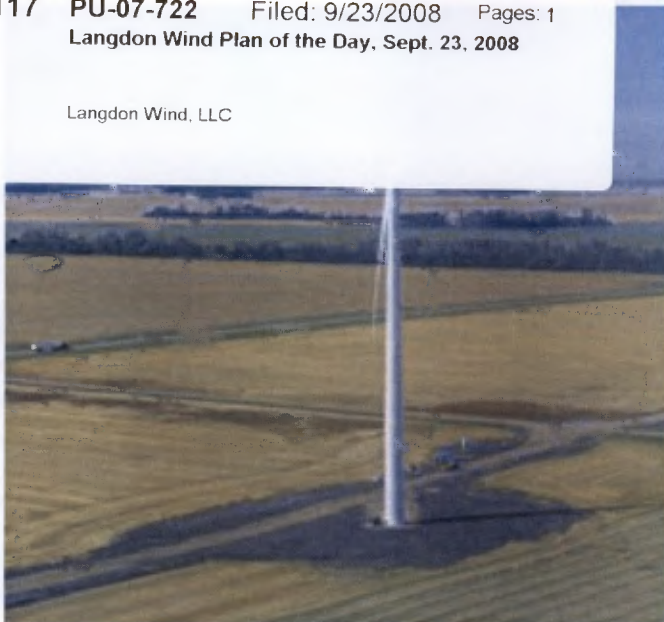

	Complete	Total	% Complete
Mechanically Completed	27	27	100.0%
Pre-Commissioned	27	27	100.0%
Final Commissioned	26	27	96.3%
(as of COB yesterday)			
