

Hamre, John G.

From: Fahn, Patrick J.
Sent: Monday, January 19, 2009 10:18 AM
To: Hamre, John G.
Subject: FW: PU-07-791 and PU-08-812- Weekly reports
Attachments: PSC Report PU-08-812 (ejk 9-Jan-09).doc; PSC Report PU-07-791 (ejk 9-Jan-09).doc; Beaver Lodge tub ring #3.jpg; Beaver Lodge tub ring #4.jpg; Beaver Lodge tub ring #5.jpg; Beaver Lodge tub ring #6.jpg; DSC02547.jpg; DSC02544.jpg; DSC02546.jpg

John – please docket in 07-791 and 08-812 from Enbridge and then forward to Commissioners, PUD, and Legal. This one should have been docketed before the other email I sent this morning.

Patrick Fahn

Utility Analyst
Email: pfahn@nd.gov
Phone: (701) 328-4077

North Dakota Public Service Commission
600 E Boulevard
Bismarck ND 58505-0480
Fax: (701) 328-2410

From: Ed Kelly [mailto:Ed.Kelly@rooney-eng.com]
Sent: Friday, January 09, 2009 2:19 PM
To: Fahn, Patrick J.
Cc: 'Brent.Horton@enbridge.com'; Troy D. Pierantoni; 'Trent_Mattick@Enbridge.com'; Tim Kinney; Ty France; Paul Giron; Casper Front Desk; 'Jessica.Faith@enbridge.com'; 'Steve Schmalzt'; 'Tony Kueffler'; 'Gary Blowers'; 'Kevin Gault'; 'Adam Cole'
Subject: RE: PU-07-791 and PU-08-812- Weekly reports

Weekly report for Jan. 9 along with pictures.

Let me know if you have any questions or comments.

Thanks,

Edward J. Kelly, P.E.

Project Manager

ROONEY ENGINEERING, INC.

Engineering for the Energy Industry

12201 E. Arapahoe Rd., Ste. C-10
Centennial, CO 80112
Office: 303-705-9325
Cell: 303-594-6157
Fax: 303-792-0227

29 **PU-08-812** Filed: 1/9/2009 Pages: 12
Enbridge Pipeline Weekly Report for week of Jan. 09, 2009

Enbridge Pipelines (North Dakota) LLC

Edward Kelly, Project Mgr.

82 **PU-07-791** Filed: 1/9/2009 Pages: 12
Enbridge Pipeline Weekly Report for week of Jan. 09, 2009

Enbridge Pipelines (North Dakota) LLC

Edward Kelly, Project Mgr.



**ROONEY ENGINEERING,
INC.**
Engineering for the Energy
Industry



Weekly Construction Progress Report

Enbridge Pipelines (North Dakota) LLC

Week of: Jan. 9, 2009

Case No. PU-08-812

	Name	Company	Office	Cell
Supervising Project Manager	Edward Kelly	Rooney Engineering	303-705-9325	303-594-6157
Supervisor - Construction Services:	Trent Mattick	Enbridge	701-857-0803	701-721-3356

Brief Description of Weekly Activities:

Stanley Injection

- Work continues on foundations but slow progress with weather. Fabrication work for mechanical started.


Specific Activity on Project			
Description	% Complete	Description	% Complete
Stanley Station			
Civil	5		
Mechanical	5		
Electrical	0		
Clean-up	0		

Significant Work Activity for next week:

Stanley Station

- Foundation work to continue as weather allows. Prefabrication work to continue.

Comments:

Name	Date
Edward J. Kelly 	1/9/09



**ROONEY ENGINEERING,
INC.**
Engineering for the Energy
Industry



Weekly Construction Progress Report

Enbridge Pipelines (North Dakota) LLC

Week of: Jan. 9, 2009

Case No. PU-07-791

	Name	Company	Office	Cell
Supervising Project Manager	Edward Kelly	Rooney Engineering	303-705-9325	303-594-6157
Supervisor - Construction Services:	Trent Mattick	Enbridge	701-857-0803	701-721-3356

Brief Description of Weekly Activities:

Alexander Station

- Nothing to report.

Trenton Station

- Nothing to report.

Beaver Lodge Station

- Installed Tub ring.

Stanley Station

- Prefabrication of piping complete.

Blaisdell Station

- Nothing to report.

Minot Station

- Continued shop fabrication of mechanical. Fabrication and painting of cable tray supports underway.

Denbigh Station

- Nothing to report – 2008 work complete.

Pleasant Lake Station

- Nothing to report – 2008 work complete.

Penn Station

- Nothing to report – 2008 work complete.

Bartlett Station

- Nothing to report – 2008 work complete.

Larimore Station

- Nothing to report – 2008 work complete.

Specific Activity on Project			
Description	% Complete	Description	% Complete
Alexander Station		Trenton Station	
Civil	0	Civil	0
Mechanical	0	Mechanical	0
Electrical	0	Electrical	0
Clean-up	0	Clean-up	0
Beaver Lodge Station		Stanley Station	
Civil	35	Civil	35
Mechanical	8	Mechanical	45
Electrical	0	Electrical	0
Clean-up	0	Clean-up	0
Blaisdell Station		Minot Station	
Civil	0	Civil	60
Mechanical	0	Mechanical	30
Electrical	0	Electrical	0
Clean-up	0	Clean-up	0
Denbigh Station		Pleasant Lake Station	
Civil	80	Civil	70
Mechanical	0	Mechanical	60
Electrical	0	Electrical	45
Clean-up	0	Clean-up	0
Penn Station		Bartlett Lake Station	
Civil	70	Civil	60
Mechanical	45	Mechanical	0
Electrical	0	Electrical	0
Clean-up	0	Clean-up	0
Larimore Station			
Civil	70		
Mechanical	45		
Electrical	30		
Clean-up	0		

Significant Work Activity for next week:
<p>Alexander Station</p> <ul style="list-style-type: none"> • Nothing to report. <p>Trenton Station</p> <ul style="list-style-type: none"> • Nothing to report. <p>Beaver Lodge Station</p> <ul style="list-style-type: none"> • Welding for steel floor work and tub ring to continue. Then the plan is to demob until spring. <p>Stanley Station</p> <ul style="list-style-type: none"> • Nothing to report. Field work on hold until weather breaks. <p>Blaisdell Station</p> <ul style="list-style-type: none"> • Nothing to report. <p>Minot Station</p> <ul style="list-style-type: none"> • Continue shop fabrication. Field install cable tray supports. <p>Denbigh Station</p> <ul style="list-style-type: none"> • Nothing to report. <p>Pleasant Lake Station</p> <ul style="list-style-type: none"> • Nothing to report.

Penn Station

- Nothing to report.


Bartlett Station

- Nothing to report.

Larimore Station

- Nothing to report.

Comments:

Name	Date
Edward J. Kelly 	1/9/09










DATE: 01-06-09
NDSE / PHASE 6 / STANLEY STATION
AFE: 0790401121
FILL HEADER PIER SUPPORTS
INSPECTOR: PAUL STEEN

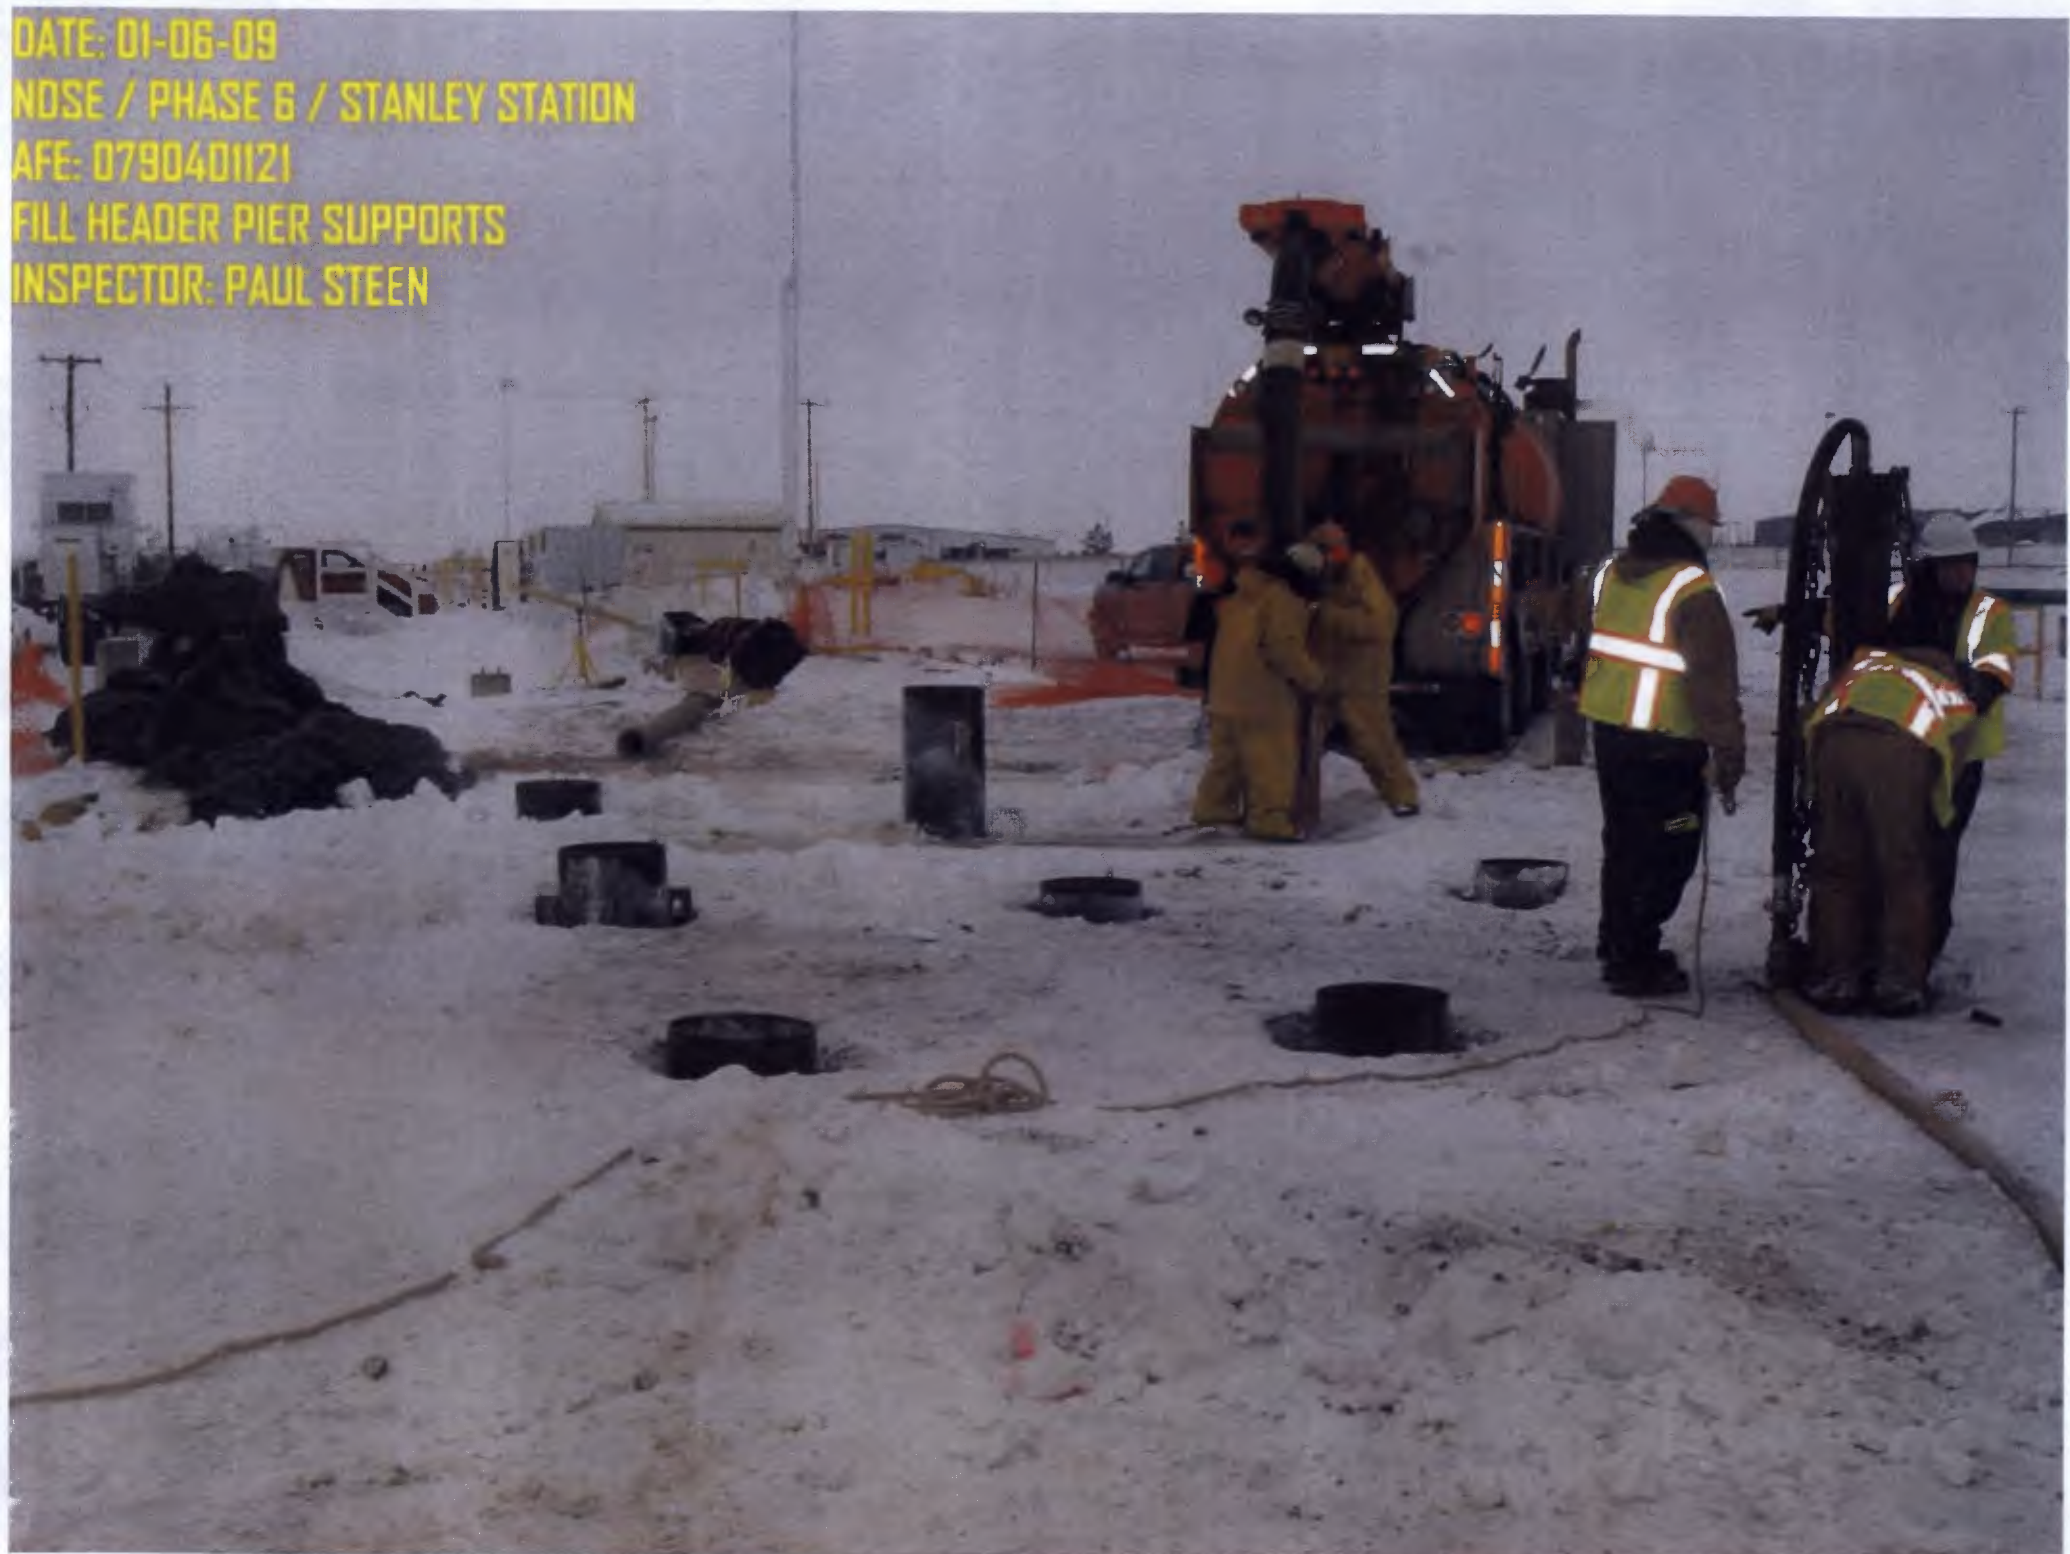

DATE: 01-06-09

NOISE / PHASE 6 / STANLEY STATION

AFE: 0790401121

HYDRO-EXCAVATION OF FILL HEADER PIER SUPPORTS

INSPECTOR: PAUL STEEN



DATE: 01-06-09
NOSE / PHASE 6 / STANLEY STATION
AFE: 0790401121
DRIVING OF CASINGS TO FILL HEADER
INSPECTOR: PAUL STEEN

