

**FPL ENERGY ASHTABULA WIND, LLC
LUVERNE, NORTH DAKOTA**

Plan of the Day (POD)

Weather Forecast: Partly Sunny
High: 89°F Low: 59°F
Winds: WSW @ 7 mph
Precipitation Chances: 24%

Thursday, July 24, 2008

COD - 12/31/08

161 Days to COD

FPL Energy

Otter Tail

Blattner

GEWE

Environmental:

- SWPPP inspection Today.
- Developing wetland impact prevention plan and maps
- Monitor environmentally sensitive areas
- Marking environmentally sensitive areas
- Environmental awareness to ALL crews, including sub-contractors
- Silt fence installation
- Wetland sign installation

Safety:

- Check back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Maintain hydration.
- Watch soft spots when off-loading trucks.

Civil:

- Sub-grade at AT1-AT4, AT66 – AT68 & AT11-AT12
- Gravel at AT17-AT21 & AT 31-AT33
- Approach AT5

Substation:


- Grading pad complete

Monthly Management Meeting is scheduled for Friday August 1st, 2008

Receiving (As of COB yesterday)

	Total	Rec'd	Balance
PMT XFR	99	21	78
Grounding XFR	9	9	0
4/0 Cable	588,000	593,673	-5,673
1000KM	396,000	397,603	-1,603
500KM	99,000	62,115	36,885
12 Fiber SM	385,000	371,758	13,242
1000 KCM (LVC)	37,000	35,175	1,825
Grounding XFR boxp	8	0	8
XFR Box Pads	100	10	90
Copperclad Cable	108,000	108,917	-917
Bases	99	0	99
Mids	99	0	99
Tops	99	0	99
Machine Heads	99	0	99
Contollers (DTA's)	99	0	99
Blade Sets	99	0	99
Hubs	99	0	99

General Construction Status

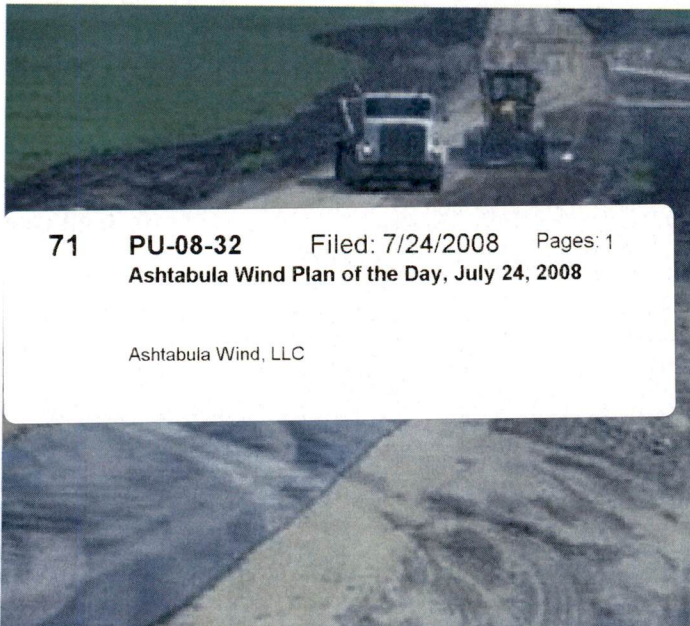

71 PU-08-32 Filed: 7/24/2008 Pages: 1
 Ashtabula Wind Plan of the Day, July 24, 2008

Ashtabula Wind, LLC

	Total	Complete	% Complete
Roads Subgraded LF	117,819	14,743	12.5%
Roads Complete LF	117,819	0	0.0%
Foundations Excavated	99	0	0.0%
Foundations Poured	99	0	0.0%
Foundations Backfilled	99	0	0.0%
Crane Pads Complete	99	0	0.0%
Tower Base Sections Erected	99	0	0.0%
Tower Mid Sections Erected	99	0	0.0%
Tower Top Sections Erected	99	0	0.0%
Machine Heads Installed	99	0	0.0%
Rotors Flown	99	0	0.0%
Mechanically Completed	99	0	0.0%
Pre-Commissioned	99	0	0.0%
Final Commissioned	99	0	0.0%
Cable Installed 4/0	588,000	0	0.0%
Cable Installed 1000 KM	396,000	0	0.0%
Cable Installed 500 KM	99,000	0	0.0%
Fiber-Optic 12 Fiber SM	385,000	0	0.0%
Copperclad Cable	108,000	0	0.0%
Transformers Set	99	0	0.0%
Transformers Terminated	99	0	0.0%
(as of COB yesterday)			

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE
