

**FPL ENERGY ASHTABULA WIND, LLC  
LIVERNE, NORTH DAKOTA**

***SUBSTATION & TRANSMISSION LINE  
Plan of the Day (POD)***

**Weather Forecast: Partly Sunny**  
**High: 85°F Low: 57°F**  
**Winds: NNW @ 8 mph**  
**Precipitation Chances: 42%**

**Thursday, July 31, 2008**


<b>FPL Energy</b>	<b>Otter Tail Power Company</b>	<b>MJ Electric</b>
-------------------	---------------------------------	--------------------

**Substation**

- Foundations Poured – 12 bases, 6 tops
- Conduit- Below Grade – Transformer area/west

**Transmission Line**

- **Safety/Environmental:**
- **Lay-down Yard:**
- 2 loads of structures on Friday @ 12:00.
- **Electrical Construction:**
- Continue to frame.
- Setting Structures 45, 46, 47, 48
- Moving some dist lines on the north end.
- **Miscellaneous:**
- Longfellow will start drilling at structure 2.  
Concrete to be delivered at 14:30 today.
- 1 rebar cage to be constructed.

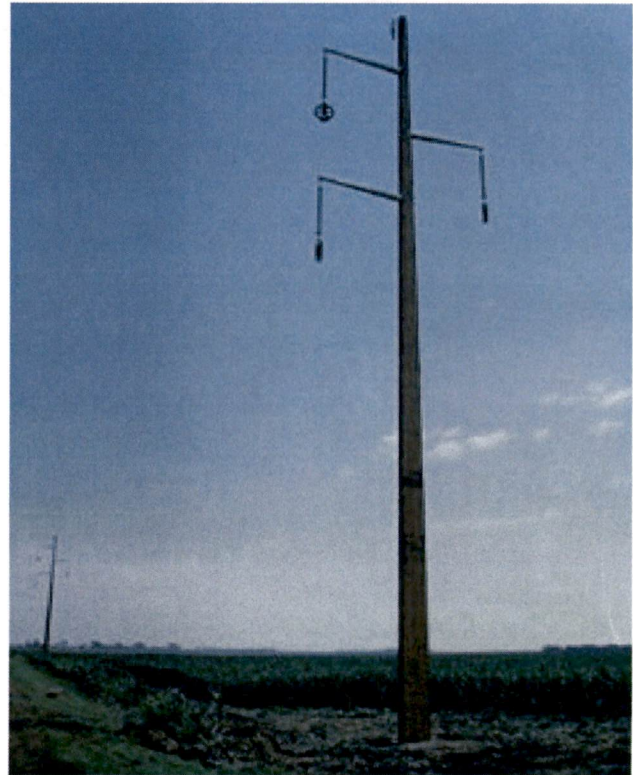

**General Construction Status**

<b>Work Progress Report</b>			
Major Task	Completed	Total	% Complete
Tangent (laminated) foundations excavated	25	74	34%
Tangent (laminated) structures framed	23	75	31%
Tangent (laminated) structures set	19	74	26%
Dead-end/angle (concrete) foundations excavated	1	14	7%
Dead-end/angle (concrete) foundations poured	1	14	7%
Dead-end/angle (steel) structures framed	0	14	0%
Dead-end/angle (steel) structures set	0	14	0%
Spans of 1272 Bittern conductor strung	0	267	0%
Spans of 1272 Bittern sagged and clipped	0	267	0%
Spans of OPGW strung, attached and grounded	0	89	0%
OPGW splices/terminations completed	0	4	0%
Miles of distribution line leaned	6	6	100%
Miles of distribution line dismantled & removed	0	6	0%
Foundation excavation spoils disposed	0	88	0%
Reclamation	0	100%	0%

PU-08-32 Filed: 7/31/2008 Pages: 1  
 Ashtabula, Substation & Transmission Line, Plan of the Day, July 31, 2008

Ashtabula Wind, LLC
