

Tuesday, August 12, 2008

**FPL ENERGY ASHTABULA WIND, LLC**  
**LUVERNE, NORTH DAKOTA**

**SUBSTATION & TRANSMISSION LINE**  
**Plan of the Day (POD)**

Weather Forecast: **Partly Sunny**  
**High: 85°F Low: 53°F**  
**Winds: W @ 6 mph**  
**Precipitation Chances: 20%**

**FPL Energy                      Otter Tail Power Company                      MJ Electric**

**Substation**

- 1 North feeder run start South feeder runs/ East of site
- Grounding from West to East

**Lay-down Yard**

**Electrical Construction**

- Framing structures 2 (steel)
- Hauling materials


**Miscellaneous**

- Longfellow drilling structure 78

<i>RECEIVING (As of COB yesterday)</i>			
Substation Materials	Total	Rec'd	Balance
Power Transformer 241.5 kV/225 MVA	1	0	1
Power Transformer 69kV/125MVA (Lease)	1	0	1
HV Motor Disconnect Switch - 230kV 1200A	2	2	0
HV Manual Disconnect Switch 230kV 1200A	3	3	0
LV Manual Disconnect Switch 34.5kV 2000A	4	4	0
LV Manual Disconnect Switch 34.5kV 4000A	1	1	0
LV Manual Disconnect Switch 34.5kV 1200A	10	10	0
LV Hook Disconnect Switch 34.5kV 1200A	60	60	0
HV Circuit Breaker 230kV 1200A	2	2	0
LV Open Air Breaker 34.5 kV 2000A 40 kA	2	2	0
LV Open Air Breaker 34.5 kV 1200A 40 kA	10	0	10
Switchgear with Building	1	0	1
Control House	1	0	1
HV CCVTs 230kV	3	3	0
HV CCVTs 69kV	3	3	0
Metering Units	1	0	1
Metering Units CT	3	0	3
Metering Units PT	3	0	3
Support Steel and Substation Package	1 Lot	1	1 Lot
Neutral Reactor	1	1	0
SUBSTATION CONSTRUCTION			% Complete
Galvanized Steel Structures			0%
Bus Conductors, Fittings, Insulators & Associated Materials			0%
Disconnect Switches			0%
Surge Protectors			0%
Circuit Breakers			0%
CCVTs, Metering CTs and PTs			0%
Equipment Control Cable, Conduit, Power Cable & 300' of Cable Trenwa System			0%
Conduit, Ground Bank, Fiber Enc., UG Cable, St Svc, Xfmr			25%
Crushed Rock Surfacing			0%
Grounding			40%
Station Lighting			0%
Sub Signage and Fence			0%
Foundations			100%
Testing			0%

**Interconnect Transmission Line**

T-LINE CONSTRUCTION	Complete	Balance	% Complete
Tangent (laminated) foundations excavated	62	74	84%
Tangent (laminated) structures framed	62	74	84%
Tangent (laminated) structures set	61	74	82%
Dead-end/angle foundations excavated	9	14	64%
Dead-end/angle foundations poured	9	14	64%
Dead-end/angle (steel) structures framed	0	14	0%
Dead-end/angle (steel) structures set	0	14	0%
Spans of 1272 Bitterm conductor strung	0	267	0%
Spans of 1272 Bitterm sagged and clipped	0	267	0%
Spans of OPGW strung, attached and grounded	0	89	0%
OPGW splices/terminations completed	0	4	0%
Miles of distribution line leaned	6	6	100%
Miles of distribution line dismantled & removed	0	6	0%
Foundation excavation spoils disposed	0	88	0%
Reclamation	0	100%	0%

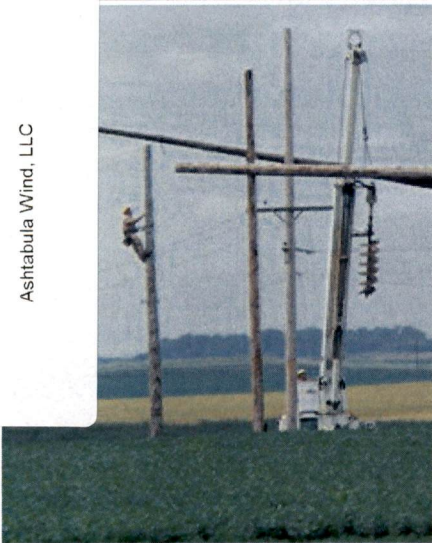

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE

103 PU-08-32 Filed: 8/12/2008 Pages: 1  
 Ashtabula Wind, Substation & Transmission Line,  
 Plan of the Day, Aug. 12, 2008  
 Ashtabula Wind, LLC
