

**FPL ENERGY ASHTABULA WIND, LLC**  
**LUVERNE, NORTH DAKOTA**

*Plan of the Day (POD)*

**Weather Forecast: Partly Sunny**  
**High: 85°F Low: 53°F**  
**Winds: W @ 6 mph**  
**Precipitation Chances: 20%**

**Tuesday, August 12, 2008**

**COD - 12/31/08**

**142 Days to COD**

FPL Energy	Otter Tail	Blattner	GEWE
------------	------------	----------	------

**Environmental:**

- SWPPP inspection August 21
- Developing wetland impact prevention plan and maps
- Monitor environmentally sensitive areas
- Marking environmentally sensitive areas
- Environmental awareness to ALL crews, including sub-contractors
- Silt fence installation

**Safety:**

- Check back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Maintain hydration.
- Watch soft spots when off-loading trucks.

**Civil:**

- Sub-grade at AT98-AT104 & AT109-AT113
- Gravel at AT69-AT80
- Approach AT102 & AT104
- Excavation at AT1, AT2 & AT7
- Mud mat at AT2 & AT4
- Install bottom rebar mat at AT18 - AT20
- Install anchor bolts at AT18 & AT19
- Install top rebar mats at AT17 & AT18
- Form base at AT31
- Pour base at AT32 & AT33

**Collection:**

- Trench & cable install 1000 – Sub F8-SP801, SP901
- Trench & cable install 500 – SP101 – JB11
- Boring408W


**Receiving (As of COB yesterday)**

	Total	Rec'd	Balance
PMT XFR	99	60	39
Grounding XFR	9	9	0
4/0 Cable	588,000	600,815	-12,815
1000KM	396,000	400,725	-4,725
500KM	99,000	99,492	-492
12 Fiber SM	385,000	371,758	13,242
1000 KCM (LVC)	37,000	35,175	1,825
Grounding XFR boxp	8	8	0
XFR Box Pads	100	25	75
Copperclad Cable	108,000	108,917	-917
Bases	99	0	99
Mids	99	0	99
Tops	99	0	99
Machine Heads	99	0	99
Contollers (DTA's)	99	0	99
Blade Sets	99	0	99
Hubs	99	0	99

**General Construction Status**

104 PU-08-32 Filed: 8/12/2008 Pages: 1  
 Ashtabula Wind, Plan of the Day, Aug. 12, 2008

Ashtabula Wind, LLC

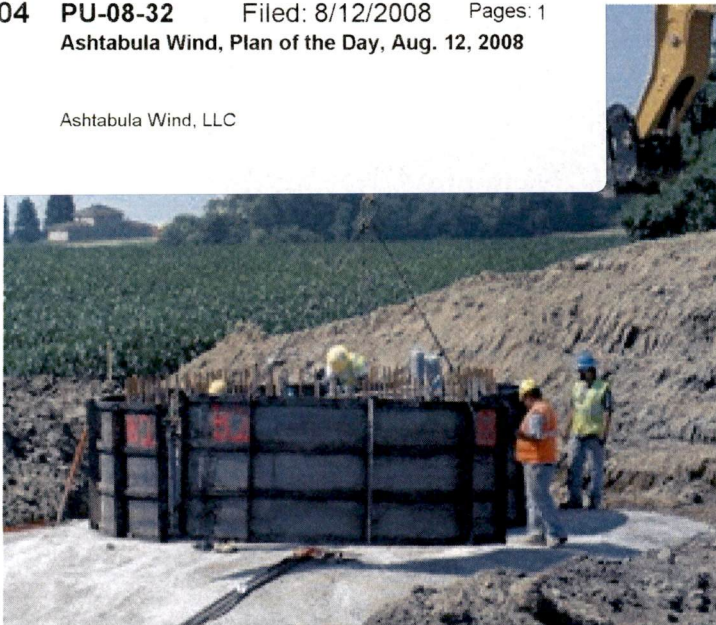

	Total	Complete	% Complete
Roads Subgraded LF	117,819	61,730	52.4%
Roads Complete LF	117,819	39,595	33.6%
Foundations Excavated	99	16	16.2%
Foundations Poured	99	0	0.0%
Foundations Backfilled	99	0	0.0%
Crane Pads Complete	99	0	0.0%
Tower Base Sections Erected	99	0	0.0%
Tower Mid Sections Erected	99	0	0.0%
Tower Top Sections Erected	99	0	0.0%
Machine Heads Installed	99	0	0.0%
Rotors Flown	99	0	0.0%
Mechanically Completed	99	0	0.0%
Pre-Commissioned	99	0	0.0%
Final Commissioned	99	0	0.0%
Cable Installed 4/0	588,000	0	0.0%
Cable Installed 1000 KM	396,000	0	0.0%
Cable Installed 500 KM	99,000	5,452	5.5%
Fiber-Optic 12 Fiber SM	385,000	0	0.0%
Copperclad Cable	108,000	0	0.0%
Transformers Set	99	0	0.0%
Transformers Terminated	99	0	0.0%
(as of COB yesterday)			

**Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE**
