

**FPL ENERGY ASHTABULA WIND, LLC**  
**LUVERNE, NORTH DAKOTA**

*OTTER TAIL Plan of the Day (POD)*

Weather Forecast: **Partly Sunny**  
 High: **86°F** Low: **54°F**  
 Winds: **WSW @ 2 mph**  
 Precipitation Chances: **1%**

**Wednesday, August 13, 2008**

**COD - 12/15/08**

**125 Days to COD**

<b>FPL Energy</b>	<b>Otter Tail</b>	<b>Blattner</b>	<b>GEWE</b>
-------------------	-------------------	-----------------	-------------

**Environmental:**

- SWPPP inspection August 21 .
- Developing wetland impact prevention plan and maps
- Monitor environmentally sensitive areas
- Marking environmentally sensitive areas
- Environmental awareness to ALL crews

**Safety:**

- Check Back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Maintain hydration.
- Watch soft spots when off-loading trucks.

**Civil:**

- Pour base at OT34
- Backfill at OT60, OT59 & OT58

**Electrical:**


- Pedestal Conduit at OT34
- Grounding grid at OT56 – OT58
- Box pad installation at OT59 – OT61

Receiving (As of COB yesterday)			
	Total	Rec'd	Balance
PMT XFR	32	32	0
Grounding XFR	2	2	0
4/0 Cable	147,000	143,366	3,634
1000KM	91,446	94,500	-3,054
500KM	45,000	46,468	-1,468
12 Fiber SM	91,000	95,535	-4,535
1001 KCM (LVC)	12,500	12,500	0
Grounding XFR boxp	2	2	0
XFR Box Pads	32	10	22
Copperclad Cable	45,000	46,291	-1291
Bases	32	0	32
Mids	32	0	32
Tops	32	0	32
Machine Heads	32	0	32
Contollers (DTA's)	32	0	32
Blade Sets	32	0	32
Hubs	32	0	32

**General Construction Status**

106 PU-08-32 Filed: 8/13/2008 Pages: 1  
 Ashtabula Wind, Otter Tail, Plan of the Day, Aug. 13, 2008

Ashtabula Wind, LLC

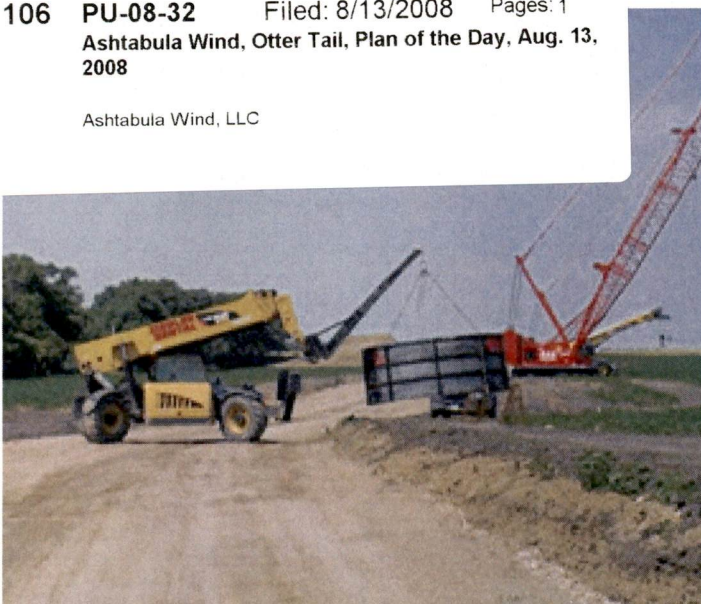

	Total	Complete	% Complete
Roads Subgraded	37,970	41,566	109.5%
Roads Complete	37,970	41,566	109.5%
Foundations Excavated	32	32	100.0%
Foundations Poured	32	31	96.9%
Foundations Backfilled	32	5	15.6%
Crane Pads Complete	32	0	0.0%
Tower Base Sections Erected	32	0	0.0%
Tower Mid Sections Erected	32	0	0.0%
Tower Top Sections Erected	32	0	0.0%
Machine Heads Installed	32	0	0.0%
Rotors Flown	32	0	0.0%
Mechanically Completed	32	0	0.0%
Pre-Commissioned	32	0	0.0%
Final Commissioned	32	0	0.0%
Cable Installed 4/0	147,000	1,528	1.0%
Cable Installed 1000 KM	91,446	25,988	28.4%
Cable Installed 500 KM	45,000	8,836	19.6%
Fiber-Optic 12 Fiber SM	91,000	0	0.0%
1001 KCM (LVC)	12,500	0	0.0%
Copperclad Cable	45,000	0	0.0%
Transformers Set	32	0	0.0%
Transformers Terminated	32	0	0.0%
(as of COB yesterday)			

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE
