

**FPL ENERGY ASHTABULA WIND, LLC
LIVERNE, NORTH DAKOTA**

Plan of the Day (POD)

Weather Forecast: **Partly Sunny**
High: 87°F Low: 58°F
Winds: S @ 16 mph
Precipitation Chances: 2%

Thursday, August 21, 2008

COD - 12/31/08

133 Days to COD

FPL Energy

Otter Tail

Blattner

GEWE

Environmental:

- SWPPP inspection Today
- Developing wetland impact prevention plan and maps
- Monitor environmentally sensitive areas
- Environmental awareness to ALL crews, including sub-contractors
- Silt fence installation

Safety:

- Check back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Maintain hydration.
- Watch soft spots when off-loading trucks.

Civil:

- Sub-grade at AT114-AT121
- Gravel at AT69-AT76, AT81, AT82 & AT86
- Excavation at AT79 - AT82
- Mud mat at AT66 - AT68, & AT77
- Install bottom rebar mat at AT27 - AT30
- Install anchor bolts at AT14- AT16
- Install top rebar mats at AT14, AT22 & AT23
- Form base at AT14, AT22 & AT23
- Pour base at AT23 - AT25
- Form pedestal at AT6, AT7 & AT26
- Pour pedestal at AT6, AT7 & AT26
- Backfill at AT31 & AT32

Electrical:

- Pedestal conduit at AT24 - AT26
- Smurf tube at AT22, AT23 & AT27
- Grounding grid at AT32 & AT33

Collection:

- Boring 305W


Receiving (As of COB yesterday)

	Total	Rec'd	Balance
PMT XFR	99	78	21
Grounding XFR	7	7	0
4/0 Cable	588,000	600,815	-12,815
1000KM	396,000	406,689	-10,689
500KM	99,000	99,492	-492
12 Fiber SM	385,000	371,758	13,242
1000 KCM (LVC)	37,000	35,175	1,825
Grounding XFR boxp	8	8	0
XFR Box Pads	100	45	55
Copperclad Cable	108,000	108,917	-917
Bases	99	0	99
Mids	99	0	99
Tops	99	0	99
Machine Heads	99	0	99
Contollers (DTA's)	99	0	99
Blade Sets	99	0	99
Hubs	99	0	99

General Construction Status

126 PU-08-32 Filed: 8/21/2008 Pages: 1
 Ashtabula Wind, Plan of the Day, Aug. 21, 2008

Ashtabula Wind, LLC

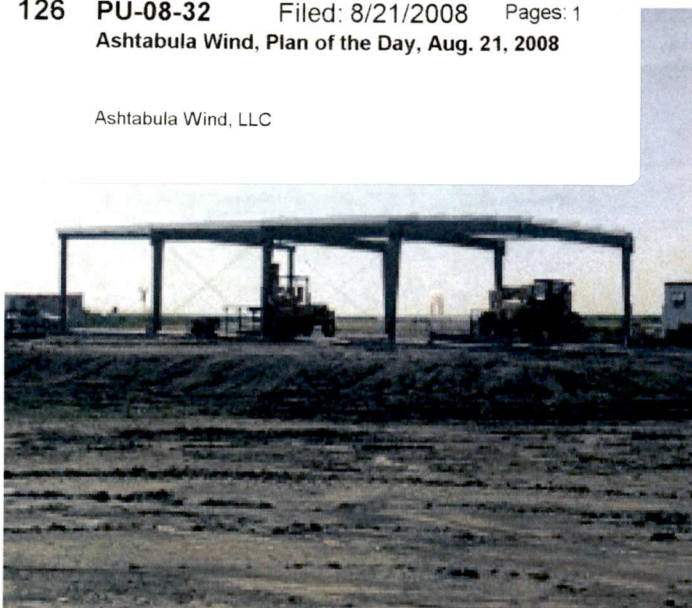

	Total	Complete	% Complete
Roads Subgraded LF	117,819	81,430	69.1%
Roads Complete LF	117,819	39,596	33.6%
Foundations Excavated	99	46	46.5%
Foundations Poured	99	19	19.2%
Foundations Backfilled	99	0	0.0%
Crane Pads Complete	99	0	0.0%
Tower Base Sections Erected	99	0	0.0%
Tower Mid Sections Erected	99	0	0.0%
Tower Top Sections Erected	99	0	0.0%
Machine Heads Installed	99	0	0.0%
Rotors Flown	99	0	0.0%
Mechanically Completed	99	0	0.0%
Pre-Commissioned	99	0	0.0%
Final Commissioned	99	0	0.0%
Cable Installed 4/0	195,491	2,568	1.3%
Cable Installed 1000 KM	145,101	8,322	5.7%
Cable Installed 500 KM	35,335	6,112	17.3%
Fiber-Optic 12 Fiber SM	385,000	0	0.0%
Copperclad Cable	108,000	0	
Transformers Set	99	0	0.0%
Transformers Terminated	99	0	0.0%
(as of COB yesterday)			

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE
