

FPL ENERGY ASHTABULA WIND, LLC
LUVERNE, NORTH DAKOTA

OTTER TAIL Plan of the Day (POD)

Weather Forecast: **Partly Sunny**
 High: **73°F** Low: **38°F**
 Winds: **WSW @ 4 mph**
 Precipitation Chances: **0%**

Thursday, October 2, 2008

COD - 12/15/08

75 Days to COD

FPL Energy	Otter Tail	Blattner	GEWE
------------	------------	----------	------

Environmental:

- SWPPP inspection Today
- Developing wetland impact prevention plan and maps
- Monitor environmentally sensitive areas
- Marking environmentally sensitive areas
- Environmental awareness to ALL crews

Safety:

- Check Back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Maintain hydration.
- Watch soft spots when off-loading trucks.

Erection:


- Erect base & mid at OT37 & OT38
- Assemble rotor at OT34
- Erect top, nacelle & rotor at OT39 & OT40
- Electrical cabling termination at OT51 & OT52
- Mechanical completion pre-walk at OT53
- IIP at OT54 & OT55

Receiving (As of COB yesterday)			
	Total	Rec'd	Balance
PMT XFR	32	33	-1
Grounding XFR	2	2	0
4/0 Cable	147,000	150,560	-3,560
1000KM	91,446	94,500	-3,054
500KM	45,000	46,468	-1,468
12 Fiber SM	91,000	95,535	-4,535
1001 KCM (LVC)	12,500	12,500	0
Grounding XFR boxp	2	2	0
XFR Box Pads	32	32	0
Copperclad Cable	45,000	46,291	-1291
Bases	32	31	1
Mids	32	31	1
Tops	32	32	0
Machine Heads	32	32	0
Contollers (DTA's)	32	32	0
Blade Sets	32	32	0
Hubs	32	32	0

General Construction Status

210 PU-08-32 Filed: 10/2/2008 Pages: 1
 Ashtabula Wind, Otter Tail, Plan of the Day, Oct. 2, 2008

Ashtabula Wind, LLC

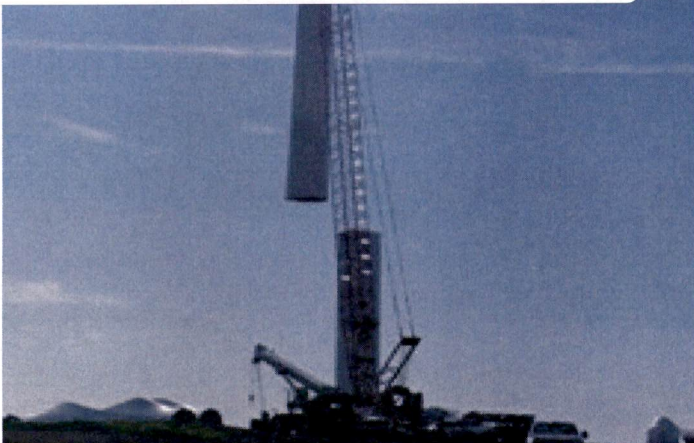

	Total	Complete	% Complete
Roads Subgraded	37,970	41,566	109.5%
Roads Complete	37,970	41,566	109.5%
Foundations Excavated	32	32	100.0%
Foundations Poured	32	32	100.0%
Foundations Backfilled	32	32	100.0%
Crane Pads Complete	32	32	100.0%
Tower Base Sections Erected	32	30	93.8%
Tower Mid Sections Erected	32	30	93.8%
Tower Top Sections Erected	32	26	81.3%
Machine Heads Installed	32	26	81.3%
Rotors Flown	32	26	81.3%
Mechanically Completed	32	8	25.0%
Pre-Commissioned	32	4	12.5%
Final Commissioned	32	0	0.0%
Cable Installed 4/0	127,188	124,602	98.0%
Cable Installed 1000 KM	58,311	77,964	133.7%
Cable Installed 500 KM	44,316	38,802	87.6%
Fiber-Optic 12 Fiber SM	91,000	84,948	93.3%
1001 KCM (LVC)	12,500	0	0.0%
Copperclad Cable	45,000	0	0.0%
Transformers Set	32	32	100.0%
Transformers Terminated	32	32	100.0%

(as of COB yesterday)
