

**FPL ENERGY ASHTABULA WIND, LLC
LIVERNE, NORTH DAKOTA**

Plan of the Day (POD)

Weather Forecast: Partly Sunny
High: 57 F Low: 36-F
Winds: ESE @ 5 mph
Precipitation Chances: 0%

Friday, October 17, 2008

COD - 12/31/08

76 Days to COD

FPL Energy	Otter Tail	Blattner	GEWE
------------	------------	----------	------

Environmental:

- SWPPP inspection October 30th
- Developing wetland impact prevention plan and maps
- Monitor environmentally sensitive areas
- Environmental awareness to ALL crews
- Silt fence installation

Safety:

- Check back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Maintain hydration.
- Watch soft spots when off-loading trucks.
- Hunters are out, Stay visible.

Civil:

- Offload tower sections, hubs & blades

Erection:

- Erect base & mid at AT1, AT2, AT13, AT29 & AT30
- Assemble rotor at AT29 & AT30
- Erect top, nacelle, & rotor at AT5, AT18, AT19 & AT20

Electrical:

- Electrical cabling & termination at AT5 –AT7, & AT17
- Controller termination at AT69 –AT72
- PMT at AT117 & AT121

Collection:


- Cable install -4/0 at AT117–AT121
- Low voltage cable termination at AT69 – AT71
- JBox at JB5-1

Receiving (As of COB yesterday)			
	Total	Rec'd	Balance
PMT XFR	99	100	-1
Grounding XFR	7	7	0
4/0 Cable	588,000	652,693	-64,693
1000KM	396,000	406,689	-10,689
500KM	99,000	102,642	-3,642
12 Fiber SM	385,000	397,827	-12,827
1000 KCM (LVC)	37,000	35,175	1,825
Grounding XFR boxp	8	8	0
XFR Box Pads	100	100	0
Bases	99	40	59
Mids	99	39	60
Tops	99	48	51
Machine Heads	99	32	67
Contollers (DTA's)	99	48	51
Blade Sets	99	17	82
Hubs	99	39	60

General Construction Status

232 PU-08-32 Filed: 10/17/2008 Pages: 1
 Ashtabula Wind, Plan of the Day, Oct. 17, 2008

Ashtabula Wind, LLC

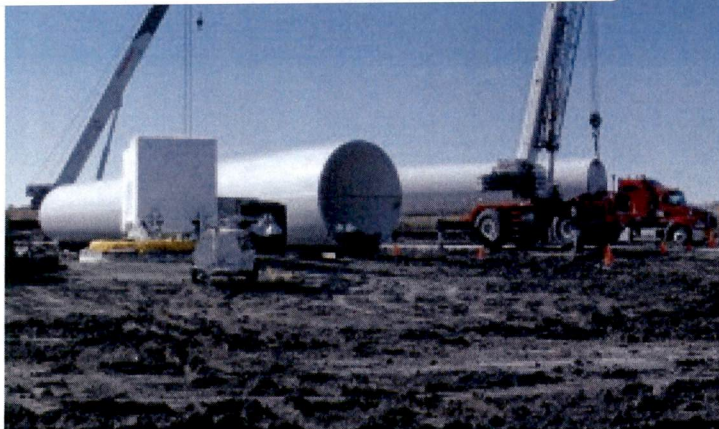

	Total	Complete	% Complete
Roads Subgraded LF	117,819	115,464	98.0%
Roads Complete LF	117,819	115,464	98.0%
Foundations Excavated	99	99	100.0%
Foundations Poured	99	99	100.0%
Foundations Backfilled	99	99	100.0%
Crane Pads Complete	99	92	92.9%
Tower Base Sections Erected	99	22	22.2%
Tower Mid Sections Erected	99	22	22.2%
Tower Top Sections Erected	99	7	7.1%
Machine Heads Installed	99	7	7.1%
Rotors Flown	99	6	6.1%
Mechanically Completed	99	0	0.0%
Pre-Commissioned	99	0	0.0%
Final Commissioned	99	0	0.0%
Cable Installed 4/0	586,473	483,978	82.5%
Cable Installed 1000 KM	435,303	348,219	80.0%
Cable Installed 500 KM	106,005	85,410	80.6%
Fiber-Optic 12 Fiber SM	385,000	281,186	73.0%
Transformers Set	99	83	83.8%
Transformers Terminated	99	38	38.4%
(as of COB yesterday)			

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE
