

**FPL ENERGY ASHTABULA WIND, LLC
LUVERNE, NORTH DAKOTA**

OTTER TAIL Plan of the Day (POD)

Weather Forecast: **Mostly Cloudy**
 High: **34°F** Low: **17°F**
 Winds: **ESE @ 4 mph**
 Precipitation Chances: **0%**

Monday, November 10, 2008

COD - 12/15/08

36 Days to COD

FPL Energy	Otter Tail	Blattner	GEWE
-------------------	-------------------	-----------------	-------------

Environmental:

- SWPPP inspection November 13th.
- Removing wetland markings
- Removing straw wattle
- Silt fence removal
- Monitor environmentally sensitive areas
- Environmental awareness to ALL crews

Safety:

- Check Back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Watch soft spots when off-loading trucks.
- Hunters are out, Stay visible

Civil:

- No work due to wet conditions

Erection:


- Continuing Precommission & Final Commission

Receiving (As of COB yesterday)			
	Total	Rec'd	Balance
PMT XFR	32	33	-1
Grounding XFR	2	2	0
4/0 Cable	147,000	150,560	-3,560
1000KM	91,446	94,500	-3,054
500KM	45,000	46,468	-1,468
12 Fiber SM	91,000	95,535	-4,535
1001 KCM (LVC)	12,500	12,500	0
Grounding XFR boxp	2	2	0
XFR Box Pads	32	32	0
Bases	32	32	0
Mids	32	32	0
Tops	32	32	0
Machine Heads	32	32	0
Contollers (DTA's)	32	32	0
Blade Sets	32	32	0
Hubs	32	32	0

General Construction Status

267 PU-08-32 Filed: 11/10/2008 Pages: 1
 Ashtabula Wind, Otter Tail, Plan of the Day, Nov. 10, 2008

Ashtabula Wind, LLC

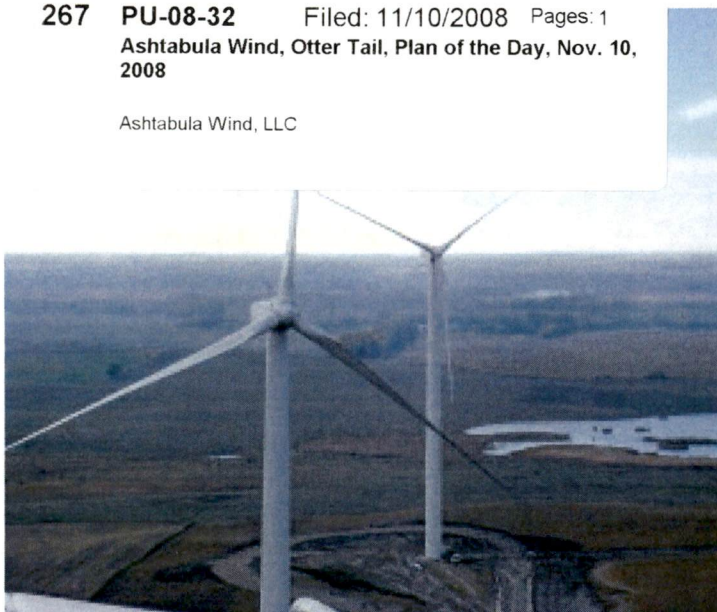

	Total	Complete	% Complete
Roads Subgraded	37,970	41,566	109.5%
Roads Complete	37,970	41,566	109.5%
Foundations Excavated	32	32	100.0%
Foundations Poured	32	32	100.0%
Foundations Backfilled	32	32	100.0%
Crane Pads Complete	32	32	100.0%
Tower Base Sections Erected	32	32	100.0%
Tower Mid Sections Erected	32	32	100.0%
Tower Top Sections Erected	32	32	100.0%
Machine Heads Installed	32	32	100.0%
Rotors Flown	32	32	100.0%
Mechanically Completed	32	32	100.0%
Pre-Commissioned	32	30	93.8%
Final Commissioned	32	29	90.6%
Cable Installed 4/0	127,188	124,602	98.0%
Cable Installed 1000 KM	58,311	77,964	133.7%
Cable Installed 500 KM	44,316	38,802	87.6%
Fiber-Optic 12 Fiber SM	91,000	87,146	95.8%
Transformers Set	32	32	100.0%
Transformers Terminated	32	32	100.0%
(as of COB yesterday)			
