

**FPL ENERGY ASHTABULA WIND, LLC
LIVERNE, NORTH DAKOTA**

Plan of the Day (POD)

Weather Forecast: **Mostly Cloudy**
High: 35 F Low: 23°F
Winds: SW @ 7 mph
Precipitation Chances: 0%

Saturday, November 15, 2008

COD - 12/31/08

47 Days to COD

FPL Energy	Otter Tail	Blattner	GEWE
------------	------------	----------	------

Environmental:

- SWPPP inspection suspended for winter
- Monitor environmentally sensitive areas
- Environmental awareness to ALL crews

Safety:

- Check back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Watch soft spots when off-loading trucks.
- Hunters are out, Stay visible.
- Watch for falling ice.

Civil:

- Offload tower sections, hubs & blades

Erection:

- Erect base & mid at AT94, AT104, AT127 & AT128
- Assemble rotor at AT103 & AT127
- Erect top & nacelle at AT102 & AT121
- Erect rotor at AT102, AT120 & AT121
- Mechanical completion pre walk at AT109 & AT110
- IIP at AT78, AT79, AT80 & AT81

Electrical:

- Electrical cabling & termination at AT88, AT90 & AT109


Receiving (As of COB yesterday)

	Total	Rec'd	Balance
PMT XFR	99	100	-1
Grounding XFR	7	7	0
4/0 Cable	588,000	652,693	-64,693
1000KM	396,000	406,689	-10,689
500KM	99,000	102,642	-3,642
12 Fiber SM	385,000	397,827	-12,827
1000 KCM (LVC)	37,000	35,175	1,825
Grounding XFR boxp	8	8	0
XFR Box Pads	100	100	0
Bases	99	89	10
Mids	99	90	9
Tops	99	91	8
Machine Heads	99	81	18
Contollers (DTA's)	99	99	0
Blade Sets	99	79	20
Hubs	99	87	12

General Construction Status

278 PU-08-32 Filed: 11/15/2008 Pages: 1
 Ashtabula Wind, Plan of the Day, Nov. 15, 2008

Ashtabula Wind, LLC

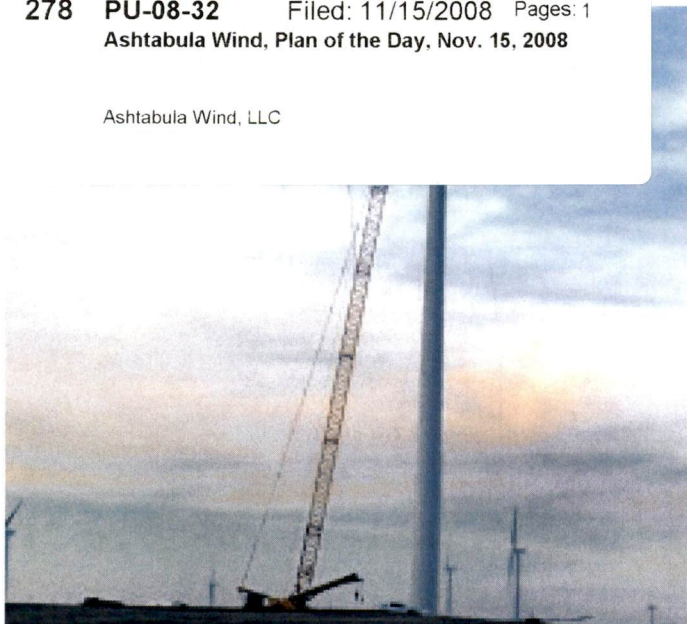

	Total	Complete	% Complete
Roads Subgraded LF	117,819	115,464	98.0%
Roads Complete LF	117,819	115,464	98.0%
Foundations Excavated	99	99	100.0%
Foundations Poured	99	99	100.0%
Foundations Backfilled	99	99	100.0%
Crane Pads Complete	99	99	100.0%
Tower Base Sections Erected	99	81	81.8%
Tower Mid Sections Erected	99	80	80.8%
Tower Top Sections Erected	99	72	72.7%
Machine Heads Installed	99	72	72.7%
Rotors Flown	99	71	71.7%
Mechanically Completed	99	45	45.5%
Pre-Commissioned	99	25	25.3%
Final Commissioned	99	3	3.0%
Cable Installed 4/0	586,473	520,686	88.8%
Cable Installed 1000 KM	435,303	348,219	80.0%
Cable Installed 500 KM	106,005	85,410	80.6%
Fiber-Optic 12 Fiber SM	385,000	310,345	80.6%
Transformers Set	99	99	100.0%
Transformers Terminated	99	92	92.9%
(as of COB yesterday)			

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE
