



**FPL ENERGY ASHTABULA WIND, LLC**  
**LUVERNE, NORTH DAKOTA**

*Plan of the Day (POD)*

Weather Forecast: Mostly Cloudy  
 High: 30 F Low: 13°F  
 Winds: S @ 9 mph  
 Precipitation Chances: 25%

**Friday, December 12, 2008**

**COD - 12/31/08**

**20 Days to COD**

<b>FPL Energy</b>	<b>Otter Tail</b>	<b>Blattner</b>	<b>GEWE</b>
-------------------	-------------------	-----------------	-------------

**Environmental:**

- SWPPP inspection suspended for winter
- Monitor environmentally sensitive areas
- Environmental awareness to ALL crews

**Safety:**

- Check back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Watch soft spots when off-loading trucks.
- Watch for falling ice.

**Erection:**


- Erect top, nacelle & rotor at AT108
- Electrical cabling & termination at AT108
- Mechanical completion pre-walk at AT108

Receiving (As of COB yesterday)			
	Total	Rec'd	Balance
PMT XFR	99	100	-1
Grounding XFR	7	7	0
4/0 Cable	588,000	652,693	-64,693
1000KM	396,000	406,689	-10,689
500KM	99,000	102,642	-3,642
12 Fiber SM	385,000	397,827	-12,827
1000 KCM (LVC)	37,000	35,175	1,825
Grounding XFR boxp	8	8	0
XFR Box Pads	100	100	0
Bases	99	99	0
Mids	99	99	0
Tops	99	99	0
Machine Heads	99	99	0
Contollers (DTA's)	99	99	0
Blade Sets	99	99	0
Hubs	99	99	0

**General Construction Status**

**301 PU-08-32** Filed: 12/12/2008 Pages: 1  
 Ashtabula Wind Plan of the Day, Dec. 12, 2008

Ashtabula Wind, LLC

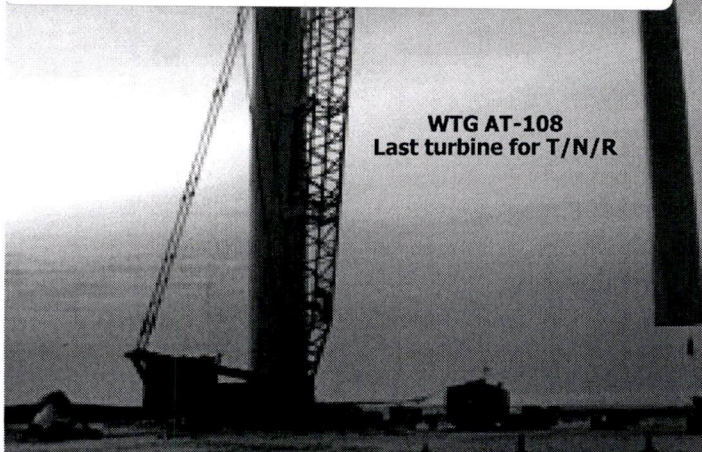

	Total	Complete	% Complete
Roads Subgraded LF	117,819	115,464	100.0%
Roads Complete LF	117,819	115,464	100.0%
Foundations Excavated	99	99	100.0%
Foundations Poured	99	99	100.0%
Foundations Backfilled	99	99	100.0%
Crane Pads Complete	99	99	100.0%
Tower Base Sections Erected	99	99	100.0%
Tower Mid Sections Erected	99	99	100.0%
Tower Top Sections Erected	99	98	99.0%
Machine Heads Installed	99	98	99.0%
Rotors Flown	99	98	99.0%
Mechanically Completed	99	98	99.0%
Pre-Commissioned	99	32	32.3%
Final Commissioned	99	93	93.9%
Cable Installed 4/0	586,473	520,686	100.0%
Cable Installed 1000 KM	435,303	348,219	100.0%
Cable Installed 500 KM	106,005	85,410	100.0%
Fiber-Optic 12 Fiber SM	385,000	310,345	100.0%
Transformers Set	99	99	100.0%
Transformers Terminated	99	99	100.0%
(as of COB yesterday)			
