

**FPL ENERGY ASHTABULA WIND, LLC
LUVERNE, NORTH DAKOTA**

Plan of the Day (POD)

Weather Forecast: **Mostly Cloudy**
 High: **-2 F** Low: **-12 F**
 Winds: **SSW @ 8 mph**
 Precipitation Chances: **3%**

Tuesday, December 16, 2008

COD - 12/31/08

16 Days to COD

FPL Energy	Otter Tail	Blattner	GEWE
------------	------------	----------	------

Environmental:

- SWPPP inspection suspended for winter
- Monitor environmentally sensitive areas
- Environmental awareness to ALL crews

Safety:

- Check back-up alarms daily and report.
- Observe speed limits.
- Wear all required PPE.
- Watch soft spots when off-loading trucks.
- Watch for falling ice.

Erection:

- Erect top, nacelle & rotor Complete
- Electrical cabling & termination Complete
- Mechanical completion pre-walk Complete
- **IIP at AT108**


Receiving (As of COB yesterday)

	Total	Rec'd	Balance
PMT XFR	99	100	-1
Grounding XFR	7	7	0
4/0 Cable	588,000	652,693	-64,693
1000KM	396,000	406,689	-10,689
500KM	99,000	102,642	-3,642
12 Fiber SM	385,000	397,827	-12,827
1000 KCM (LVC)	37,000	35,175	1,825
Grounding XFR boxp	8	8	0
XFR Box Pads	100	100	0
Bases	99	99	0
Mids	99	99	0
Tops	99	99	0
Machine Heads	99	99	0
Contollers (DTA's)	99	99	0
Blade Sets	99	99	0
Hubs	99	99	0

General Construction Status

302 PU-08-32 Filed: 12/16/2008 Pages: 1
 Ashtabula Wind Plan of the Day, Dec. 16, 2008

Ashtabula Wind, LLC

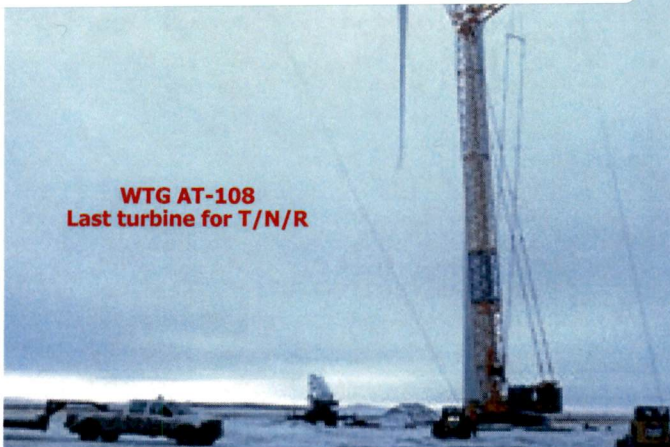

	Total	Complete	% Complete
Roads Subgraded LF	117,819	115,464	100.0%
Roads Complete LF	117,819	115,464	100.0%
Foundations Excavated	99	99	100.0%
Foundations Poured	99	99	100.0%
Foundations Backfilled	99	99	100.0%
Crane Pads Complete	99	99	100.0%
Tower Base Sections Erected	99	99	100.0%
Tower Mid Sections Erected	99	99	100.0%
Tower Top Sections Erected	99	99	100.0%
Machine Heads Installed	99	99	100.0%
Rotors Flown	99	99	100.0%
Mechanically Completed	99	98	99.0%
Pre-Commissioned	99	32	100.0%
Final Commissioned	99	93	93.9%
Cable Installed 4/0	586,473	520,686	100.0%
Cable Installed 1000 KM	435,303	348,219	100.0%
Cable Installed 500 KM	106,005	85,410	100.0%
Fiber-Optic 12 Fiber SM	385,000	310,345	100.0%
Transformers Set	99	99	100.0%
Transformers Terminated	99	99	100.0%
(as of COB yesterday)			

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE
