


PU-08-75

	Units Complete	% Complete
Access Roads	53	69%
Crane Pads	35	45%
Deliver Padmount	77	100%
Install Padmount	26	34%
Foundation Construction	58	75%
Delivery Turbine Components	37	48%
Set Base & Mid Tower Sections	11	14%
Grout & Bolt Tensioning	3	4%
Set Tower Top, Nacelle, Rotor	2	3%
Tower Wiring & Mech. Completion	0	0%




Prairie Winds 1 Project

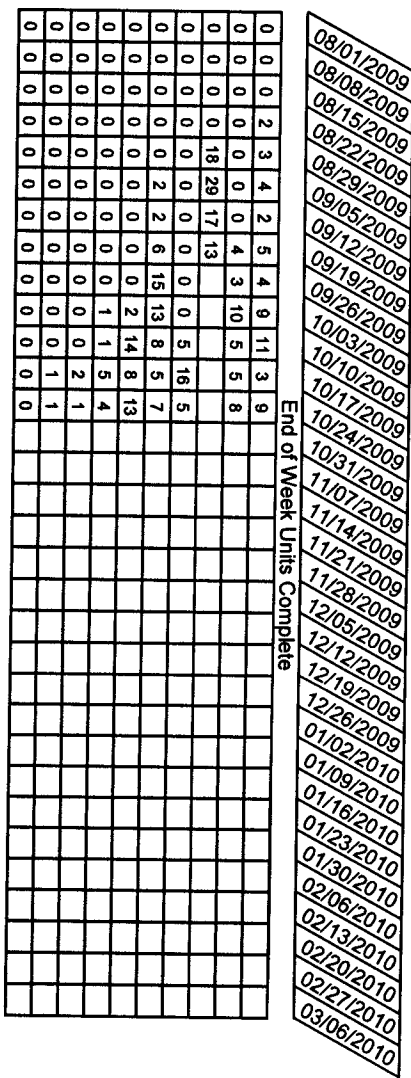


52
35
77
26
58
37
11
3
2
0

- Access Roads
- Crane Pads
- Deliver Padmount
- Install Padmount
- Foundation Construction
- Delivery Turbine Components
- Set Base & Mid Tower Sections
- Grout & Bolt Tensioning
- Set Tower Top, Nacelle, Rotor
- Tower Wiring & Mech. Completion

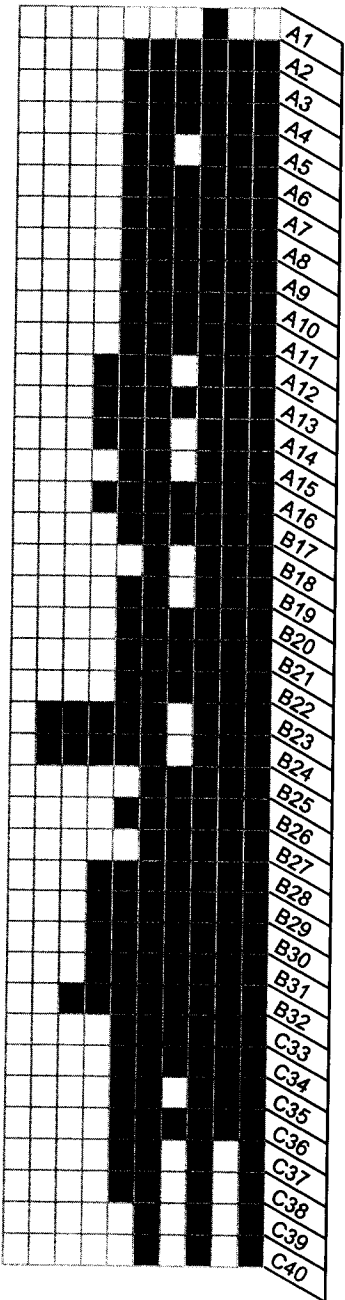

- Access Roads
- Crane Pads
- Deliver Padmount
- Install Padmount
- Foundation Construction
- Delivery Turbine Components
- Set Base & Mid Tower Sections
- Grout & Bolt Tensioning
- Set Tower Top, Nacelle, Rotor
- Tower Wiring & Mech. Completion

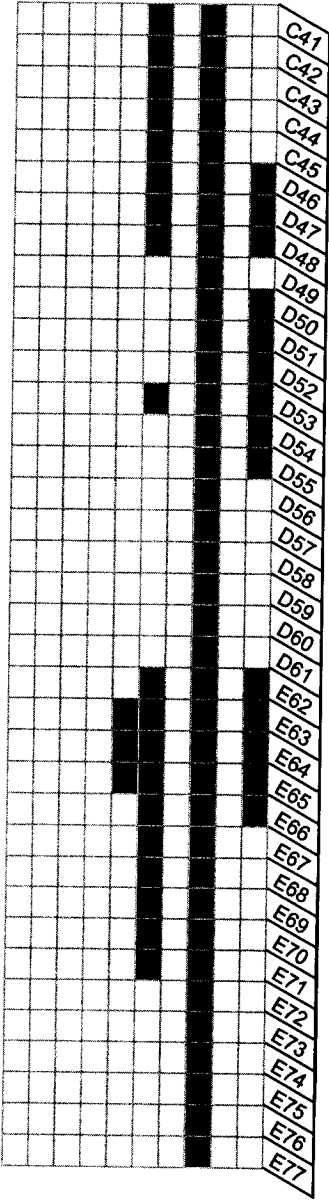

	Wind Connect Staffing	213	Subcontractor Staffing	49
Management	8		10	
Safety	3		11	
Civil	179		6	
Electrical	13		12	
Logistics / QA	10		7	
			3	

Complete Unit
