

PU-08-75

Units Complete
% Complete

Access Roads	67	87%
Crane Pads	48	62%
Deliver Padmount	77	100%
Install Padmount	48	62%
Foundation Construction	77	100%
Delivery Turbine Components	57	74%
Set Base & Mid Tower Sections	50	65%
Groat & Bolt Tensioning	25	32%
Set Tower Top, Nacelle, Rotor	21	27%
Tower Wiring & Mech. Completion	3	4%




Prairie Winds 1 Project


End of Week Units Complete	08/01/2009	08/08/2009	08/15/2009	08/22/2009	08/29/2009	09/05/2009	09/12/2009	09/19/2009	09/26/2009	10/03/2009	10/10/2009	10/17/2009	10/24/2009	10/31/2009	11/07/2009	11/14/2009	11/21/2009	11/28/2009	12/05/2009	12/12/2009	12/19/2009	12/26/2009	01/02/2010	01/09/2010	01/16/2010	01/23/2010	01/30/2010	02/06/2010	02/13/2010	02/20/2010	02/27/2010	03/06/2010			
A1	0	0	0	2	3	4	2	5	4	9	11	3	9	10	5																				
A2	0	0	0	0	0	0	0	4	3	10	5	5	8	7	6																				
A3	0	0	0	0	18	29	17	13																											
A4	0	0	0	0	0	0	0	0	0	5	16	5	6	16																					
A5	0	0	0	0	0	2	2	6	15	13	8	5	7	19																					
A6	0	0	0	0	0	0	0	0	2	14	8	13	9	11																					
A7	0	0	0	0	0	0	0	0	1	5	4	16	23																						
A8	0	0	0	0	0	0	0	0	0	0	2	1	13	9																					
A9	0	0	0	0	0	0	0	0	0	0	1	1	9	10																					
A10	0	0	0	0	0	0	0	0	0	0	0	0	0	0	3																				
A11																																			
A12																																			
A13																																			
A14																																			
A15																																			
A16																																			
A17																																			
A18																																			
A19																																			
A20																																			
A21																																			
A22																																			
A23																																			
A24																																			
A25																																			
A26																																			
A27																																			
A28																																			
A29																																			
A30																																			
A31																																			
A32																																			
A33																																			
A34																																			
A35																																			
A36																																			
A37																																			
A38																																			
A39																																			
A40																																			

67
48
77
48
57
50
25
21
3

- Access Roads
- Crane Pads
- Deliver Padmount
- Install Padmount
- Foundation Construction
- Delivery Turbine Components
- Set Base & Mid Tower Sections
- Groat & Bolt Tensioning
- Set Tower Top, Nacelle, Rotor
- Tower Wiring & Mech. Completion

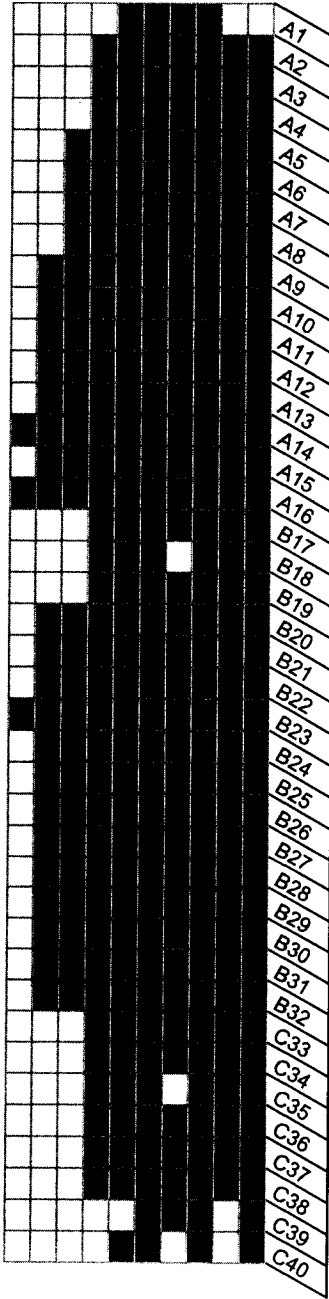

- Access Roads
- Crane Pads
- Deliver Padmount
- Install Padmount
- Foundation Construction
- Delivery Turbine Components
- Set Base & Mid Tower Sections
- Groat & Bolt Tensioning
- Set Tower Top, Nacelle, Rotor
- Tower Wiring & Mech. Completion

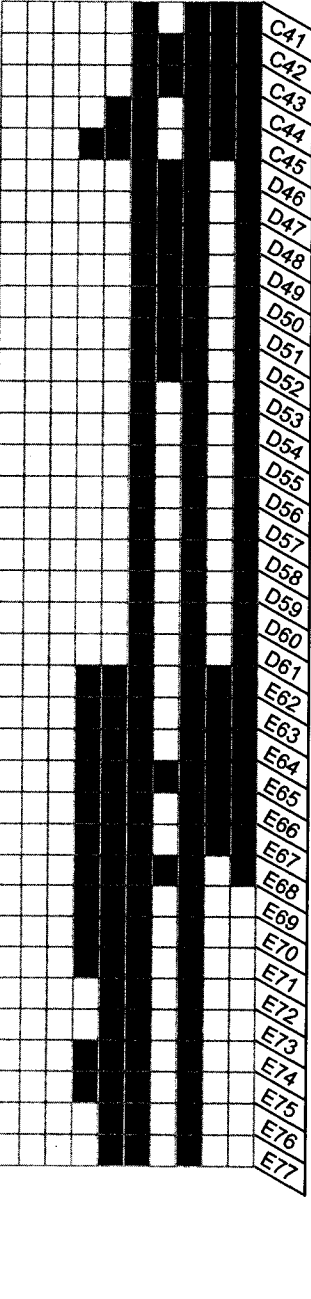

Wind Connect Staffing	213	Subcontractor Staffing	52
Management	8	Building Dimensions Inc.	11
Safety	3	L & H Utility Contractors Inc.	16
Civil	179	World Wind Services Inc.	11
Electrical	13	Timberline	7
Logistics / QA	10	Great Western Erectors (rebar)	4
		Brundage Bone Concrete Pumping	3

Complete Unit
