

## Hamre, John G.

---

**From:** Fahn, Patrick J.  
**Sent:** Monday, January 19, 2009 10:18 AM  
**To:** Hamre, John G.  
**Subject:** FW: PU-07-791 and PU-08-812- Weekly reports  
**Attachments:** PSC Report PU-08-812 (ejk 9-Jan-09).doc; PSC Report PU-07-791 (ejk 9-Jan-09).doc; Beaver Lodge tub ring #3.jpg; Beaver Lodge tub ring #4.jpg; Beaver Lodge tub ring #5.jpg; Beaver Lodge tub ring #6.jpg; DSC02547.jpg; DSC02544.jpg; DSC02546.jpg

John – please docket in 07-791 and 08-812 from Enbridge and then forward to Commissioners, PUD, and Legal. This one should have been docketed before the other email I sent this morning.

### Patrick Fahn

Utility Analyst  
Email: [pfahn@nd.gov](mailto:pfahn@nd.gov)  
Phone: (701) 328-4077

North Dakota Public Service Commission  
600 E Boulevard  
Bismarck ND 58505-0480  
Fax: (701) 328-2410

---

**From:** Ed Kelly [<mailto:Ed.Kelly@rooney-eng.com>]  
**Sent:** Friday, January 09, 2009 2:19 PM  
**To:** Fahn, Patrick J.  
**Cc:** 'Brent.Horton@enbridge.com'; Troy D. Pierantoni; 'Trent\_Mattick@Enbridge.com'; Tim Kinney; Ty France; Paul Giron; Casper Front Desk; 'Jessica.Faith@enbridge.com'; 'Steve Schmaltz'; 'Tony Kueffler'; 'Gary Blowers'; 'Kevin Gault'; 'Adam Cole'  
**Subject:** RE: PU-07-791 and PU-08-812- Weekly reports

Weekly report for Jan. 9 along with pictures.

Let me know if you have any questions or comments.

Thanks,

**Edward J. Kelly, P.E.**

Project Manager

### ROONEY ENGINEERING, INC.

Engineering for the Energy Industry

12201 E. Arapahoe Rd., Ste. C-10  
Centennial, CO 80112  
Office: 303-705-9325  
Cell: 303-594-6157  
Fax: 303-792-0227

29 **PU-08-812** Filed: 1/9/2009 Pages: 12  
**Enbridge Pipeline Weekly Report for week of Jan. 09, 2009**

Enbridge Pipelines (North Dakota) LLC

Edward Kelly, Project Mgr.

1

82 **PU-07-791** Filed: 1/9/2009 Pages: 12  
**Enbridge Pipeline Weekly Report for week of Jan. 09, 2009**

Enbridge Pipelines (North Dakota) LLC

Edward Kelly, Project Mgr.



**ROONEY ENGINEERING,  
INC.**  
Engineering for the Energy  
Industry



**Weekly Construction Progress Report**

**Enbridge Pipelines (North Dakota) LLC**

**Week of: Jan. 9, 2009**

**Case No. PU-08-812**

	Name	Company	Office	Cell
<b>Supervising Project Manager</b>	Edward Kelly	Rooney Engineering	303-705-9325	303-594-6157
<b>Supervisor - Construction Services:</b>	Trent Mattick	Enbridge	701-857-0803	701-721-3356

**Brief Description of Weekly Activities:**

**Stanley Injection**

- Work continues on foundations but slow progress with weather. Fabrication work for mechanical started.

**Specific Activity on Project**

Description	% Complete	Description	% Complete
<b>Stanley Station</b>			
Civil	5		
Mechanical	5		
Electrical	0		
Clean-up	0		

**Significant Work Activity for next week:**

**Stanley Station**

- Foundation work to continue as weather allows. Prefabrication work to continue.

**Comments:**

Name	Date
Edward J. Kelly 	1/9/09



**ROONEY ENGINEERING,  
INC.**  
Engineering for the Energy  
Industry



**Weekly Construction Progress Report**

**Enbridge Pipelines (North Dakota) LLC**

**Week of: Jan. 9, 2009**

**Case No. PU-07-791**

	Name	Company	Office	Cell
<b>Supervising Project Manager</b>	Edward Kelly	Rooney Engineering	303-705-9325	303-594-6157
<b>Supervisor - Construction Services:</b>	Trent Mattick	Enbridge	701-857-0803	701-721-3356

**Brief Description of Weekly Activities:**

**Alexander Station**

- Nothing to report.

**Trenton Station**

- Nothing to report.

**Beaver Lodge Station**

- Installed Tub ring.

**Stanley Station**

- Prefabrication of piping complete.

**Blaisdell Station**

- Nothing to report.

**Minot Station**

- Continued shop fabrication of mechanical. Fabrication and painting of cable tray supports underway.

**Denbigh Station**

- Nothing to report – 2008 work complete.

**Pleasant Lake Station**

- Nothing to report – 2008 work complete.

**Penn Station**

- Nothing to report – 2008 work complete.

**Bartlett Station**

- Nothing to report – 2008 work complete.

**Larimore Station**

- Nothing to report – 2008 work complete.

<b>Specific Activity on Project</b>			
<b>Description</b>	<b>% Complete</b>	<b>Description</b>	<b>% Complete</b>
<b>Alexander Station</b>		<b>Trenton Station</b>	
Civil	0	Civil	0
Mechanical	0	Mechanical	0
Electrical	0	Electrical	0
Clean-up	0	Clean-up	0
<b>Beaver Lodge Station</b>		<b>Stanley Station</b>	
Civil	35	Civil	35
Mechanical	8	Mechanical	45
Electrical	0	Electrical	0
Clean-up	0	Clean-up	0
<b>Blaisdell Station</b>		<b>Minot Station</b>	
Civil	0	Civil	60
Mechanical	0	Mechanical	30
Electrical	0	Electrical	0
Clean-up	0	Clean-up	0
<b>Denbigh Station</b>		<b>Pleasant Lake Station</b>	
Civil	80	Civil	70
Mechanical	0	Mechanical	60
Electrical	0	Electrical	45
Clean-up	0	Clean-up	0
<b>Penn Station</b>		<b>Bartlett Lake Station</b>	
Civil	70	Civil	60
Mechanical	45	Mechanical	0
Electrical	0	Electrical	0
Clean-up	0	Clean-up	0
<b>Larimore Station</b>			
Civil	70		
Mechanical	45		
Electrical	30		
Clean-up	0		

<b>Significant Work Activity for next week:</b>
<p><b>Alexander Station</b></p> <ul style="list-style-type: none"> <li>• Nothing to report.</li> </ul> <p><b>Trenton Station</b></p> <ul style="list-style-type: none"> <li>• Nothing to report.</li> </ul> <p><b>Beaver Lodge Station</b></p> <ul style="list-style-type: none"> <li>• Welding for steel floor work and tub ring to continue. Then the plan is to demob until spring.</li> </ul> <p><b>Stanley Station</b></p> <ul style="list-style-type: none"> <li>• Nothing to report. Field work on hold until weather breaks.</li> </ul> <p><b>Blaisdell Station</b></p> <ul style="list-style-type: none"> <li>• Nothing to report.</li> </ul> <p><b>Minot Station</b></p> <ul style="list-style-type: none"> <li>• Continue shop fabrication. Field install cable tray supports.</li> </ul> <p><b>Denbigh Station</b></p> <ul style="list-style-type: none"> <li>• Nothing to report.</li> </ul> <p><b>Pleasant Lake Station</b></p> <ul style="list-style-type: none"> <li>• Nothing to report.</li> </ul>

**Penn Station**

- Nothing to report.

**Bartlett Station**

- Nothing to report.

**Larimore Station**


- Nothing to report.

**Comments:**

**Name**

**Date**

Edward J. Kelly



1/9/09










DATE: 01-06-09

NOSE / PHASE 6 / STANLEY STATION

AFF: 0790401121

FILL HEADER PIER SUPPORTS

INSPECTOR: PAUL STEEN

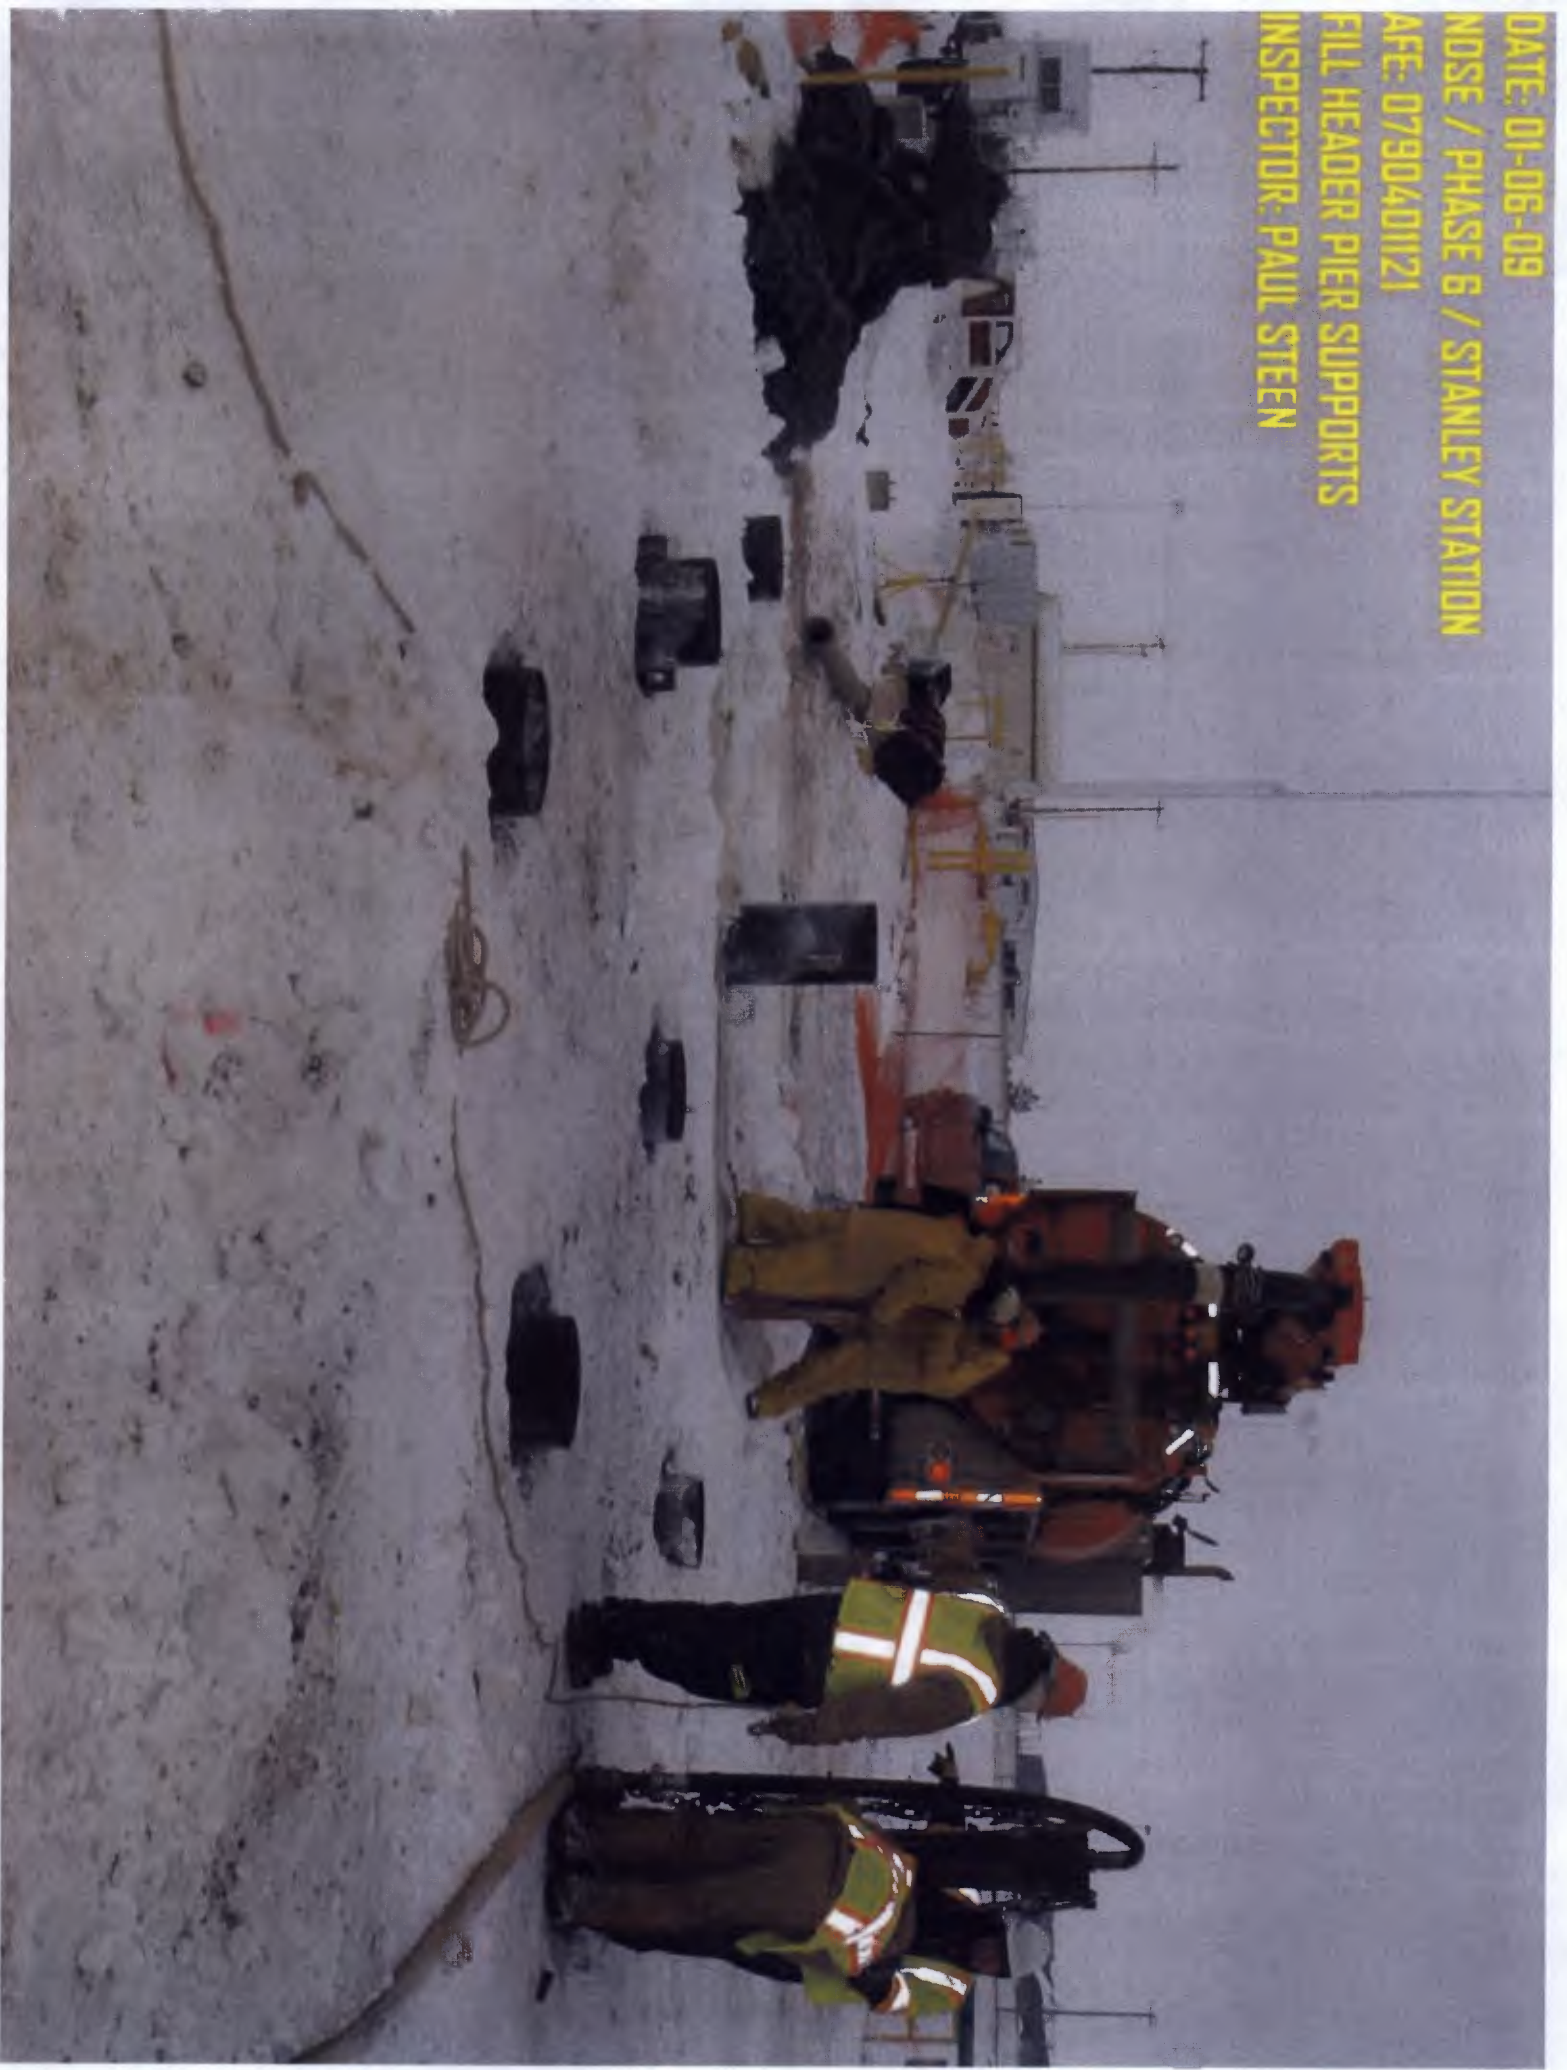


DATE: 01-06-09

NDSE / PHASE 6 / STANLEY STATION

AFF: 0790401121

HYDRD-EXCAVATION OF FILL HEADER PIER SUPPORTS

INSPECTOR: PAUL STEEN

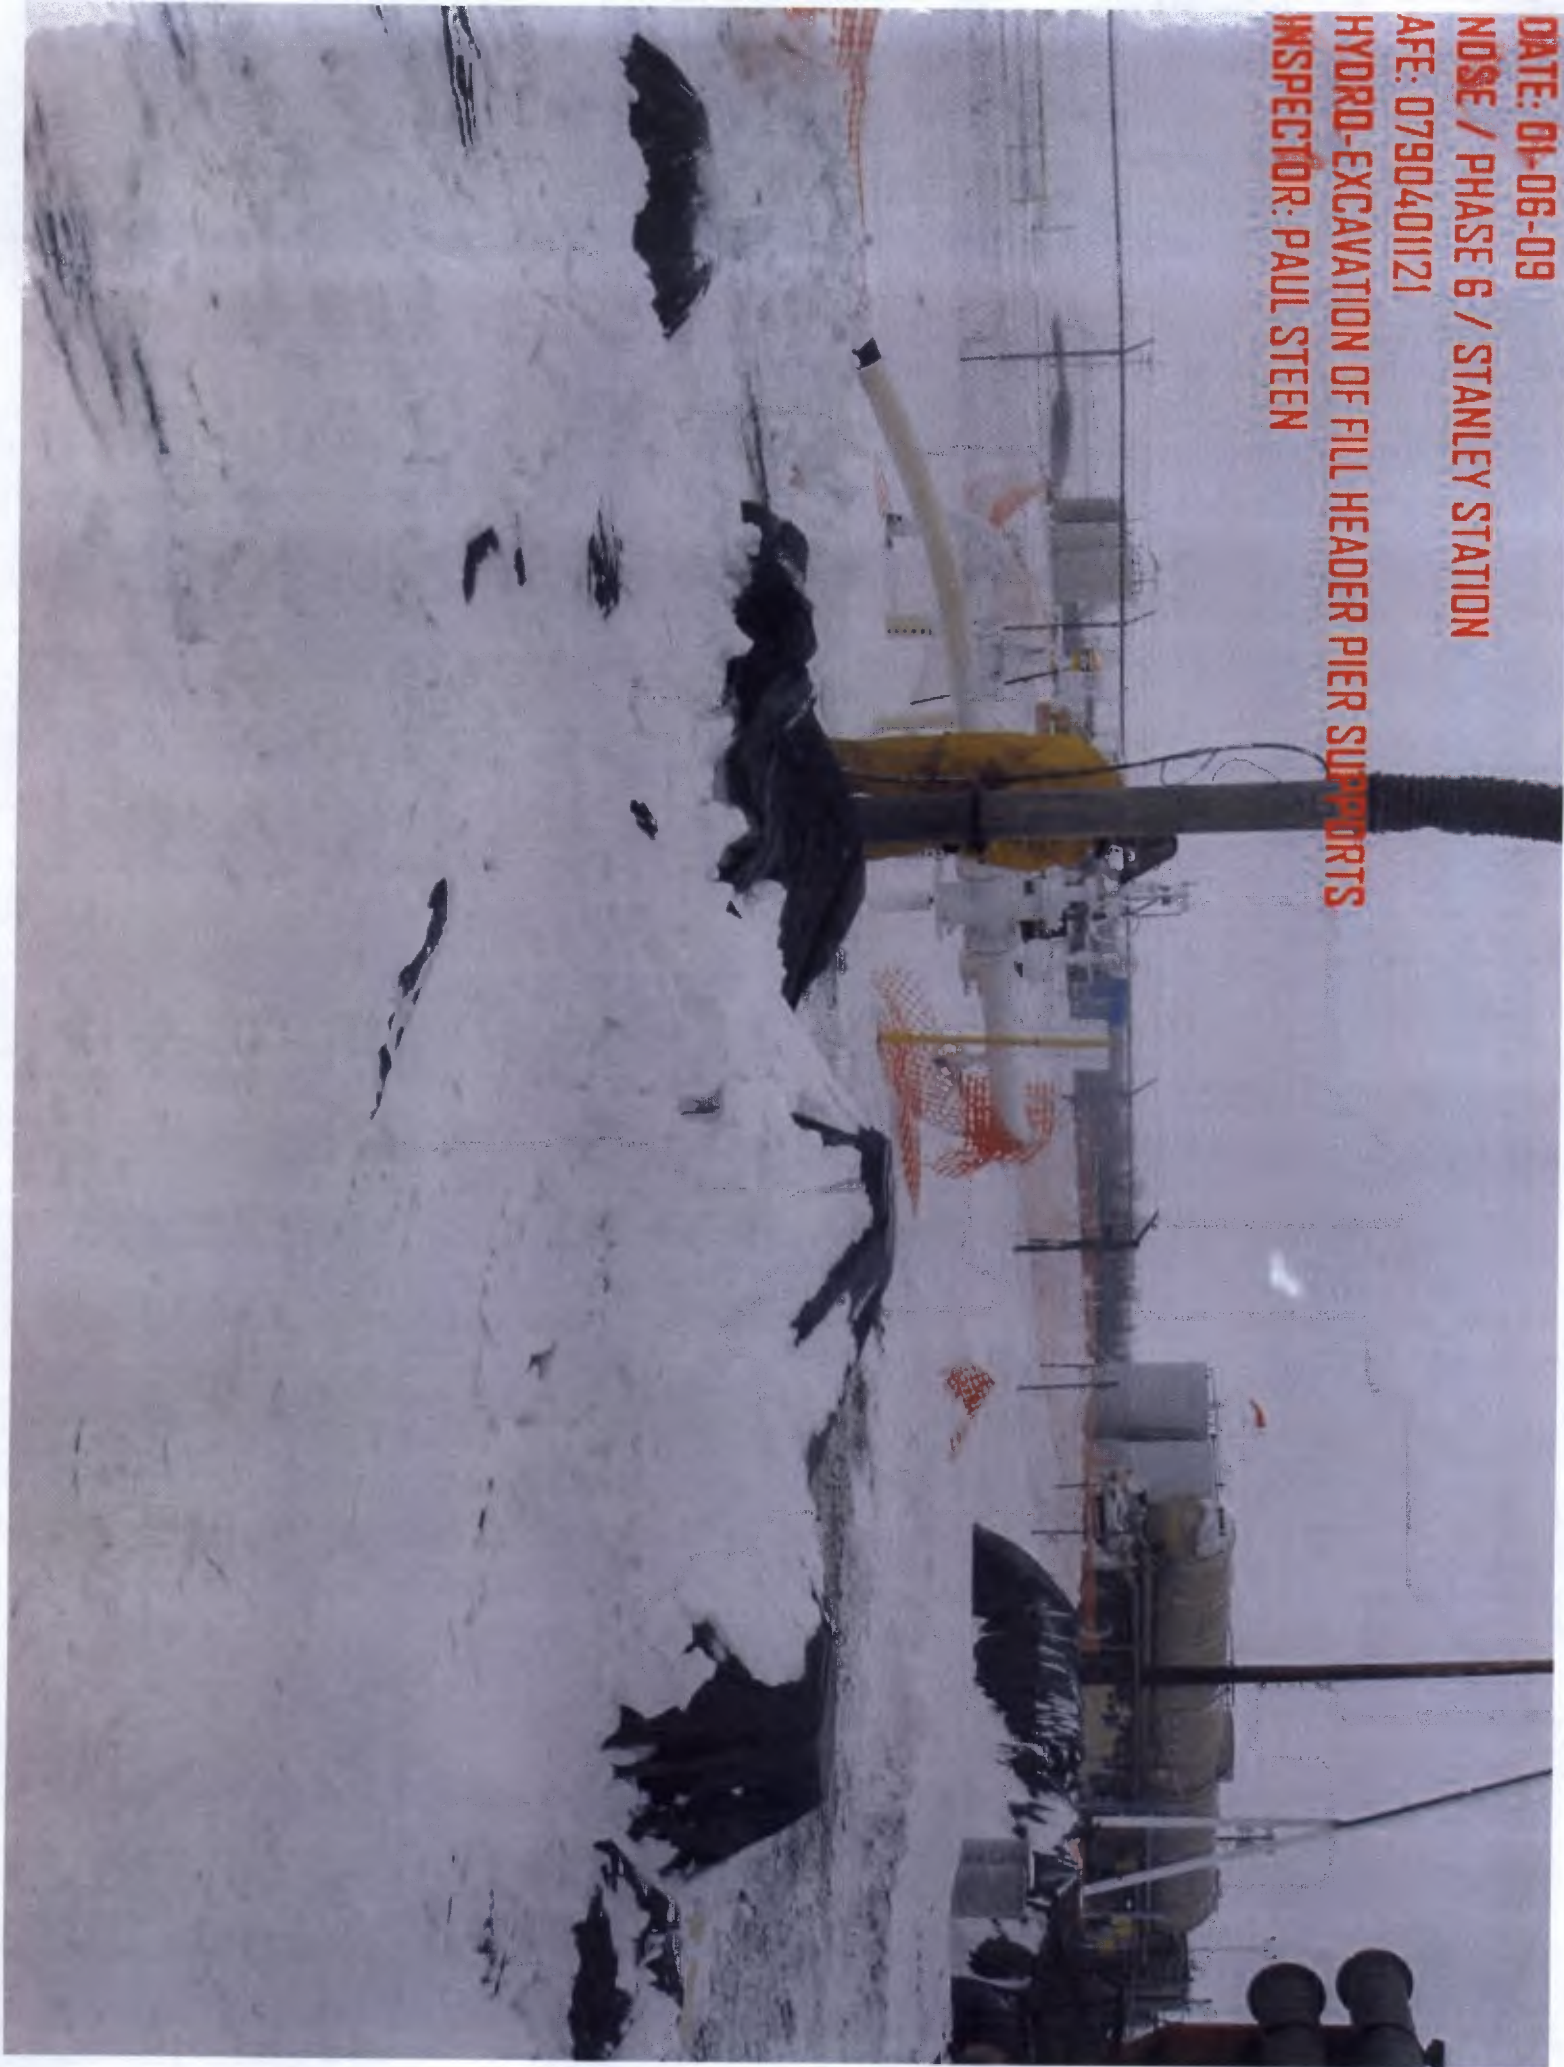

DATE: 01-06-09  
NOSE / PHASE B / STANLEY STATION  
AFE: 0790401121  
DRIVING OF CASINGS TO FILL HEADER  
INSPECTOR: PAUL STEEN

