



**Luverne Wind Farm
Transmission Line Construction
Plan of the Week (POW)**


Week of July 20th- 24th, 2009

Otter Tail Power Company

Activities:

- **Safety/Environmental:**
None.
- **Lay down Yard:**
None.
- **Electrical/Construction:**
None.
- **Potential Schedule Delays:**
None.
- **Plan for the week:**
Finish stringing the Conductor and Fiber into the two substations. Aevenia will be here this week to complete the splicing of the OPGW.

General Information and Announcements

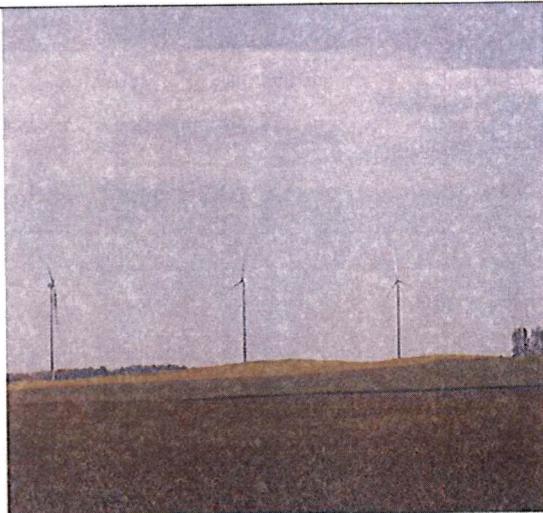

Work In Progress

	Total	Complete	Remaining	% Complete
Poles Framed	87	87	0	100%
Poles Set	87	87	0	100%
Conductor Strung	12	11.5	.5	96%
Conductor Sagged	12	11.5	.5	96%
Conductor Clipped	12	11.5	.5	96%
Fiber Strung	12	11.5	.5	96%
Fiber Sagged	12	11.5	.5	96%
Fiber Clipped	12	11.5	.5	96%
