



**Luverne Wind Farm
Transmission Line Construction
Plan of the Week (POW)**


Week of August 3rd- 7th, 2009

Otter Tail Power Company

Activities:

- **Safety/Environmental:**
None.
- **Lay down Yard:**
None.
- **Electrical/Construction:**
None.
- **Potential Schedule Delays:**
None.
- **Plan for the week:**
Change of schedule for Aevenia and they will be here early next week.

General Information and Announcements

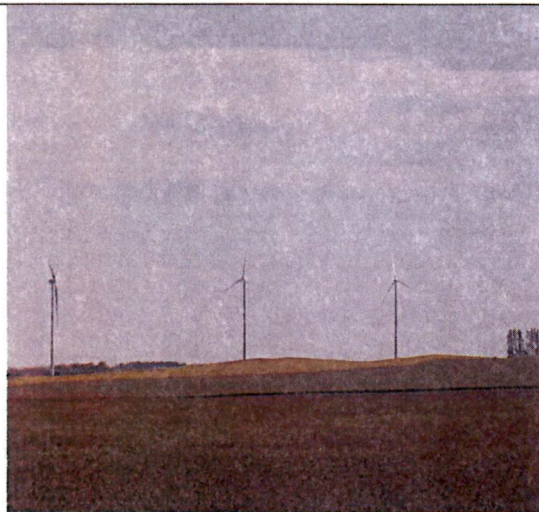

Work In Progress

	Total	Complete	Remaining	% Complete
Poles Framed	87	87	0	100%
Poles Set	87	87	0	100%
Conductor Strung	12	12	0	100%
Conductor Sagged	12	12	0	100%
Conductor Clipped	12	12	0	100%
Fiber Strung	12	12	0	100%
Fiber Sagged	12	12	0	100%
Fiber Clipped	12	12	0	100%
