



**Luverne Wind Farm
Transmission Line Construction
Plan of the Week (POW)**


Week of August 10th – 14th, 2009

Otter Tail Power Company

Activities:

- **Safety/Environmental:**
None.
- **Lay down Yard:**
None.
- **Electrical/Construction:**
None.
- **Potential Schedule Delays:**
None.
- **Plan for the week:**
T-Line fiber was spliced and tested from Pillsbury to Luverne by Aevenia. Bird diverters will be completed next week. Storm Water Permit will be terminated next week.

General Information and Announcements

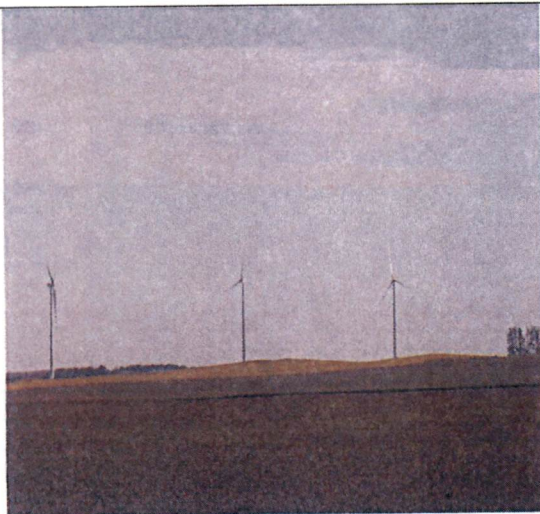

Work In Progress

	Total	Complete	Remaining	% Complete
Poles Framed	87	87	0	100%
Poles Set	87	87	0	100%
Conductor Strung	12	12	0	100%
Conductor Sagged	12	12	0	100%
Conductor Clipped	12	12	0	100%
Fiber Strung	12	12	0	100%
Fiber Sagged	12	12	0	100%
Fiber Clipped	12	12	0	100%
