



**Luverne Wind Farm
Transmission Line Construction
Final Plan of the Week (POW)**

Weeks of August 17th – 28th, 2009

Otter Tail Power Company




Activities:

- **Safety/Environmental:**
None.
- **Lay down Yard:**
None.
- **Electrical/Construction:**
None.
- **Potential Schedule Delays:**
None.
- **Plan for the week:**
Bird diverters were installed. Line was tested on August 20th and energized on August 25th.

Comments: This will be the last report as the project has been completed, please contact us if additional information is required pertaining to the construction phase of the Luverne Transmission Line.

General Information and Announcements

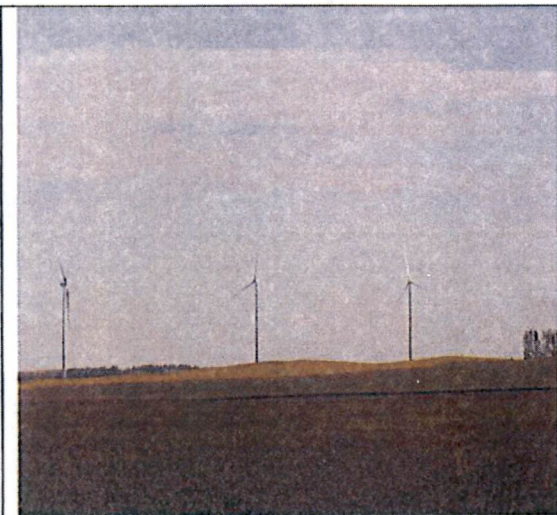

Work In Progress

	Total	Complete	Remaining	% Complete
Poles Framed	87	87	0	100%
Poles Set	87	87	0	100%
Conductor Strung	12	12	0	100%
Conductor Sagged	12	12	0	100%
Conductor Clipped	12	12	0	100%
Fiber Strung	12	12	0	100%
Fiber Sagged	12	12	0	100%
Fiber Clipped	12	12	0	100%

Bauske, Shelly A.

From: KBurgau@otpc.com
Sent: Thursday, September 10, 2009 1:32 PM
To: 'jlein@nd.gov'; 'ndpsc@nd.gov'
Cc: HMcMahon@otpc.com; WPreston@otpc.com; TLangston@otpc.com; RSynstelien@otpc.com; 'DeeDee.Olson@fpl.com'; 'aseydel@icsgf.com'; TWahlund@otpc.com; CKuismi@otpc.com; JSmestad@ottertail.com; Dick.Rausch@nexteraenergy.com; PRossow@otpc.com
Subject: PU-09-388/PU-09-407/POW August 17 - August 28, 2009
Attachments: POW SUB WE 82809.pdf; POW TLine WE 82809.pdf

Jerry,

Attached are the Final weekly construction activities as requested per #9 of Order PU-08-34/PU-09-73/PU-09-407 and #6 of Order PU-08-107/PU-09-136/PU-09-388.

Sorry for the delay, the substation was energized on the 25th and final commissioning on the last turbine was Sept. 5th.

If you have any questions, please do not hesitate to call or email.

Sincerely,
Kathryn Burgau
Contracts and Due Diligence Administrator
Otter Tail Power Company - On for you !

kburgau@otpc.com
218.731.9096 Cell
218.739.8763 Direct
218.739.8218 Fax
