



**NextEra™ Energy Resources
Ashtabula Wind II**

NEXTerA Energy

Plan of the Day (POD)



Date: Saturday, 7/25/2009
High: 80
Precipitation Chances: 0%

COD: 10-31-09
Low: 56

Days to COD: 99
Winds: NW @ 8 mph
Weather Forecast: Sunny

NextEra™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- **The corn stalk is beginning to impair vision, be cautious at intersections**
- **Wear proper PPE while on the job site**
- **Use correct procedure when offloading any material**
- **Keep your speed to a minimum**
- **SWPPP inspection every two weeks**

Civil/Erection:

- **Subgrade at 166-169 & 232-235**
- **Approach at 167**
- **Foundations:**
- **Excavation at 232 & 233**
- **Mud mat at 232-234**
- **Install bottom rebar mat at 211-213**
- **Install anchor bolts at 212-213**
- **Install top rebar mat at 215-216**
- **Form base at 192, 193 & 216**
- **Pour base at 180 & 194**
- **Form pedestal at 183 & 184**
- **Pour pedestal at 181 & 182**
- **Backfill at 197-198**
- **Build crane pads at 197-198**

Electrical:

- **Pedestal conduit at 183 & 184**
- **Smurf tube at 193 & 194**


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	257,812	183,188
500 KCM	36,000	27,755	8,245
Copperdad	84,000	84,579	-579
1000 KCM	333,000	320,837	12,163
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	34,585	117,188	29.5%
Gravel Roads (6")	30,135	117,188	25.7%
Roads Complete	22,688	117,188	19.4%
Silt Fence Installed	12,308	17,700	69.5%
Foundations Excavated	28	80	35.0%
Foundations Poured	12	80	15.0%
Foundations Backfilled	3	80	3.8%
Crane Pads Completed	2	80	2.5%
Tower Base Sections Erected	0	80	0.0%
Tower Mid Sections Erected	0	80	0.0%
Tower Top Sections Erected	0	80	0.0%
Nacelles Installed	0	80	0.0%
Rotors Installed	0	80	0.0%
Tower Wiring Complete	0	80	0.0%
Mechanically Complete	0	80	0.0%
Final Commissioned	0	80	0.0%
4/0 Cable Trenched	0	441,000	0.0%
500 Cable Trenched	0	36,000	0.0%
1000 Cable Trenched	0	333,000	0.0%
Copperdad	0	84,000	0.0%
1000 Low Voltage Trenched	0	30,500	0.0%
Fiber Optic 12 Fiber SM	0	270,000	0.0%
Transformers Set/Terminated	0	80	0.0%

(as of COB yesterday)

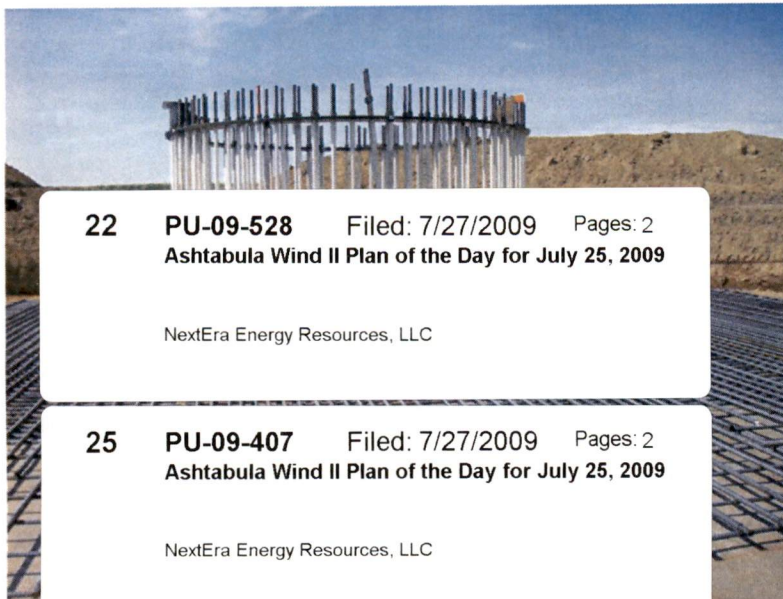

22 PU-09-528 Filed: 7/27/2009 Pages: 2
 Ashtabula Wind II Plan of the Day for July 25, 2009


NextEra Energy Resources, LLC

25 PU-09-407 Filed: 7/27/2009 Pages: 2
 Ashtabula Wind II Plan of the Day for July 25, 2009

NextEra Energy Resources, LLC



NextEra™ Energy Resources Ashtabula Wind II



Otter Tail

Plan of the Day (POD)

Date: Saturday, 7/25/2009
High: 80
Precipitation Chances: 0%

COD: 10-15-09
Low: 56

Days to COD: 83
Winds: NW @ 8 mph
Weather Forecast: Sunny

NextEra™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- **The corn stalk is beginning to impair vision, be cautious at intersections**
- **Wear proper PPE while on the job site**
- **Make sure not to use any equipment if it is tagged out**
- **Keep your speed to a minimum**
- **SWPPP inspection every two weeks**

Civil/Erection:

Erection:

- **Assemble rotor at 135**
- **Erect top, nacelle & rotor at 132**

Collections:

•

Electrical:

- **Grounding grid testing**
- **Controller termination at 143-145**
- **Install box pad at 152-154 & 158**
- **Low voltage cable termination install wire at 139-146**
- **Boring at 4th circuit sub bore**

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	129,912	59,088
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	6	27
Controllers	33	8	25
Bases	33	5	28
Mids	33	5	28
Tops	33	5	28
Nacelles	33	6	27
Hubs	33	8	25
Blade Sets	33	5	28

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	49,614	83.1%
Gravel Road (6")	41,232	49,614	83.1%
Roads Complete	41,232	49,614	83.1%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	29	33	87.9%
Crane Pads Completed	23	33	69.7%
Tower Base Sections Erected	4	33	12.1%
Tower Mid Sections Erected	4	33	12.1%
Tower Top Sections Erected	0	33	0.0%
Nacelles Installed	0	33	0.0%
Rotors Installed	0	33	0.0%
Tower Wiring Complete	0	33	0.0%
Mechanically Complete	0	33	0.0%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	35,455	189,000	18.8%
500 Cable Trenched	17,295	117,000	14.8%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set/Terminated	15	33	45.5%
(as of COB yesterday)			

