



# NEXTer<sup>TM</sup> Energy Resources Ashtabula Wind II



## Otter Tail

### Plan of the Day (POD)

**Date:** Tuesday, 8/25/2009  
**High:** 81  
**Precipitation Chances:** 0%

**COD:** 10-15-09  
**Low:** 51

**Days to COD:** 52  
**Winds:** WNW @ 4 mph  
**Weather Forecast:** Partly Sunny


NEXTer <sup>TM</sup> Energy Resources	Otter Tail	Blattner Energy	GE
---------------------------------------	------------	-----------------	----

**Safety/Environmental:**

- Most falls are preventable, take precautions to avoid
- Keep your speed to a minimum
- Watch out for blind corners in areas where corn is growing
- SWPPP inspection every two weeks

**Erection:**

- Erect top nacelle & rotor at 148-149
- Collections:
- Electrical:
- Fiber termination testing 2N
- Tower wiring at 150
- Mechanical completion pre-walk at 153-154
- IIP at 162
- GE Pre-Commissioning at 140, 141 & 146

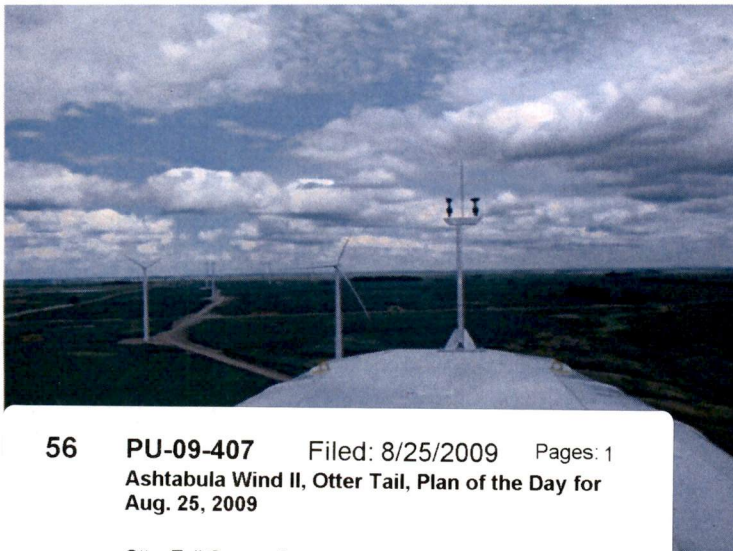

56 PU-09-407 Filed: 8/25/2009 Pages: 1  
 Ashtabula Wind II, Otter Tail, Plan of the Day for  
 Aug. 25, 2009

Otter Tail Corporation

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	33	0
Grounding XFR	3	3	0
4/0 Cable	189,000	195,397	-6,397
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	33	0
Bases	33	33	0
Mids	33	33	0
Tops	33	33	0
Nacelles	33	33	0
Hubs	33	33	0
Blade Sets	33	33	0

Negative Number Indicates Overage of Cable

General Construction Status			
	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	33	33	100.0%
Crane Pads Completed	33	33	100.0%
Tower Base Sections Erected	33	33	100.0%
Tower Mid Sections Erected	33	33	100.0%
Tower Top Sections Erected	27	33	81.8%
Nacelles Installed	27	33	81.8%
Rotors Installed	26	33	78.8%
Tower Wiring Complete	26	33	78.8%
Mechanically Complete	21	33	63.6%
Pre-Commissioned	12	33	36.4%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	179,188	189,000	94.8%
500 Cable Trenched	100,122	117,000	85.6%
1000 Low Voltage Installed	12,750	12,750	100.0%
Fiber Optic 12 Fiber SM	97,000	97,000	100.0%
Transformers Set	33	33	100.0%

(as of COB yesterday)
