




NextEra™ Energy Resources Ashtabula Wind II

NEXTERA Energy

Plan of the Day (POD)



Date: Thursday, 7/16/2009
High: 72
Precipitation Chances: 2%

COD: 10-31-09
Low: 45

Days to COD: 108
Winds: WNW @ 11 mph
Weather Forecast: Cloudy

NextEra™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Wear proper PPE while on the job site
- Use correct procedure when offloading any material
- Keep your speed to a minimum
- Traffic congestion in the north laydown yard, use caution and make sure to have a spotter
- SWPPP inspection
- Wetland markings

Civil/Erection:

- Subgrade at 179-183, & 192-194
- Gravel at 184-187
- Approach at 192

Foundations:

- Excavation on foundation at 185-187
- Mud mat at 185-187
- Install bottom rebar mat at 198-199
- Install anchor bolts at 196-198
- Install top rebar mat at 195-197
- Form base at 195-197

Collection:

Electrical:


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	257,812	183,188
500 KCM	36,000	27,755	8,245
Copperclad	84,000	0	84,000
1000 KCM	333,000	274,970	58,030
12 Fiber SM FOC	270,000	135,000	135,000
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	12,375	117,188	10.6%
Gravel Roads (6")	8,525	117,188	7.3%
Roads Complete	7,025	117,188	6.0%
Silt Fence Installed	5,219	17,700	29.5%
Foundations Excavated	7	80	8.8%
Foundations Poured	0	80	0.0%
Foundations Backfilled	0	80	0.0%
Crane Pads Completed	0	80	0.0%
Tower Base Sections Erected	0	80	0.0%
Tower Mid Sections Erected	0	80	0.0%
Tower Top Sections Erected	0	80	0.0%
Nacelles Installed	0	80	0.0%
Rotors Installed	0	80	0.0%
Tower Wiring Complete	0	80	0.0%
Mechanically Complete	0	80	0.0%
Final Commissioned	0	80	0.0%
4/0 Cable Trenched	0	441,000	0.0%
500 Cable Trenched	0	36,000	0.0%
1000 Cable Trenched	0	333,000	0.0%
Copperclad	0	84,000	0.0%
1000 Low Voltage Trenched	0	30,500	0.0%
Fiber Optic 12 Fiber SM	0	270,000	0.0%
Transformers Set/Terminated	0	80	0.0%

(as of COB yesterday)

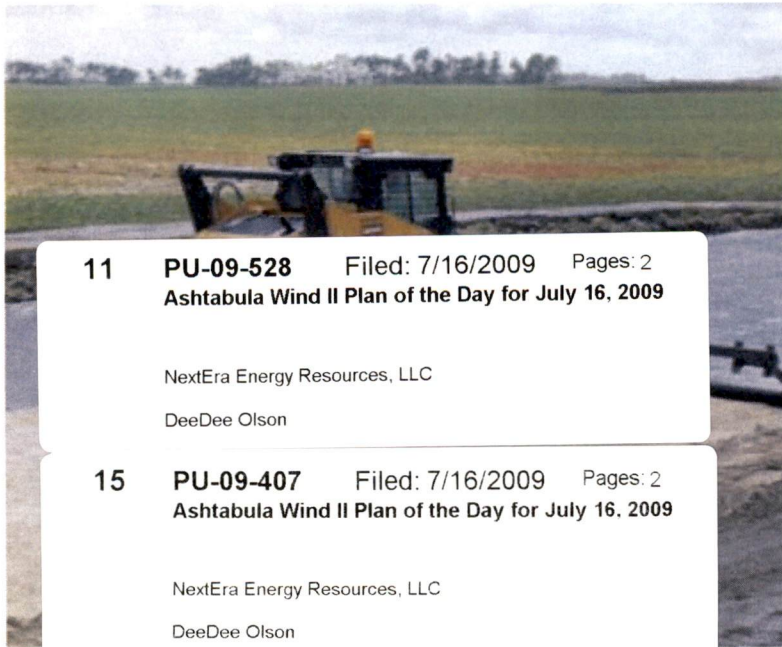

11 PU-09-528 Filed: 7/16/2009 Pages: 2
 Ashtabula Wind II Plan of the Day for July 16, 2009

NextEra Energy Resources, LLC
 DeeDee Olson

15 PU-09-407 Filed: 7/16/2009 Pages: 2
 Ashtabula Wind II Plan of the Day for July 16, 2009

NextEra Energy Resources, LLC
 DeeDee Olson



NextEra™ Energy Resources Ashtabula Wind II

Otter Tail

Plan of the Day (POD)



Date: **Thursday, 7/16/2009**
 High: **72**
 Precipitation Chances: **2%**

COD: **10-15-09**
 Low: **45**

Days to COD: **92**
 Winds: **WNW @ 11 mph**
 Weather Forecast: **Cloudy**

NextEra™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- **Wear proper PPE while on the job site**
- **Make sure not to use any equipment if it is tagged out**
- **Narrow roads; use caution when passing**
- **Keep your speed to a minimum**
- **Uneven surfaces; use caution when using equipment**
- **SWPPP inspection**

Civil/Erection:

Foundations:

- **Pour base at 150 & 152**
- **Form pedestal at 151, 153 & 154**
- **Pour pedestal at 153, 154 & 158**
- **Backfill at 141 & 159**
- **Build Crane pad at 141, 143-145**

Collections:

- **Boring at 158-163**
- **Trench & cable install 4/0 at 139-158**

Electrical:

- **Pedestal Conduit at 151 & 153**
- **Smurf tube at 150 & 195**
- **Grounding Grid at 151 & 153**
- **Install box pad at 138-142**



RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	122,723	66,277
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	0	12,750
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	0	33
Controllers	33	0	33
Bases	33	0	33
Mids	33	0	33
Tops	33	0	33
Nacelles	33	0	33
Hubs	33	0	33
Blade Sets	33	0	33

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	49,614	83.1%
Gravel Road (6")	41,232	49,614	83.1%
Roads Complete	32,975	49,614	66.5%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	24	33	72.7%
Foundations Backfilled	15	33	45.5%
Crane Pads Completed	4	33	12.1%
Tower Base Sections Erected	0	33	0.0%
Tower Mid Sections Erected	0	33	0.0%
Tower Top Sections Erected	0	33	0.0%
Nacelles Installed	0	33	0.0%
Rotors Installed	0	33	0.0%
Tower Wiring Complete	0	33	0.0%
Mechanically Complete	0	33	0.0%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	20,573	189,000	10.9%
500 Cable Trenched	0	117,000	0.0%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set/Terminated	0	33	0.0%

(as of COB yesterday)
