




NEXtera™ Energy Resources Ashtabula Wind II

NEXtera Energy

Plan of the Day (POD)



Date: Monday, 8/3/2009
High: 82
Precipitation Chances: 25%

COD: 10-31-09
Low: 49

Days to COD: 90
Winds: WSW @ 8 mph
Weather Forecast: Mostly Cloudy

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Drive cautiously
- Use correct procedure when offloading any material
- Keep your speed to a minimum
- SWPPP inspection every two weeks

Civil/Erection:

- Subgrade at 176-178
- Gravel at 229-231, 238-244
- Approach at 176

Foundations:


- Excavation at 243-244
- Mud mat at 243-244
- Install bottom rebar mat at 240-241
- Install anchor bolts at 238-240
- Install top rebar mat at 230, 231 & 238
- Form base at 230, 231 & 238
- Pour base at 229, 230 & 232
- Form pedestal at 233-235
- Pour pedestal at 209, 234 & 235
- Backfill at 182-183
- Build crane pads at 183-184

Collection:

- Boring at 8th St & 123rd

Electrical:

- Pedestal conduit at 209, 234 & 235
- Smurf tube at 229-231
- Grounding grid at 192-194
- Controller termination at 196-198

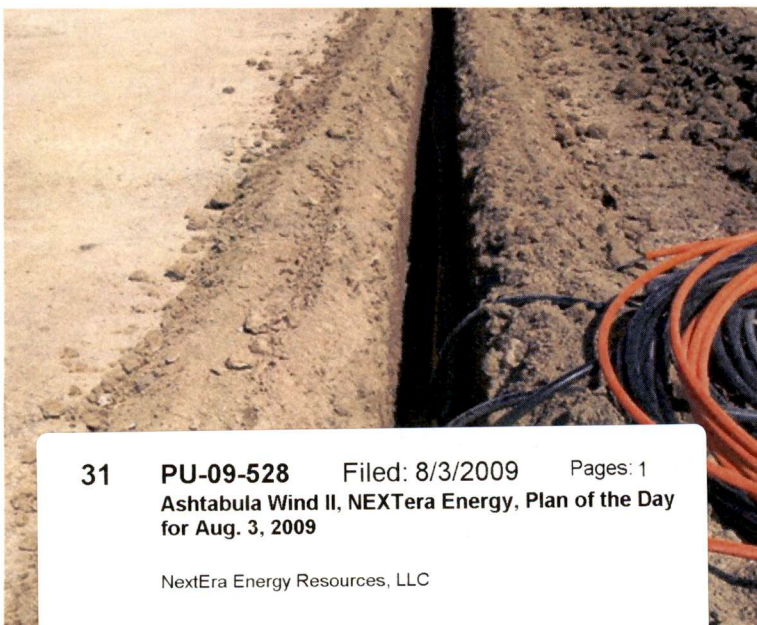

31 PU-09-528 Filed: 8/3/2009 Pages: 1
 Ashtabula Wind II, NEXtera Energy, Plan of the Day
 for Aug. 3, 2009

NextEra Energy Resources, LLC

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	381,214	59,786
500 KCM	36,000	37,036	-1,036
Copperclad	84,000	84,579	-579
1000 KCM	333,000	320,837	12,163
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	52,240	117,188	44.6%
Gravel Roads (6")	48,920	117,188	41.7%
Roads Complete	40,547	117,188	34.6%
Silt Fence Installed	13,911	17,700	78.6%
Foundations Excavated	43	80	53.8%
Foundations Poured	26	80	32.5%
Foundations Backfilled	12	80	15.0%
Crane Pads Completed	11	80	13.8%
Tower Base Sections Erected	0	80	0.0%
Tower Mid Sections Erected	0	80	0.0%
Tower Top Sections Erected	0	80	0.0%
Nacelles Installed	0	80	0.0%
Rotors Installed	0	80	0.0%
Tower Wiring Complete	0	80	0.0%
Mechanically Complete	0	80	0.0%
Final Commissioned	0	80	0.0%
4/0 Cable Trenched	14,987	441,000	3.4%
500 Cable Trenched	2834	36,000	7.9%
1000 Cable Trenched	0	333,000	0.0%
Copperclad	0	84,000	0.0%
1000 Low Voltage Trenched	0	30,500	0.0%
Fiber Optic 12 Fiber SM	0	270,000	0.0%
Transformers Set/Terminated	0	80	0.0%
(as of COB yesterday)			
