




NEXTerTM Energy Resources Ashtabula Wind II

NEXTerTM Energy

Plan of the Day (POD)



Date: Friday, 8/14/2009
High: 90
Precipitation Chances: 40%

COD: 10-31-09
Low: 63

Days to COD: 79
Winds: NW @ 8 mph
Weather Forecast: Mostly Cloudy

NEXTerTM Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Keep hydrated
- Keep your speed to a minimum
- Watch out for blind corners in areas where corn is growing
- SWPPP inspection every two weeks

Civil/Erection:

- Subgrade at 205-207
- Gravel at 187-190, 201-203 & 206-207

Foundations:

- Excavation at 201 & 207
- Mud mat at 201 & 207
- Install bottom rebar mat at 188-190
- Install anchor bolts at 188-190
- Install top rebar mat at 169, 187 & 188
- Form base at 169, 187 & 188
- Pour base at 170-171
- Form pedestal at 172-174
- Pour pedestal at 173-175
- Backfill at 238-239
- Build crane pads at 238-239

Erection:


- Erect base & mid at 178-179
- Assemble rotor at 178-180
- Erect top, nacelle & rotor at 183

Collection:

- Trench & cable install – 4/0 at JB 189, 169-171
- Trench & cable install-500 at 175-JB553

Electrical:

- Pedestal conduit at 229-231
- Smurf tube at 169, 187 & 188
- Grounding grid at 176-177
- Controller termination at 191 & 214
- Box pad installation at 228, 234 & 237
- Tower wiring at 200-201
- Tower wiring pre-walk at 199-200
- IIP at 197
- Mechanical completion at 198-199

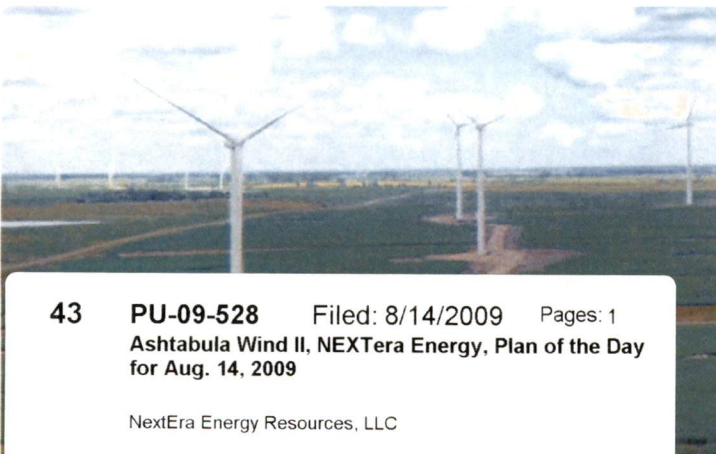

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	453,555	-12,555
500 KCM	36,000	37,036	-1,036
Copperclad	84,000	84,579	-579
1000 KCM	333,000	334,956	-1,956
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	68,864	117,188	58.8%
Gravel Roads (6")	65,134	117,188	55.6%
Roads Complete	60,930	117,188	52.0%
Silt Fence Installed	19,695	17,700	111.3%
Foundations Excavated	61	80	76.3%
Foundations Poured	47	80	58.8%
Foundations Backfilled	34	80	42.5%
Crane Pads Completed	31	80	38.8%
Tower Base Sections Erected	16	80	20.0%
Tower Mid Sections Erected	16	80	20.0%
Tower Top Sections Erected	11	80	13.8%
Nacelles Installed	11	80	13.8%
Rotors Installed	11	80	13.8%
Tower Wiring Complete	5	80	6.3%
Mechanically Complete	1	80	1.3%
Final Commissioned	0	80	0.0%
4/0 Cable Trenched	86,892	441,000	19.7%
500 Cable Trenched	17,194	36,000	47.8%
1000 Cable Trenched	110,340	333,000	33.1%
Copperclad	0	84,000	0.0%
1000 Low Voltage installed	7875	30,500	25.8%
Fiber Optic 12 Fiber SM	71,475	270,000	26.5%
Transformers Set/Terminated	27	80	33.8%
(as of COB yesterday)			

43 PU-09-528 Filed: 8/14/2009 Pages: 1
 Ashtabula Wind II, NEXTerTM Energy, Plan of the Day
 for Aug. 14, 2009

NextEra Energy Resources, LLC
